



GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (°F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-01	08/16/16	0.7	27.0	14.7	57.6	139.8	-6.6	Y	
GIW-01	08/16/16	0.9	33.8	12.1	53.2	140.4	-1.9	Y	
GIW-01	08/22/16	1.4	43.3	7.6	47.7	152.1	-0.9	Y	
GIW-01	08/22/16	1.4	44.4	7.6	46.6	151.3	-0.7	Y	
GIW-01	09/06/16	4.5	60.0	0.9	34.6	183.3	-4.1	Y	
GIW-01	09/06/16	5.0	63.0	0.8	31.2	182.9	-4.4	Y	
GIW-01	09/15/16	3.2	61.7	2.2	32.9	183.5	-3.9	Y	
GIW-01	09/15/16	3.3	61.8	1.8	33.1	183.6	-3.7	Y	
GIW-01	09/20/16	3.5	58.3	1.2	37.0	183.9	-3.5	Y	
GIW-01	09/20/16	2.6	64.6	0.4	32.4	184.6	-0.4	Y	
GIW-01	09/21/16	2.8	61.9	0.3	35.0	185.7	0.4	Y	
GIW-01	09/21/16	2.8	65.6	0.3	31.3	185.7	-0.9	Y	
GIW-01	09/27/16	3.6	60.1	0.3	36.0	185.1	-0.6	Y	
GIW-01	09/27/16	3.9	65.9	0.3	29.9	185.1	-0.6	Y	
GIW-01	10/04/16	3.4	60.9	0.1	35.6	185.7	-0.1	Y	
GIW-01	10/04/16	2.4	64.5	0.1	33.0	185.7	-0.2	Y	
GIW-01	10/13/16	4.4	29.9	0.7	65.0	180.9	-5.3	Y	
GIW-01	10/13/16	5.5	61.9	0.0	32.6	180.9	-5.4	Y	
GIW-01	10/17/16	2.2	58.9	0.0	38.9	183.7	-3.0	Y	
GIW-01	10/17/16	2.6	64.3	0.0	33.1	183.6	-3.0	Y	
GIW-01	10/25/16	4.8	60.7	0.0	34.5	183.9	-1.9	Y	
GIW-01	10/25/16	3.5	66.6	0.0	29.9	183.6	-2.0	Y	
GIW-01	11/04/16	4.4	63.2	0.4	32.0	183.7	-2.4	Y	
GIW-01	11/04/16	4.0	70.0	0.4	25.6	183.5	-2.4	Y	
GIW-01	11/09/16	3.4	61.8	0.1	34.7	184.3	-2.0	Y	
GIW-01	11/09/16	3.4	62.9	0.0	33.7	184.3	-1.7	Y	
GIW-01	11/15/16	3.7	58.2	0.0	38.1	183.9	-1.3	Y	
GIW-01	11/15/16	3.3	64.5	0.0	32.2	183.9	-1.2	Y	
GIW-01	11/22/16	4.1	62.9	0.0	33.0	179.2	-3.9	Y	
GIW-01	11/22/16	5.1	65.2	0.0	29.7	179.2	-4.1	Y	
GIW-01	11/29/16	3.6	58.0	0.1	38.3	177.0	-0.7	Y	
GIW-01	11/29/16	3.1	64.8	0.0	32.1	178.0	-0.6	Y	
GIW-01	12/08/16	5.1	62.3	0.4	32.2	151.3	-6.3	Y	
GIW-01	12/08/16	5.2	60.8	0.6	33.4	147.7	-6.4	Y	
GIW-01	12/14/16	13.5	54.3	1.4	30.8	157.8	-11.8	Y	
GIW-01	12/14/16	12.2	57.2	1.0	29.6	158.0	-12.3	Y	

GIW-1 Wellhead Temperatures

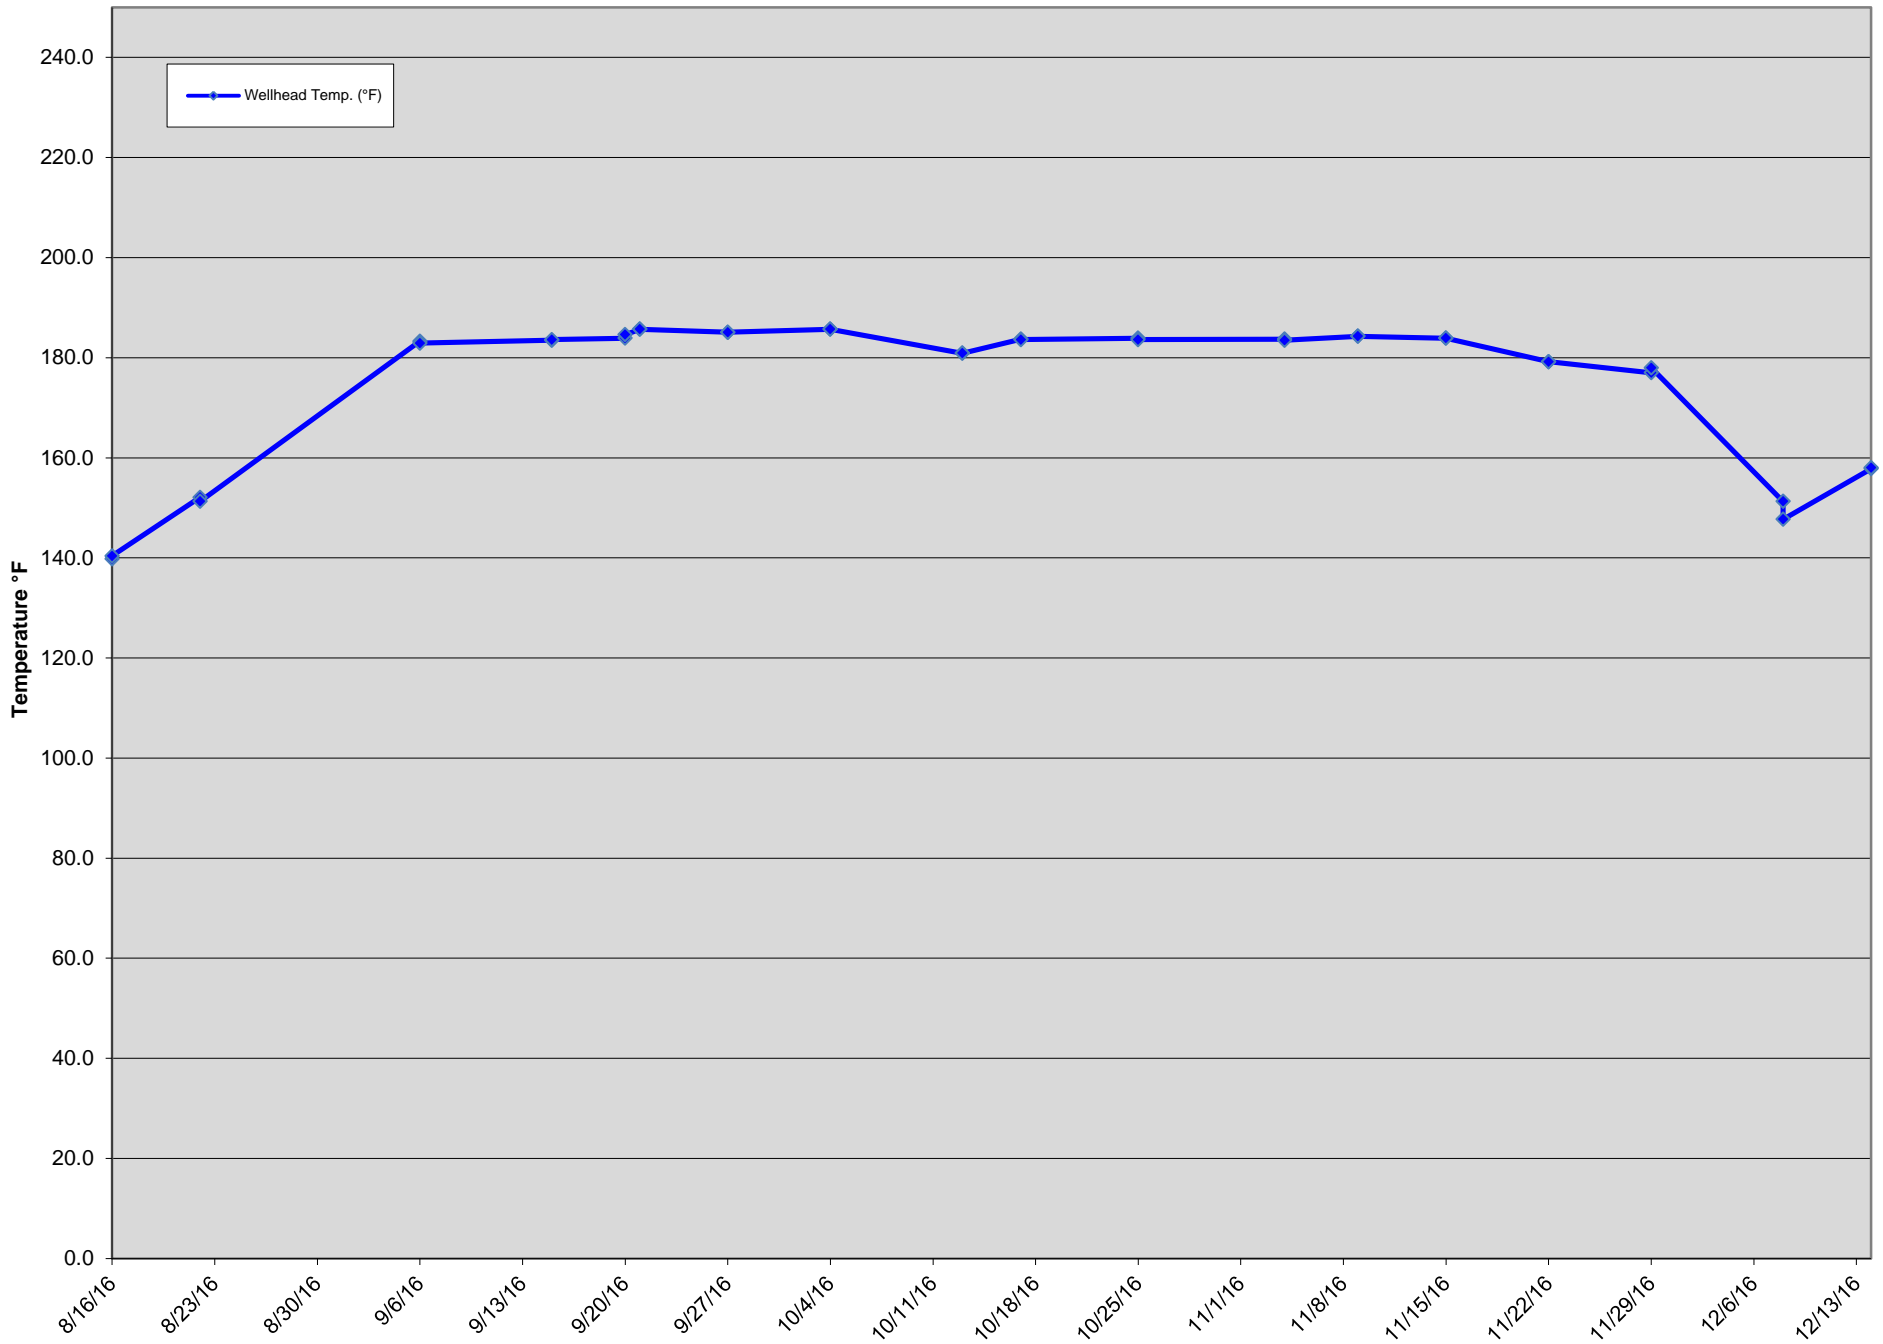


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-02	08/16/16	5.3	35.2	11.4	48.1	78.3	-0.5	N/A	(HES Installed)
GIW-02	08/16/16	5.4	34.2	11.5	48.9	78.5	-0.5	N/A	(HES Installed)
GIW-02	08/22/16	6.4	36.1	10.4	47.1	89.6	-0.4	N/A	(HES Installed)
GIW-02	08/22/16	6.7	33.8	10.6	48.9	90.3	-0.4	N/A	(HES Installed)
GIW-02	08/29/16	6.8	36.5	10.3	46.4	100.6	-0.4	N/A	(HES Installed)
GIW-02	08/29/16	7.2	34.6	10.4	47.8	100.6	-0.4	N/A	(HES Installed)
GIW-02	09/06/16	5.1	30.8	11.5	52.6	104.5	-0.5	N/A	(HES Installed)
GIW-02	09/06/16	5.3	29.2	11.5	54.0	104.3	-0.5	N/A	(HES Installed)
GIW-02	09/15/16	3.3	21.9	14.6	60.2	88.2	-0.4	N/A	(HES Installed)
GIW-02	09/15/16	3.3	21.5	14.6	60.6	88.6	-0.4	N/A	(HES Installed)
GIW-02	09/20/16	1.5	19.5	15.0	64.0	106.2	-0.4	N/A	(HES Installed)
GIW-02	09/20/16	1.5	18.2	15.2	65.1	107.2	-0.4	N/A	(HES Installed)
GIW-02	09/21/16	3.2	29.5	12.2	55.1	93.4	-0.3	N/A	(HES Installed)
GIW-02	09/21/16	3.2	27.7	12.2	56.9	94.1	-0.3	N/A	(HES Installed)
GIW-02	09/27/16	5.3	36.5	10.2	48.0	87.0	-0.3	N/A	(HES Installed)
GIW-02	09/27/16	5.9	33.0	10.3	50.8	87.1	-0.3	N/A	(HES Installed)
GIW-02	10/04/16	4.6	37.1	9.7	48.6	90.6	-0.2	N/A	(HES Installed)
GIW-02	10/04/16	4.9	34.3	9.9	50.9	89.6	-0.2	N/A	(HES Installed)
GIW-02	10/13/16	4.2	50.9	13.2	31.7	61.3	-0.2	N/A	(HES Installed)
GIW-02	10/13/16	3.0	29.4	15.6	52.0	61.8	-0.3	N/A	(HES Installed)
GIW-02	10/17/16	2.8	45.4	12.2	39.6	85.9	-0.3	N/A	(HES Installed)
GIW-02	10/17/16	3.7	33.4	12.8	50.1	87.0	-0.2	N/A	(HES Installed)
GIW-02	10/25/16	3.0	25.9	13.9	57.2	64.9	-0.2	N/A	(HES Installed)
GIW-02	10/25/16	3.0	24.9	14.0	58.1	64.8	-0.2	N/A	(HES Installed)
GIW-02	11/04/16	0.3	15.7	18.8	65.2	74.8	-0.2	N/A	(HES Installed)
GIW-02	11/04/16	0.3	10.0	18.5	71.2	75.0	-0.1	N/A	(HES Installed)
GIW-02	11/09/16	2.8	63.2	0.1	33.9	65.2	-0.1	N/A	(HES Installed)
GIW-02	11/09/16	3.1	61.1	0.2	35.6	64.0	-0.1	N/A	(HES Installed)
GIW-02	11/15/16	2.9	65.2	0.0	31.9	71.6	-0.2	N/A	(HES Installed)
GIW-02	11/22/16	3.9	65.7	0.0	30.4	52.5	-0.1	N/A	(HES Installed)
GIW-02	11/29/16	4.1	66.3	0.0	29.6	68.4	-0.1	N/A	(HES Installed)
GIW-02	12/08/16	3.7	67.1	0.0	29.2	28.2	-0.1	N/A	(HES Installed)
GIW-02	12/08/16	3.8	67.3	0.0	28.9	28.6	-0.1	N/A	(HES Installed)
GIW-02	12/14/16	5.4	62.3	0.1	32.2	30.9	0.0	N/A	(HES Installed)

GIW-2 Wellhead Temperatures

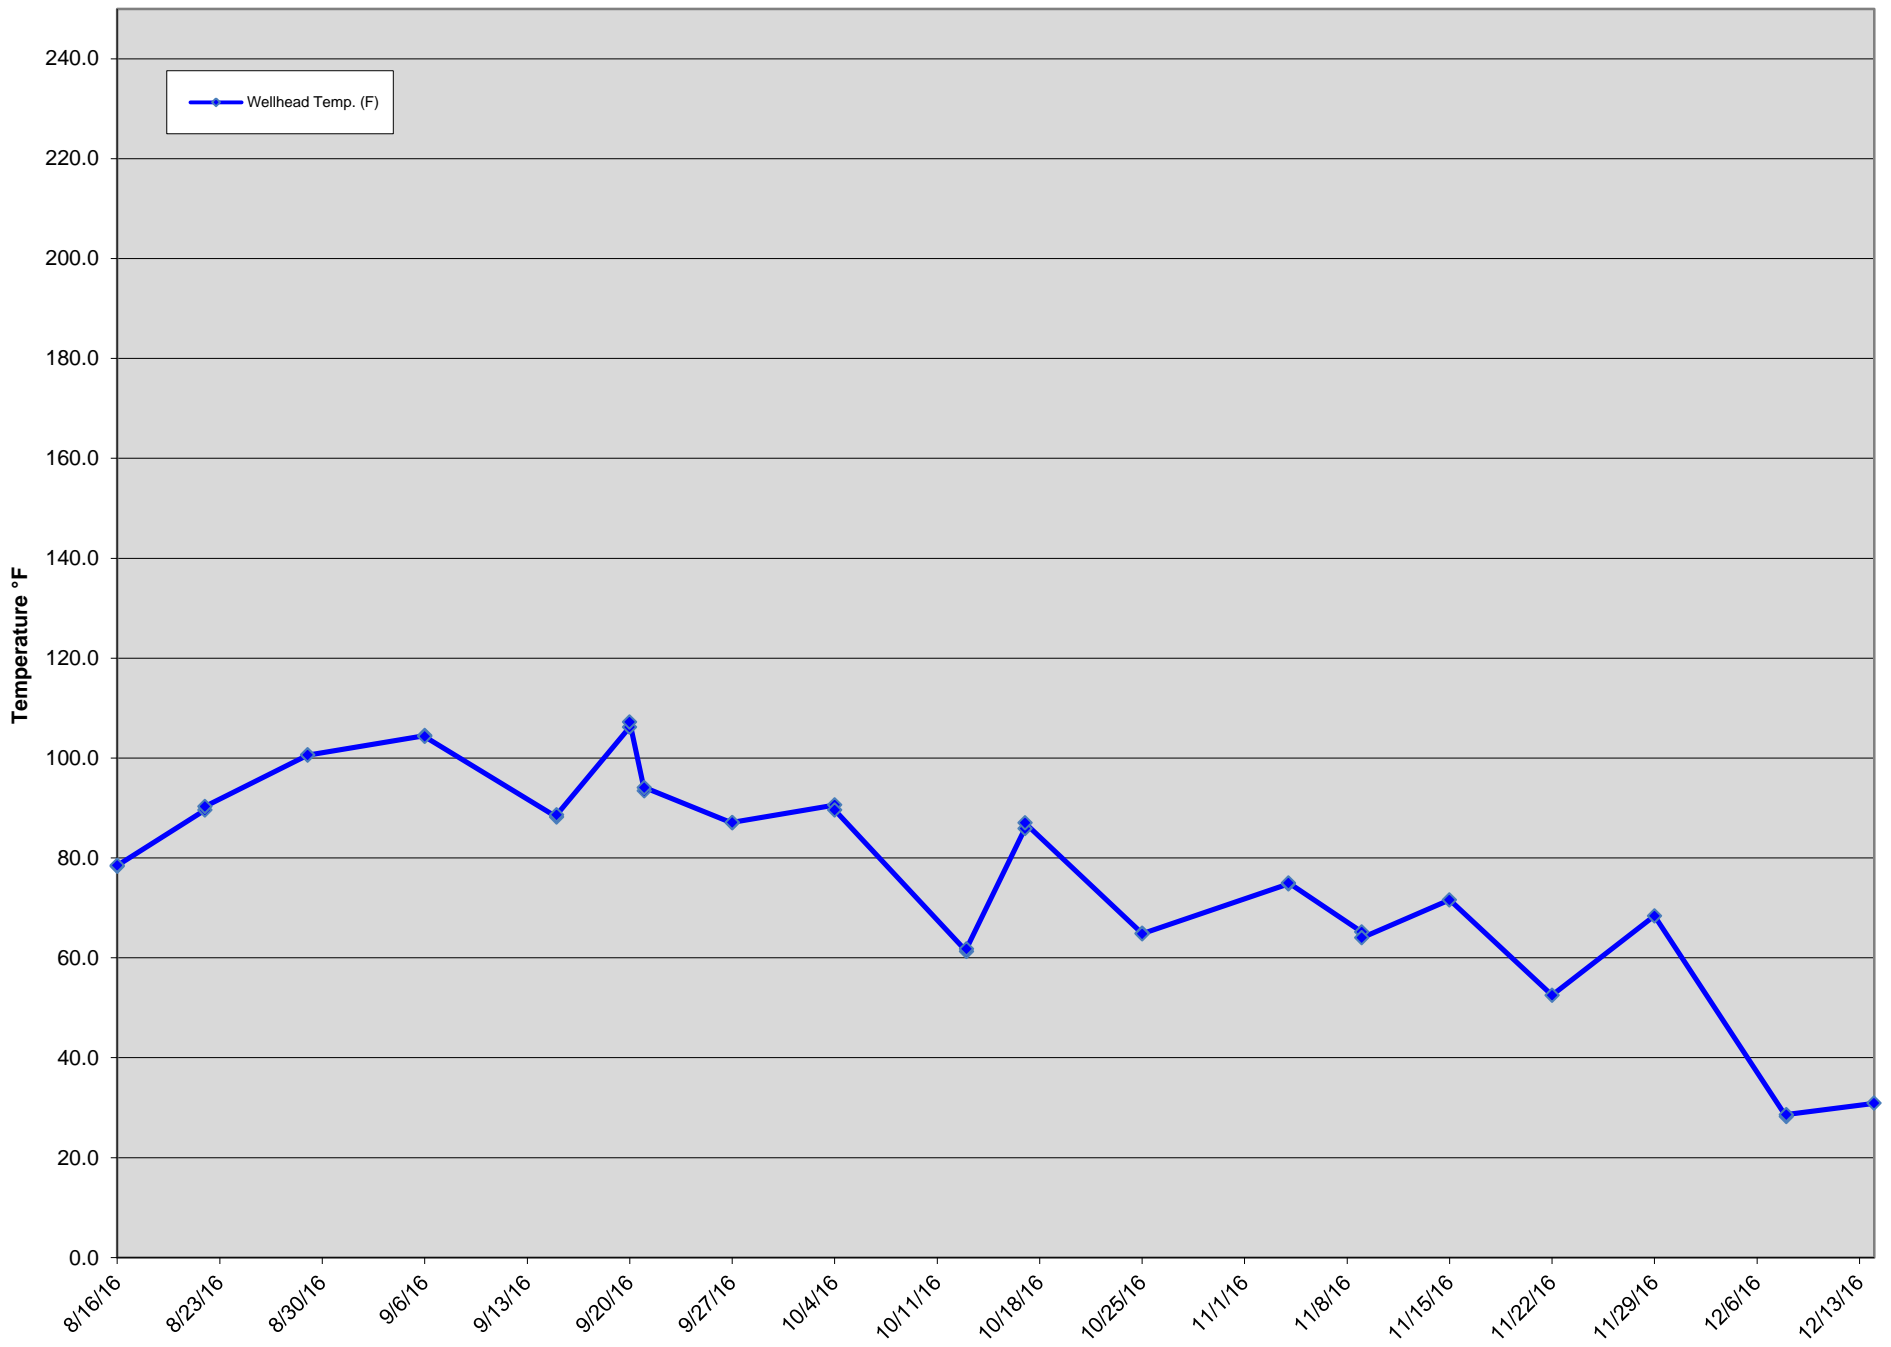


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-03	08/16/16	0.7	66.9	0.1	32.3	77.8	0.4	N/A	(HES Installed)
GIW-03	08/16/16	0.7	68.9	0.2	30.2	78.0	-0.8	N/A	(HES Installed)
GIW-03	08/22/16	1.0	53.3	4.2	41.5	83.0	-2.4	N/A	(HES Installed)
GIW-03	08/22/16	0.9	57.7	2.7	38.7	83.0	-0.7	N/A	(HES Installed)
GIW-03	08/29/16	0.7	70.4	0.5	28.4	97.3	1.1	N/A	(HES Installed)
GIW-03	08/29/16	0.7	69.9	0.8	28.6	97.9	-0.6	N/A	(HES Installed)
GIW-03	09/06/16	1.8	51.2	5.4	41.6	108.0	-10.7	N/A	(HES Installed)
GIW-03	09/06/16	2.1	49.8	5.2	42.9	108.0	-10.4	N/A	(HES Installed)
GIW-03	09/15/16	2.0	49.8	5.7	42.5	99.4	-15.8	N/A	(HES Installed)
GIW-03	09/15/16	2.1	50.8	6.5	40.6	105.2	-15.6	N/A	(HES Installed)
GIW-03	09/20/16	2.3	47.2	5.1	45.4	110.0	-8.4	N/A	(HES Installed)
GIW-03	09/20/16	2.1	45.8	6.0	46.1	110.2	-3.7	N/A	(HES Installed)
GIW-03	09/21/16	1.3	54.6	4.3	39.8	87.0	-2.8	N/A	(HES Installed)
GIW-03	09/21/16	1.4	54.9	3.3	40.4	87.6	-0.6	N/A	(HES Installed)
GIW-03	09/27/16	1.5	58.0	1.9	38.6	91.8	-0.5	N/A	(HES Installed)
GIW-03	10/04/16	0.9	64.3	0.1	34.7	88.9	-0.2	N/A	(HES Installed)
GIW-03	10/04/16	0.7	55.4	2.2	41.7	93.3	-0.6	N/A	(HES Installed)
GIW-03	10/13/16	1.2	50.3	4.9	43.6	59.7	-2.7	N/A	(HES Installed)
GIW-03	10/17/16	2.2	46.3	3.8	47.7	84.0	-1.6	N/A	(HES Installed)
GIW-03	10/25/16	1.0	48.6	5.3	45.1	65.5	-2.7	N/A	(HES Installed)
GIW-03	10/25/16	1.1	50.0	5.2	43.7	66.3	-2.1	N/A	(HES Installed)
GIW-03	11/04/16	0.5	46.2	7.2	46.1	81.4	-2.3	N/A	(HES Installed)
GIW-03	11/04/16	0.7	50.3	5.9	43.1	82.2	-1.0	N/A	(HES Installed)
GIW-03	11/09/16	0.7	63.4	0.1	35.8	70.9	0.1	N/A	(HES Installed)
GIW-03	11/09/16	0.7	60.2	0.3	38.8	71.1	0.0	N/A	(HES Installed)
GIW-03	11/15/16	1.4	57.7	3.1	37.8	74.3	-0.6	N/A	(HES Installed)
GIW-03	11/22/16	1.6	59.6	3.3	35.5	51.5	-0.6	N/A	(HES Installed)
GIW-03	11/29/16	0.9	64.5	0.3	34.3	70.9	-0.1	N/A	(HES Installed)
GIW-03	12/08/16	1.4	52.8	3.3	42.5	36.0	-0.7	N/A	(HES Installed)
GIW-03	12/08/16	1.2	55.8	3.6	39.4	36.3	-0.6	N/A	(HES Installed)
GIW-03	12/14/16	1.2	66.0	0.0	32.8	29.6	-2.0	N/A	(HES Installed)

GIW-3 Wellhead Temperatures

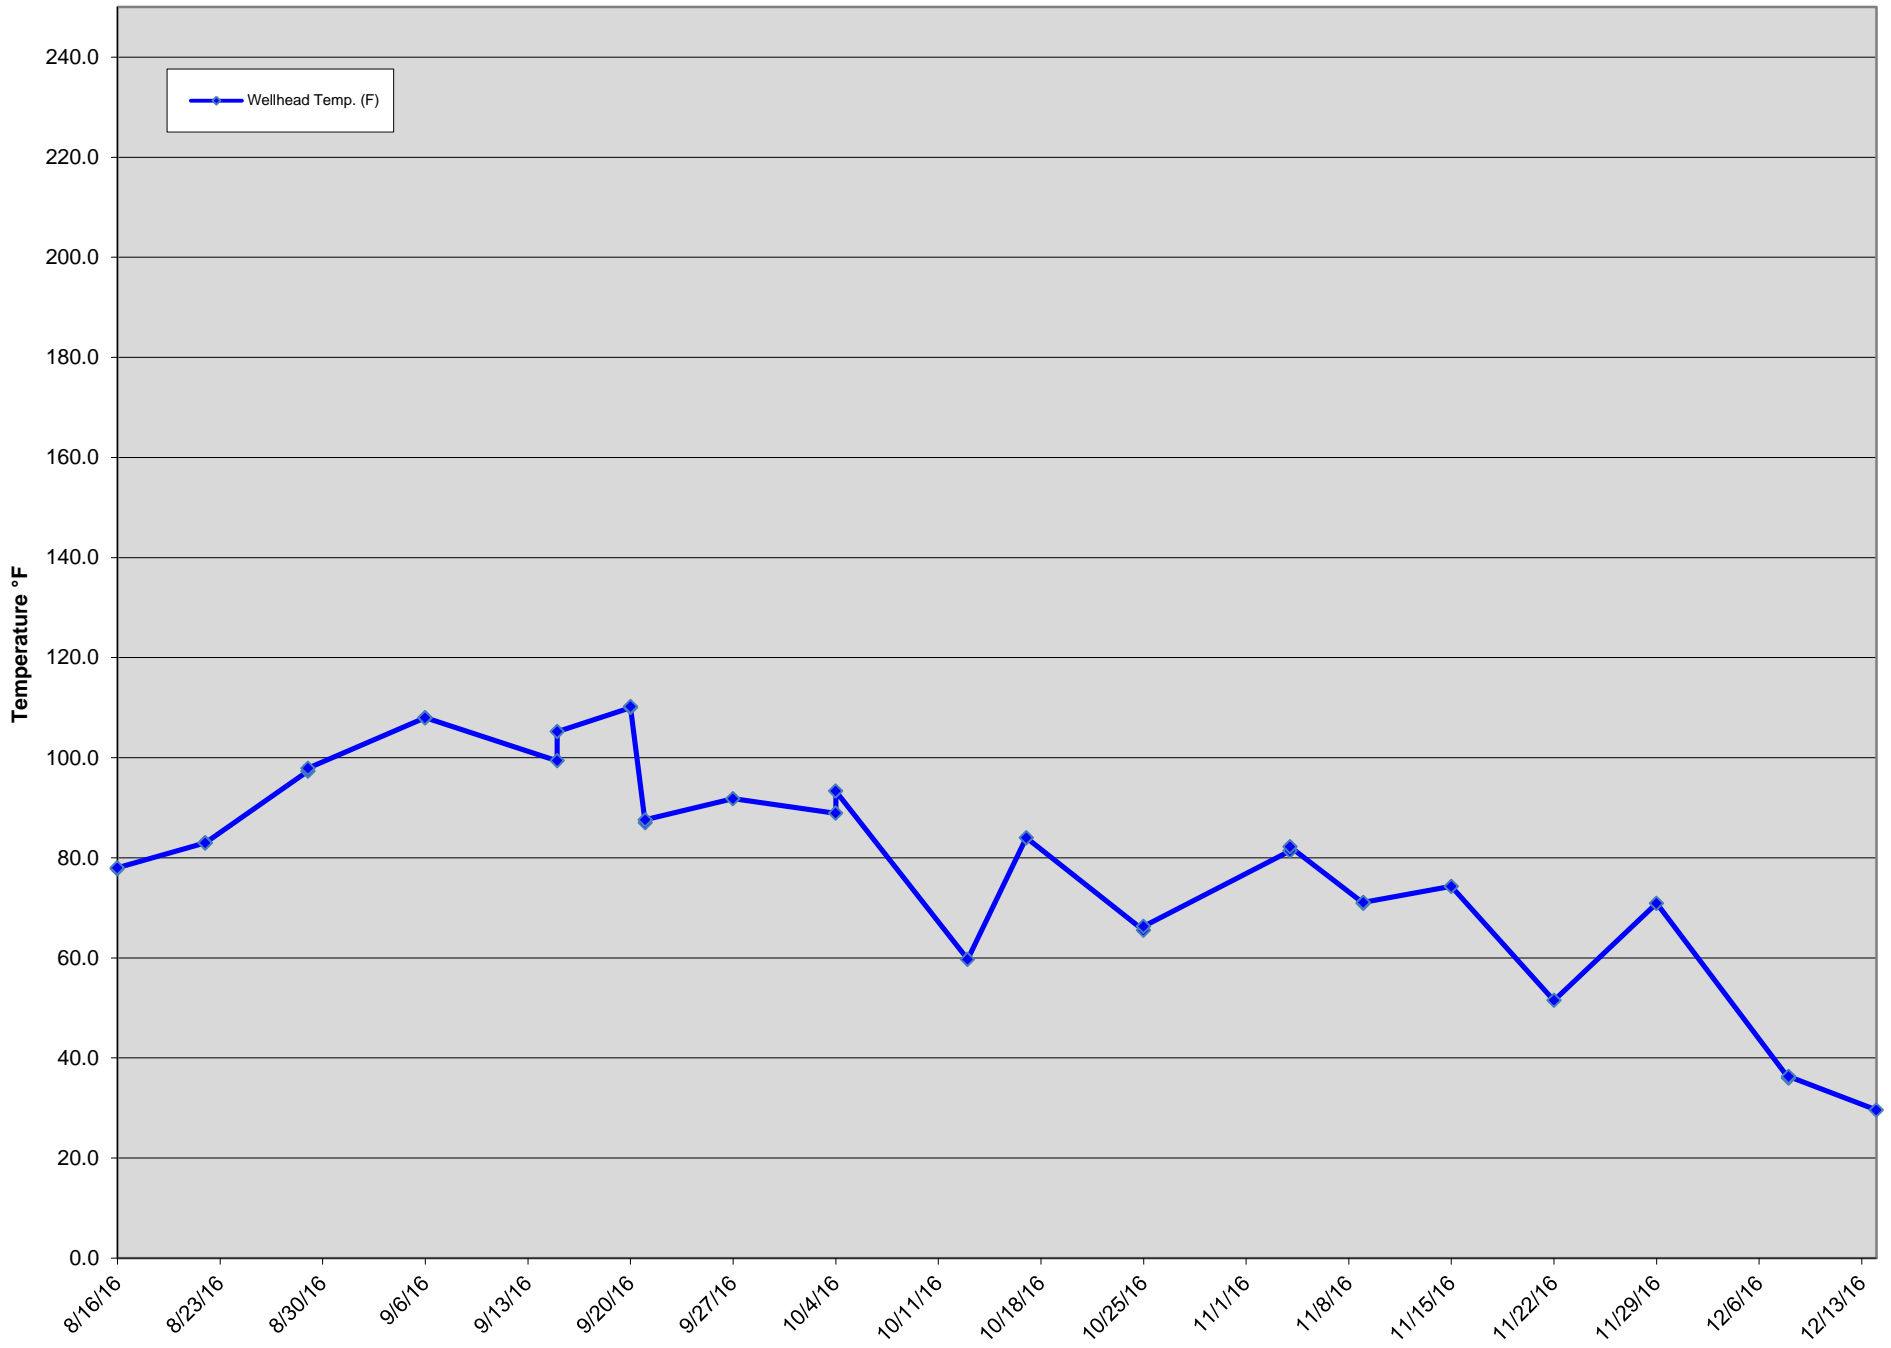


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-04	08/16/16	0.9	60.9	0.1	38.1	77.4	-10.3	N/A	(HES Installed)
GIW-04	08/22/16	0.9	57.1	0.5	41.5	91.7	-8.3	N/A	(HES Installed)
GIW-04	08/29/16	1.2	61.2	0.5	37.1	101.9	-8.2	N/A	(HES Installed)
GIW-04	09/06/16	0.9	54.6	1.4	43.1	105.8	-8.7	N/A	(HES Installed)
GIW-04	09/06/16	1.4	55.7	1.4	41.5	106.5	-9.1	N/A	(HES Installed)
GIW-04	09/15/16	1.3	58.6	0.8	39.3	88.6	-13.4	N/A	(HES Installed)
GIW-04	09/20/16	1.7	54.2	0.5	43.6	107.0	-6.4	N/A	(HES Installed)
GIW-04	09/20/16	1.3	58.3	0.5	39.9	107.5	-4.0	N/A	(HES Installed)
GIW-04	09/21/16	1.9	58.2	0.5	39.4	91.4	-3.4	N/A	(HES Installed)
GIW-04	09/27/16	1.5	56.5	0.6	41.4	87.3	-8.1	N/A	(HES Installed)
GIW-04	10/04/16	1.5	55.1	0.2	43.2	90.5	-4.0	N/A	(HES Installed)
GIW-04	10/04/16	1.5	53.8	0.2	44.5	90.3	-3.8	N/A	(HES Installed)
GIW-04	10/13/16	1.7	50.2	0.1	48.0	61.4	-5.1	N/A	(HES Installed)
GIW-04	10/17/16	1.0	56.0	0.1	42.9	86.1	-3.8	N/A	(HES Installed)
GIW-04	10/25/16	0.7	54.1	0.3	44.9	68.4	-5.0	N/A	(HES Installed)
GIW-04	11/04/16	0.9	51.0	1.1	47.0	80.3	-5.1	N/A	(HES Installed)
GIW-04	11/09/16	1.2	53.8	1.7	43.3	77.1	-6.1	N/A	(HES Installed)
GIW-04	11/09/16	1.2	50.6	2.0	46.2	77.5	-6.5	N/A	(HES Installed)
GIW-04	11/15/16	2.1	54.7	1.8	41.4	76.5	-4.9	N/A	(HES Installed)
GIW-04	11/22/16	1.9	56.6	1.4	40.1	51.5	-6.1	N/A	(HES Installed)
GIW-04	11/29/16	1.4	56.8	1.5	40.3	69.3	-5.5	N/A	(HES Installed)
GIW-04	12/08/16	1.1	54.1	0.4	44.4	33.8	-7.0	N/A	(HES Installed)
GIW-04	12/08/16	1.0	52.3	0.7	46.0	36.4	-7.0	N/A	(HES Installed)
GIW-04	12/14/16	0.8	52.7	1.8	44.7	29.5	-7.1	N/A	(HES Installed)

GIW-4 Wellhead Temperatures

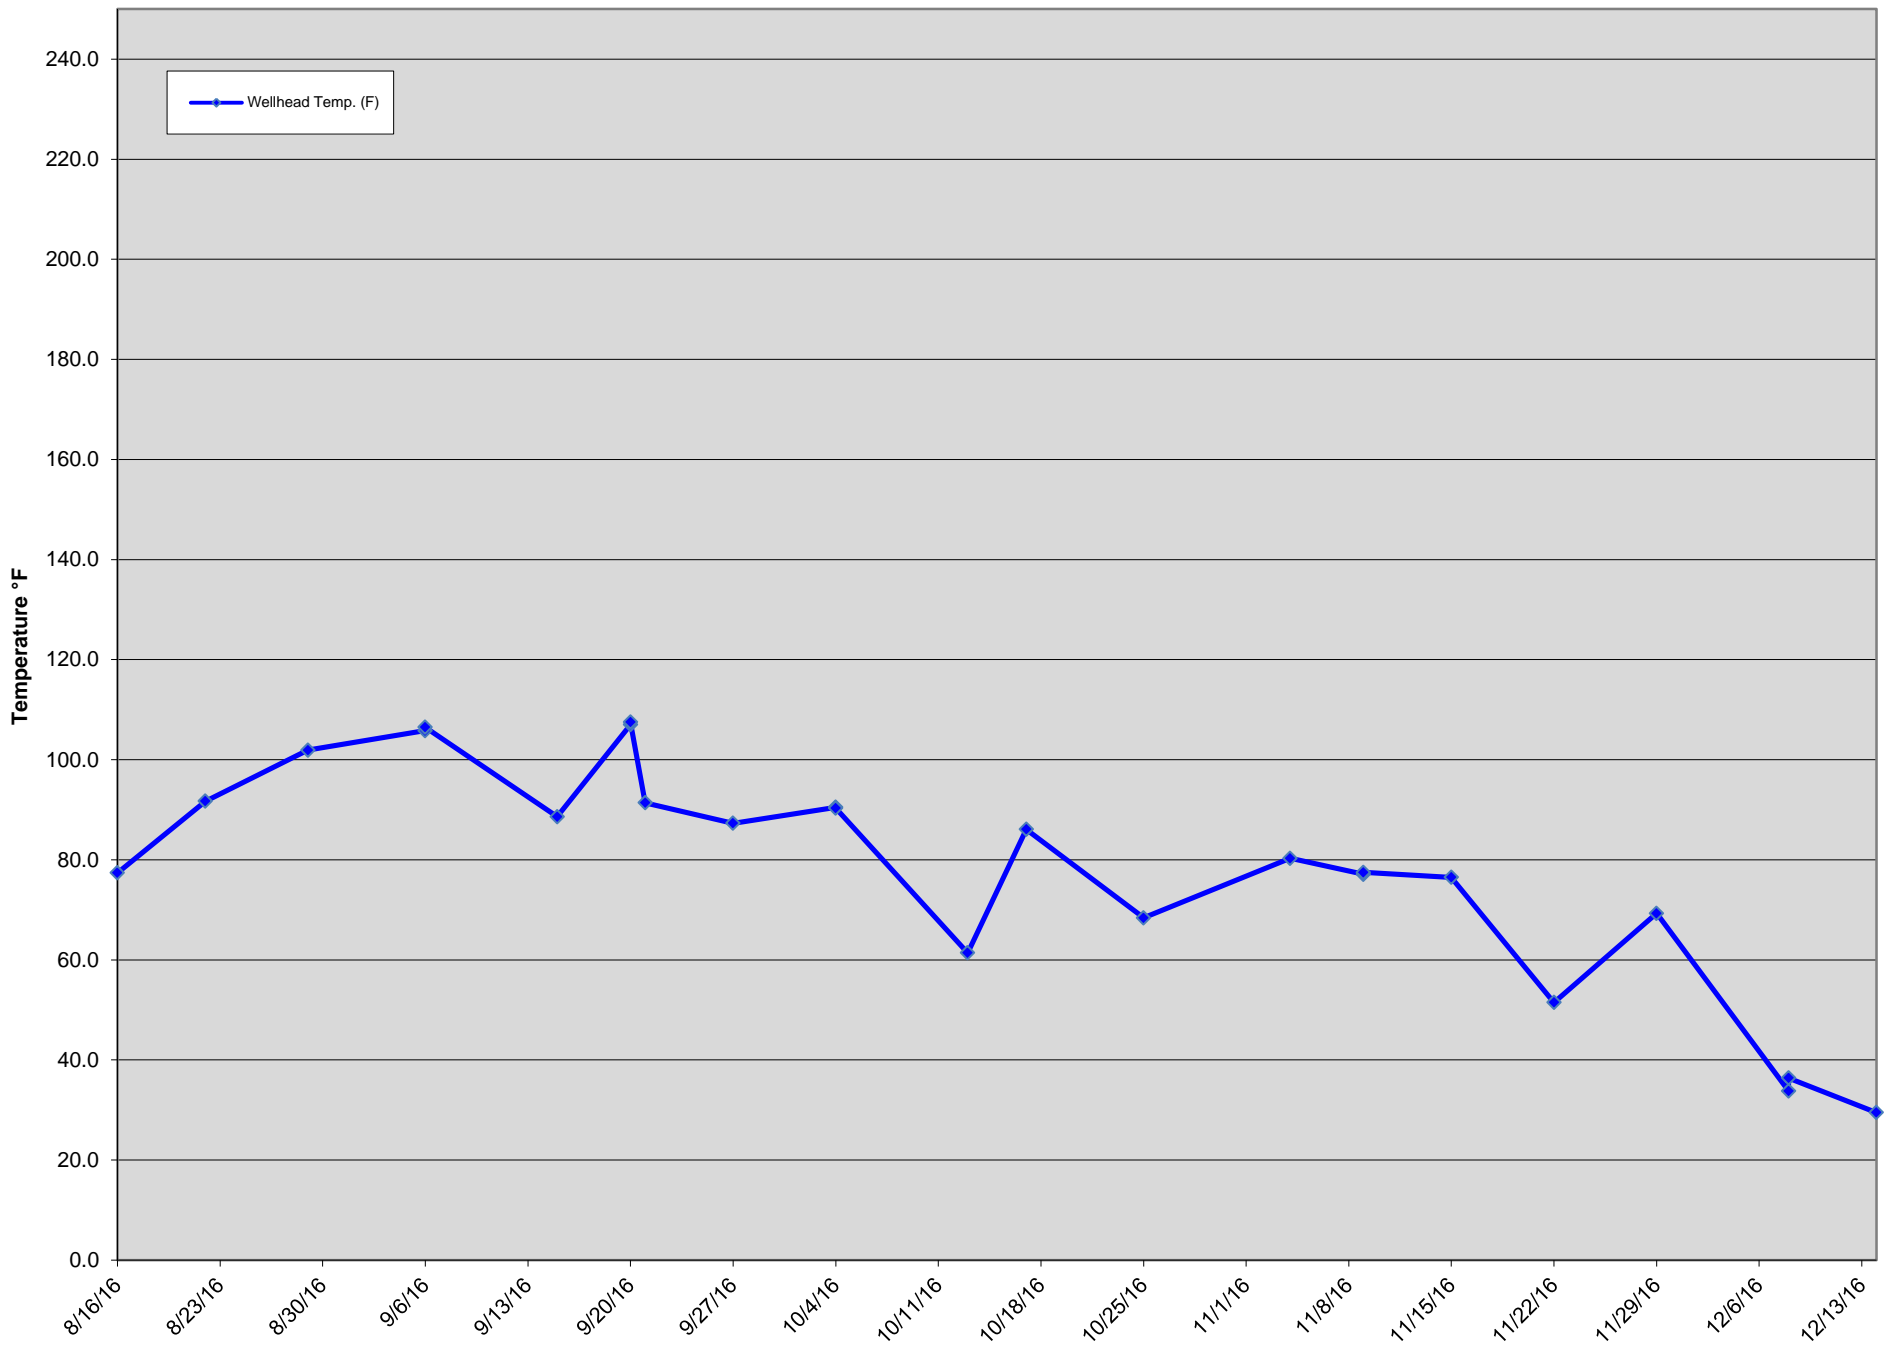


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-05	08/16/16	3.5	58.4	1.0	37.1	77.7	-5.9	N/A	(HES Installed)
GIW-05	08/22/16	2.2	56.2	1.1	40.5	89.2	-4.4	N/A	(HES Installed)
GIW-05	08/22/16	2.0	56.4	1.1	40.5	90.0	-2.8	N/A	(HES Installed)
GIW-05	08/29/16	2.0	56.8	1.8	39.4	97.3	-2.5	N/A	(HES Installed)
GIW-05	09/06/16	2.7	56.7	1.6	39.0	100.9	-1.7	N/A	(HES Installed)
GIW-05	09/06/16	3.3	59.1	1.6	36.0	101.3	-1.7	N/A	(HES Installed)
GIW-05	09/12/16	2.3	61.2	0.3	36.2	88.0	-0.1	N/A	(HES Installed)
GIW-05	09/12/16	1.8	64.2	0.3	33.7	88.9	-0.2	N/A	(HES Installed)
GIW-05	09/15/16	2.3	61.8	0.2	35.7	83.2	1.8	N/A	(HES Installed)
GIW-05	09/15/16	2.3	62.5	0.2	35.0	82.4	-15.0	N/A	(HES Installed)
GIW-05	09/20/16	1.9	48.8	4.6	44.7	102.1	-8.0	N/A	(HES Installed)
GIW-05	09/20/16	1.2	41.1	7.5	50.2	102.5	-3.5	N/A	(HES Installed)
GIW-05	09/21/16	2.5	55.1	0.2	42.2	87.5	-1.6	N/A	(HES Installed)
GIW-05	09/27/16	2.1	52.4	1.7	43.8	84.0	-17.4	N/A	(HES Installed)
GIW-05	09/27/16	2.0	57.0	1.4	39.6	84.0	-16.7	N/A	(HES Installed)
GIW-05	10/04/16	0.1	1.4	21.0	77.5	79.6	-7.6	N/A	(HES Installed)
GIW-05	10/04/16	0.1	1.0	20.8	78.1	80.5	-9.0	N/A	(HES Installed)
GIW-05	10/04/16	0.0	0.0	20.8	79.2	86.8	-5.8	N/A	(HES Installed)
GIW-05	10/04/16	0.0	0.0	20.8	79.2	87.7	-6.3	N/A	(HES Installed)
GIW-05	10/13/16	1.3	37.1	18.1	43.5	57.8	-4.8	N/A	(HES Installed)
GIW-05	10/13/16	0.0	10.2	22.3	67.5	59.0	-6.9	N/A	(HES Installed)
GIW-05	10/17/16	0.2	29.1	18.1	52.6	83.8	-3.8	N/A	(HES Installed)
GIW-05	10/17/16	0.0	8.4	19.6	72.0	84.7	-5.8	N/A	(HES Installed)
GIW-05	10/25/16	0.3	6.8	19.9	73.0	61.8	-2.1	N/A	(HES Installed)
GIW-05	10/25/16	0.1	2.2	20.9	76.8	62.3	-2.4	N/A	(HES Installed)
GIW-05	11/04/16	0.3	17.0	19.9	62.8	75.0	-1.3	N/A	(HES Installed)
GIW-05	11/04/16	0.0	1.0	21.7	77.3	76.4	-2.0	N/A	(HES Installed)
GIW-05	11/09/16	0.0	2.2	21.8	76.0	67.9	-2.3	N/A	(HES Installed)
GIW-05	11/09/16	0.0	0.3	22.4	77.3	71.0	-2.4	N/A	(HES Installed)
GIW-05	11/15/16	0.1	8.7	20.1	71.1	68.5	-1.2	N/A	(HES Installed)
GIW-05	11/15/16	0.0	2.7	21.4	75.9	68.9	-1.3	N/A	(HES Installed)
GIW-05	11/22/16	0.2	20.8	19.3	59.7	52.2	-0.9	N/A	(HES Installed)
GIW-05	11/22/16	0.0	5.8	21.9	72.3	51.8	-1.1	N/A	(HES Installed)
GIW-05	11/29/16	0.1	15.3	19.7	64.9	67.9	-0.6	N/A	(HES Installed)
GIW-05	11/29/16	0.0	4.0	21.7	74.3	67.9	-0.6	N/A	(HES Installed)
GIW-05	12/08/16	0.0	6.4	21.0	72.6	33.1	-2.2	N/A	(HES Installed)
GIW-05	12/08/16	0.0	1.2	22.5	76.3	33.4	-0.5	N/A	(HES Installed)
GIW-05	12/14/16	0.0	14.4	19.4	66.2	30.9	-0.5	N/A	(HES Installed)
GIW-05	12/14/16	0.0	4.5	21.4	74.1	30.5	-0.3	N/A	(HES Installed)

GIW-5 Wellhead Temperatures

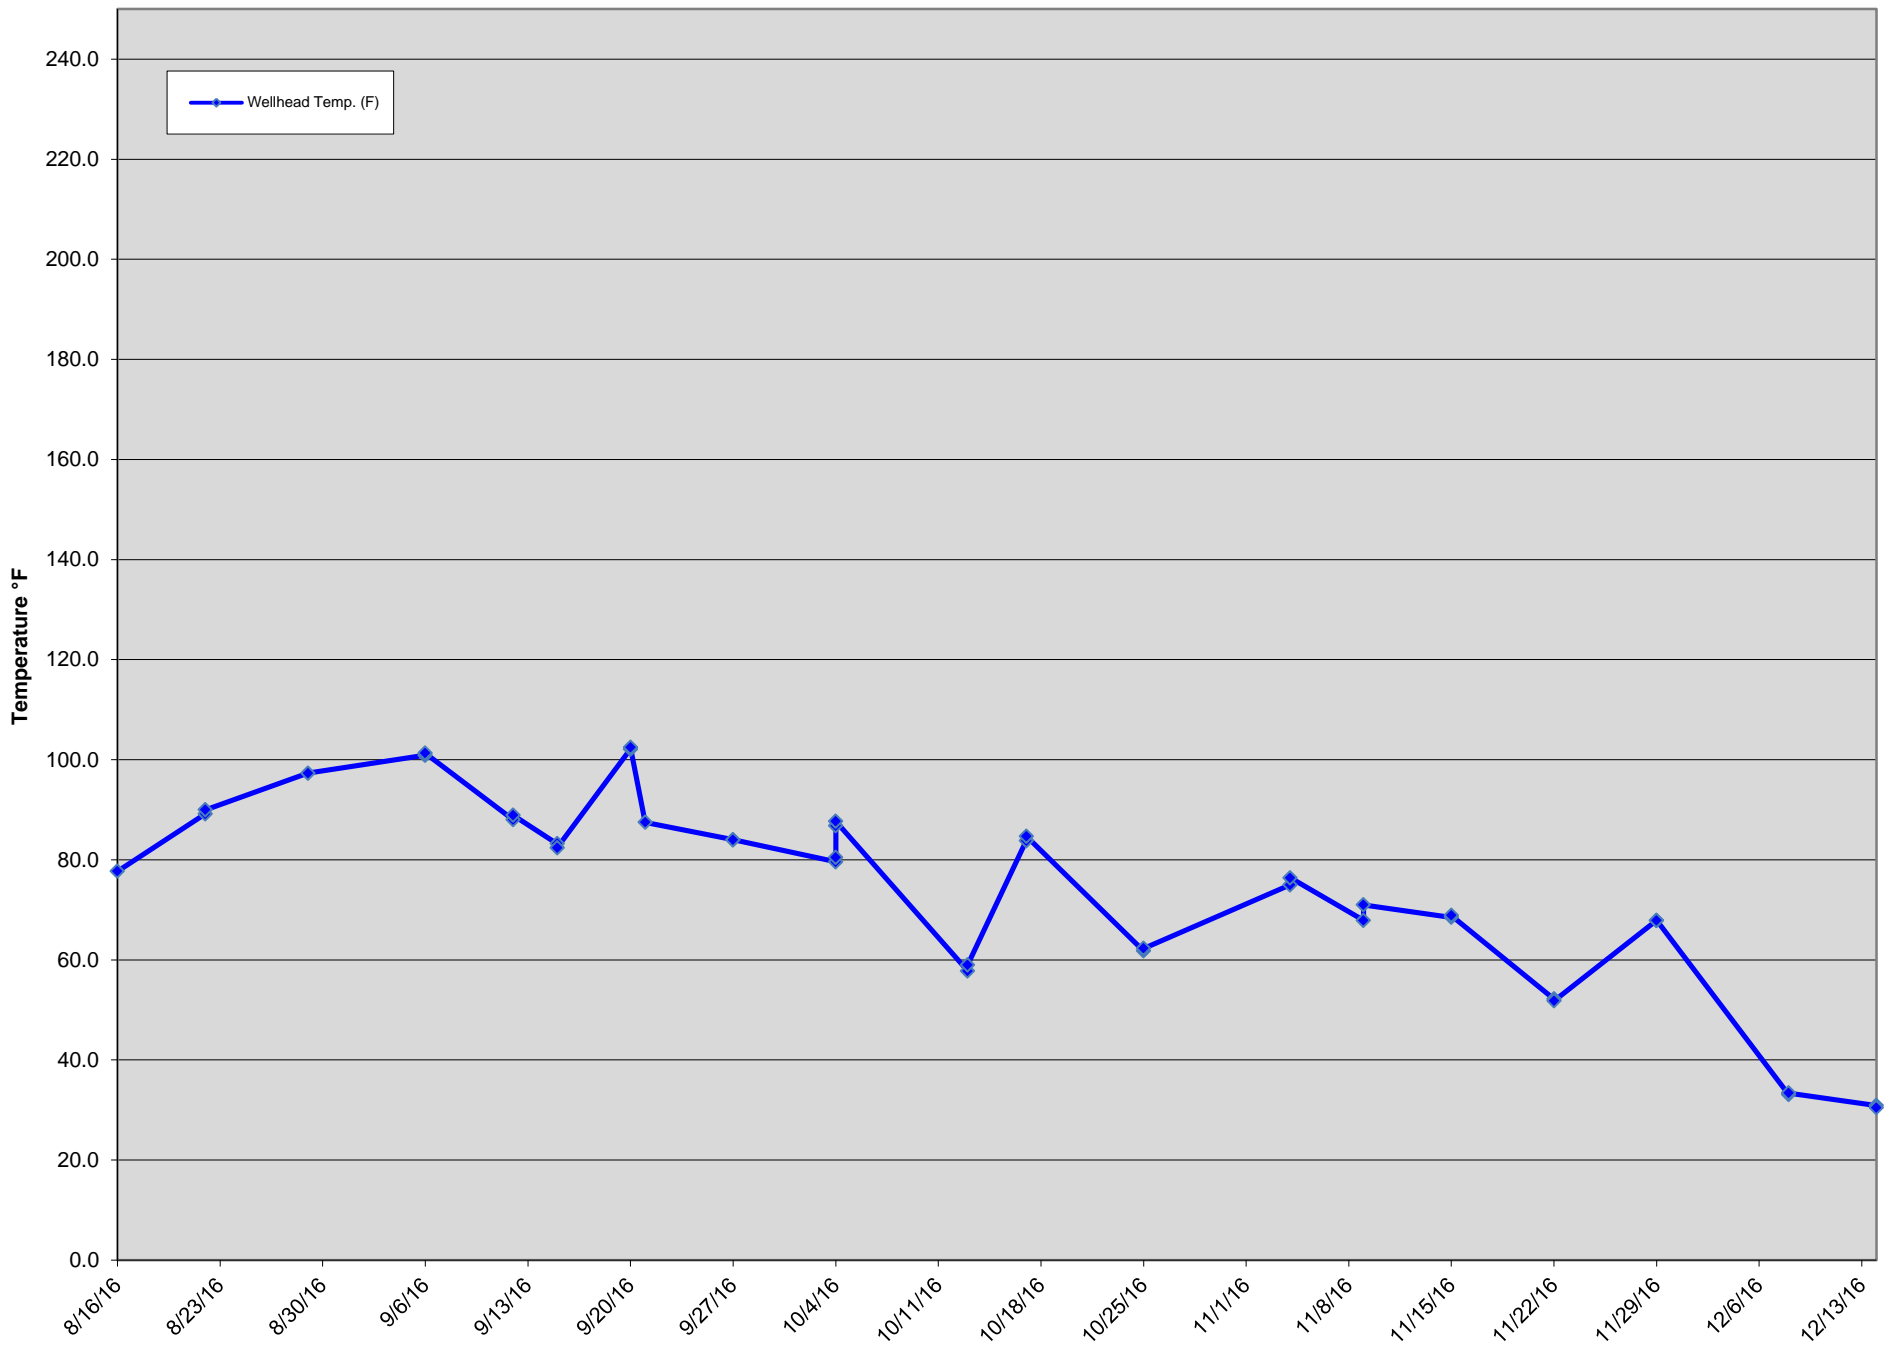


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-06	08/15/16	4.0	51.0	0.4	44.6	84.7	-13.5	N/A	(HES Installed)
GIW-06	08/22/16	4.5	49.3	0.4	45.8	83.8	-11.7	N/A	(HES Installed)
GIW-06	08/29/16	5.4	52.9	0.5	41.2	96.4	-10.7	N/A	(HES Installed)
GIW-06	09/06/16	4.9	55.2	0.5	39.4	92.7	-9.8	N/A	(HES Installed)
GIW-06	09/06/16	4.7	53.6	0.5	41.2	93.2	-10.2	N/A	(HES Installed)
GIW-06	09/15/16	6.4	50.5	0.4	42.7	83.8	-16.6	N/A	(HES Installed)
GIW-06	09/21/16	11.2	54.1	0.4	34.3	86.6	-10.0	N/A	(HES Installed)
GIW-06	09/27/16	9.5	57.1	0.5	32.9	88.6	-17.5	N/A	(HES Installed)
GIW-06	10/04/16	7.9	55.5	0.3	36.3	80.3	-10.6	N/A	(HES Installed)
GIW-06	10/04/16	7.9	55.7	0.3	36.1	81.0	-8.7	N/A	(HES Installed)
GIW-06	10/13/16	4.5	33.2	0.9	61.4	60.8	-8.3	N/A	(HES Installed)
GIW-06	10/17/16	6.7	23.6	0.6	69.1	84.4	-6.4	N/A	(HES Installed)
GIW-06	10/25/16	12.3	48.5	0.4	38.8	62.1	-8.3	N/A	(HES Installed)
GIW-06	11/04/16	12.4	55.1	0.5	32.0	83.0	-8.5	N/A	(HES Installed)
GIW-06	11/08/16	18.4	53.3	0.3	28.0	60.6	-10.4	N/A	(HES Installed)
GIW-06	11/08/16	17.4	51.3	0.2	31.1	60.9	-10.4	N/A	(HES Installed)
GIW-06	11/15/16	14.7	51.3	0.0	34.0	74.1	-6.4	N/A	(HES Installed)
GIW-06	11/22/16	27.3	48.5	0.2	24.0	51.8	-7.0	N/A	(HES Installed)
GIW-06	11/29/16	26.5	38.0	0.3	35.2	69.7	-6.1	N/A	(HES Installed)
GIW-06	12/09/16	27.3	49.5	0.1	23.1	40.2	-7.5	N/A	(HES Installed)
GIW-06	12/09/16	26.7	46.9	0.1	26.3	38.8	-7.5	N/A	(HES Installed)
GIW-06	12/14/16	3.5	36.4	0.6	59.5	31.7	-7.0	N/A	(HES Installed)

GIW-6 Wellhead Temperatures

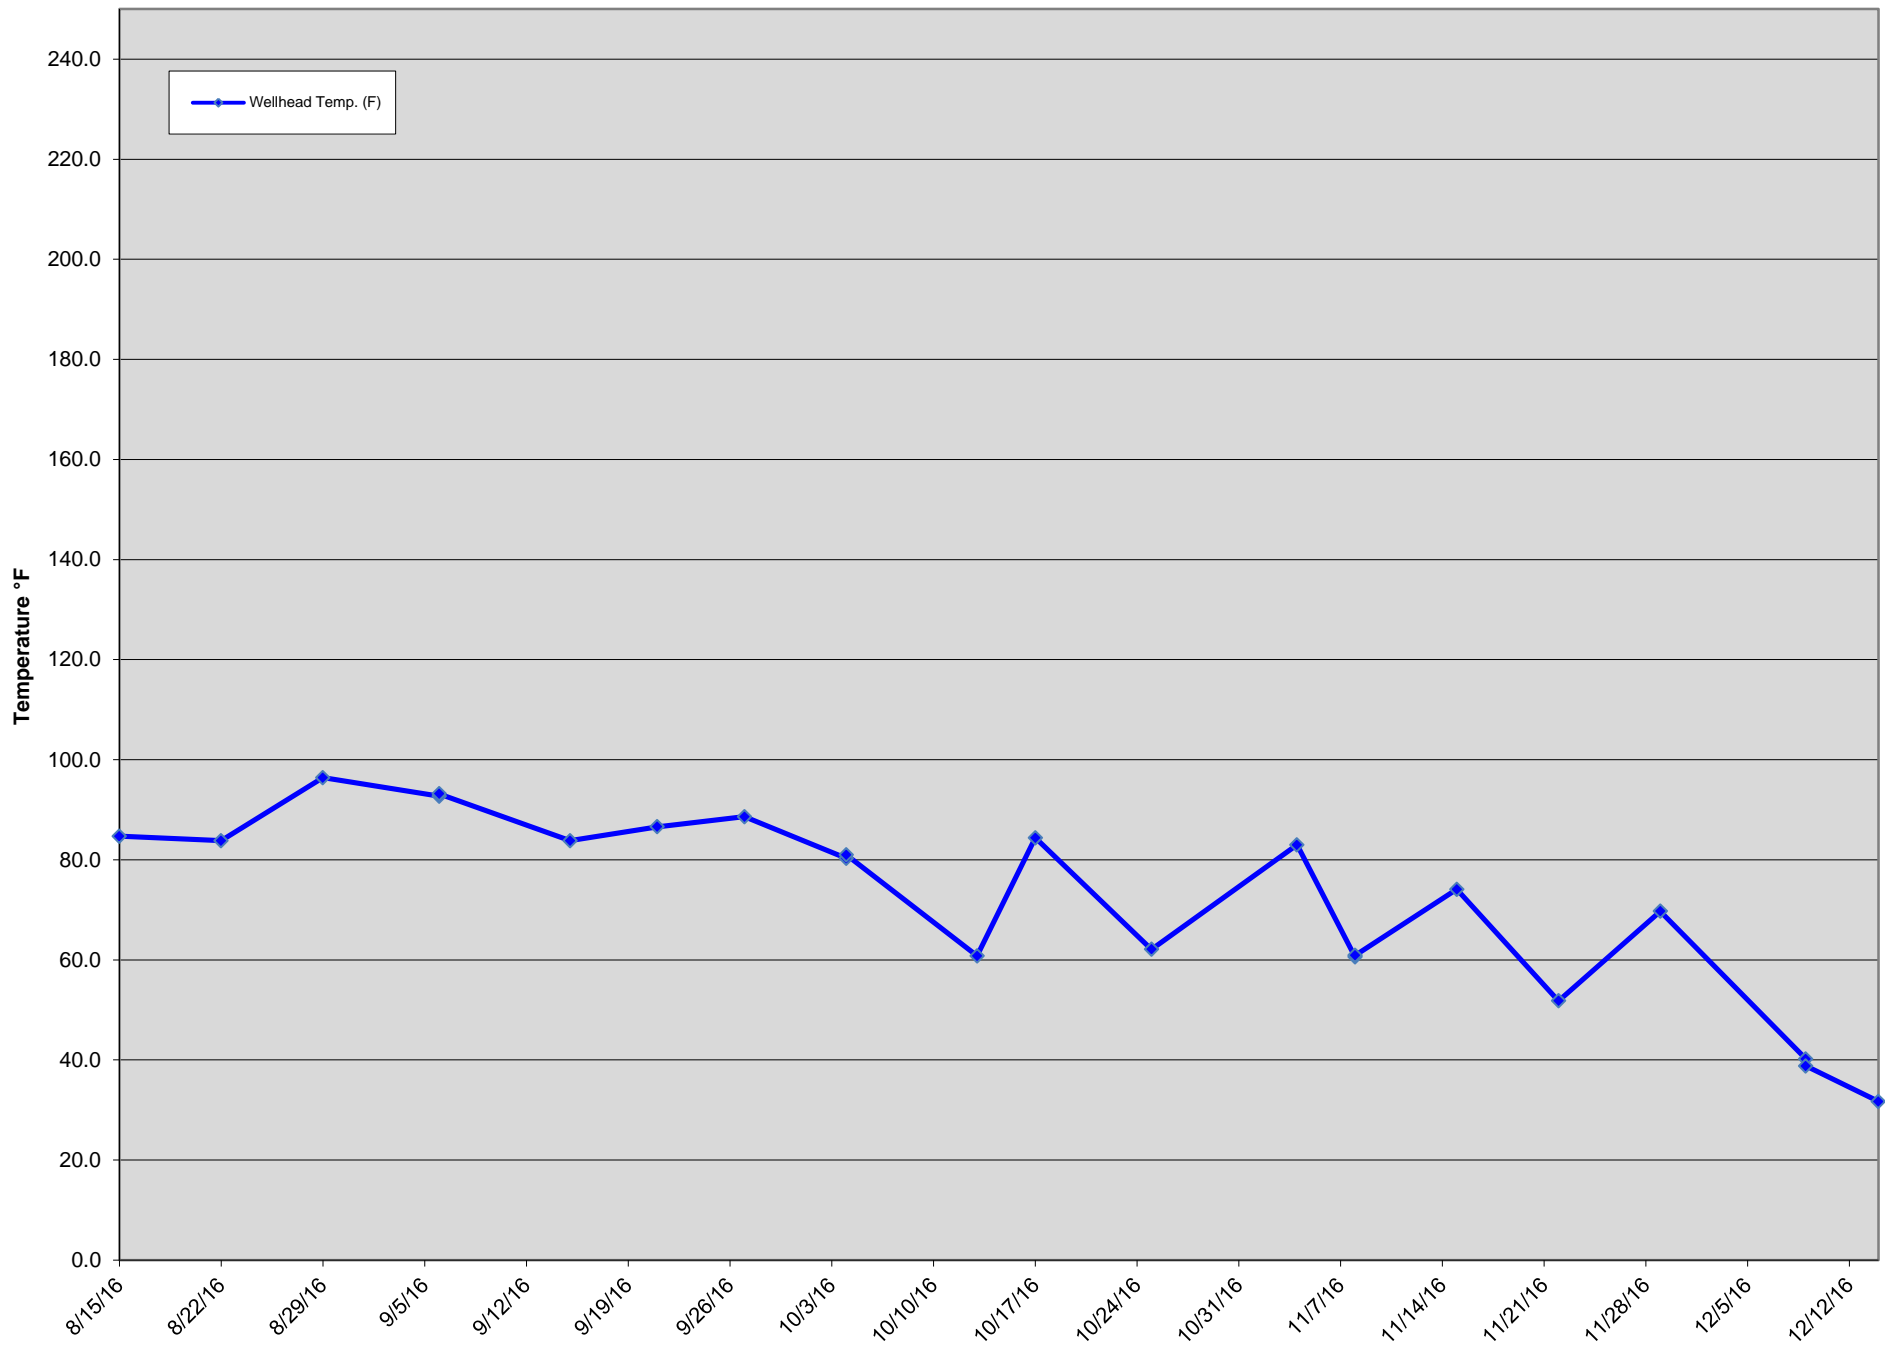


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-07	08/15/16	4.9	33.5	11.3	50.3	84.0	-2.7	N/A	(HES Installed)
GIW-07	08/15/16	5.4	37.3	10.6	46.7	83.8	-2.4	N/A	(HES Installed)
GIW-07	08/22/16	1.0	8.4	18.7	71.9	91.1	-2.5	N/A	(HES Installed)
GIW-07	08/22/16	1.2	10.1	18.1	70.6	92.1	-2.6	N/A	(HES Installed)
GIW-07	08/29/16	0.7	9.8	19.2	70.3	98.5	-2.4	N/A	(HES Installed)
GIW-07	08/29/16	1.0	7.9	19.0	72.1	99.8	-2.5	N/A	(HES Installed)
GIW-07	09/06/16	1.1	11.3	17.9	69.7	97.3	-2.4	N/A	(HES Installed)
GIW-07	09/06/16	1.4	13.1	17.3	68.2	97.9	-2.4	N/A	(HES Installed)
GIW-07	09/06/16	1.4	11.4	17.5	69.7	98.9	-2.4	N/A	(HES Installed)
GIW-07	09/06/16	1.5	12.2	17.2	69.1	101.1	-2.3	N/A	(HES Installed)
GIW-07	09/15/16	4.7	45.4	8.0	41.9	85.3	-0.7	N/A	(HES Installed)
GIW-07	09/15/16	5.3	52.2	6.4	36.1	86.6	-0.6	N/A	(HES Installed)
GIW-07	09/21/16	8.2	71.3	0.5	20.0	91.7	0.2	N/A	(HES Installed)
GIW-07	09/21/16	8.1	69.9	1.1	20.9	91.9	-1.8	N/A	(HES Installed)
GIW-07	09/27/16	18.2	53.8	2.1	25.9	90.5	-4.6	N/A	(HES Installed)
GIW-07	09/27/16	17.7	56.3	2.1	23.9	91.5	-2.8	N/A	(HES Installed)
GIW-07	10/04/16	12.0	61.3	1.7	25.0	81.5	-1.4	N/A	(HES Installed)
GIW-07	10/04/16	12.0	60.4	1.8	25.8	83.0	-0.7	N/A	(HES Installed)
GIW-07	10/13/16	9.8	49.9	3.3	37.0	61.5	-0.5	N/A	(HES Installed)
GIW-07	10/17/16	9.0	58.6	0.3	32.1	87.4	-0.2	N/A	(HES Installed)
GIW-07	10/25/16	5.8	48.7	0.1	45.4	62.8	1.1	N/A	(HES Installed)
GIW-07	10/25/16	4.7	48.1	0.2	47.0	63.5	-0.5	N/A	(HES Installed)
GIW-07	11/04/16	11.8	61.2	1.2	25.8	75.0	-1.1	N/A	(HES Installed)
GIW-07	11/08/16	13.1	55.3	1.7	29.9	61.6	-2.2	N/A	(HES Installed)
GIW-07	11/08/16	12.2	53.4	1.7	32.7	61.9	-2.0	N/A	(HES Installed)
GIW-07	11/15/16	20.2	55.0	0.0	24.8	72.7	0.1	N/A	(HES Installed)
GIW-07	11/15/16	20.6	56.0	0.2	23.2	75.5	-4.7	N/A	(HES Installed)
GIW-07	11/22/16	24.6	46.4	1.8	27.2	51.8	-7.0	N/A	(HES Installed)
GIW-07	11/29/16	20.2	51.4	1.6	26.8	69.8	-6.1	N/A	(HES Installed)
GIW-07	11/29/16	18.8	52.7	2.0	26.5	70.2	-3.5	N/A	(HES Installed)
GIW-07	12/09/16	28.0	45.0	1.2	25.8	40.5	-3.1	N/A	(HES Installed)
GIW-07	12/09/16	26.9	48.3	1.2	23.6	36.2	-2.9	N/A	(HES Installed)
GIW-07	12/14/16	22.1	46.1	0.9	30.9	34.1	-1.9	N/A	(HES Installed)

GIW-7 Wellhead Temperatures

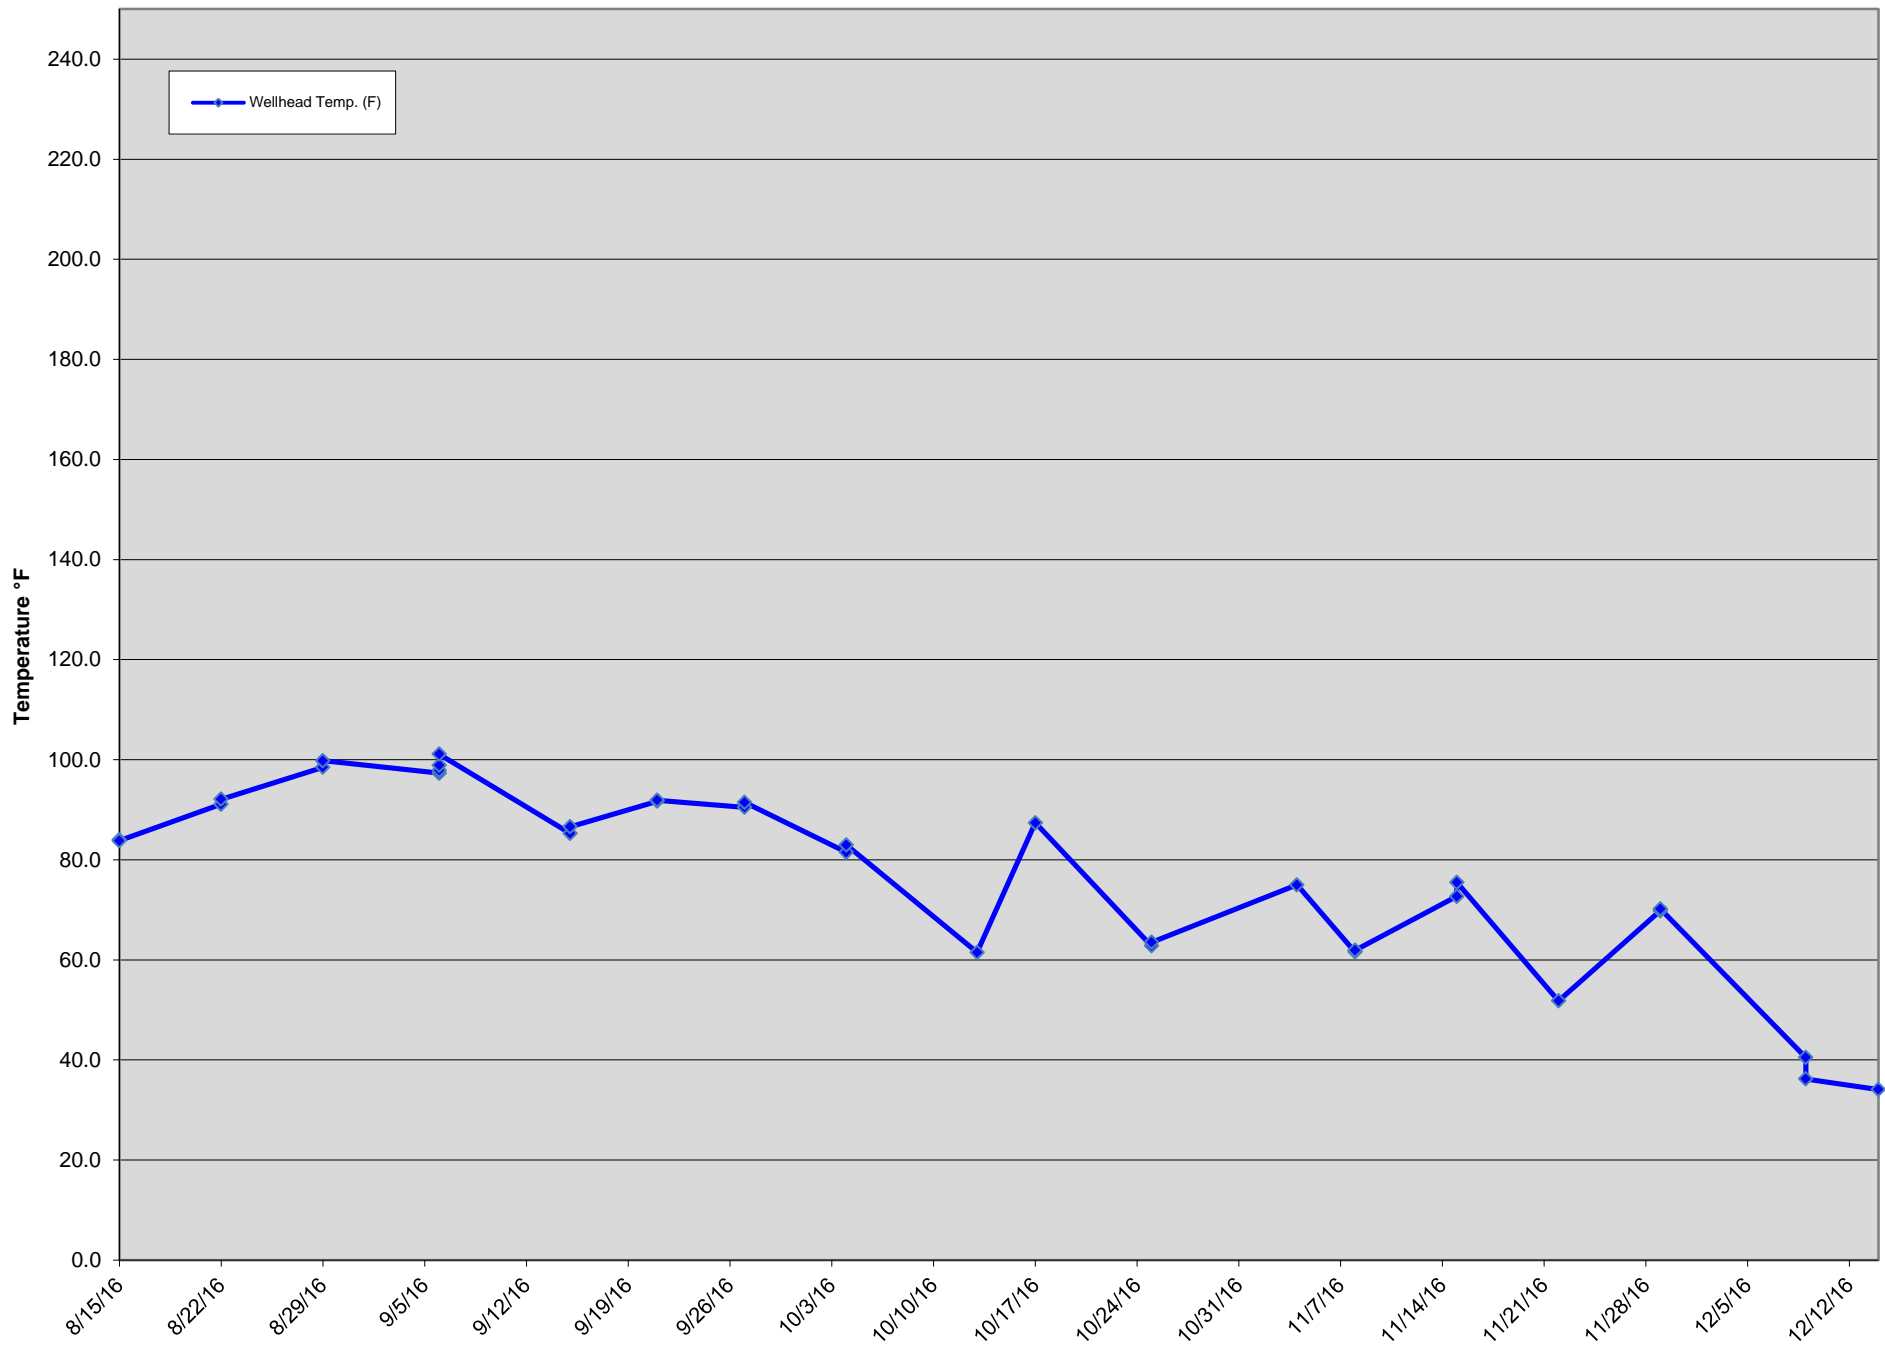


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-08	08/15/16	16.0	55.7	0.2	28.1	84.9	-9.1	N/A	(HES Installed)
GIW-08	08/15/16	16.2	54.5	0.2	29.1	85.3	-7.2	N/A	(HES Installed)
GIW-08	08/22/16	17.0	55.1	0.1	27.8	88.4	-5.9	N/A	(HES Installed)
GIW-08	08/29/16	17.3	59.3	0.2	23.2	96.1	-5.3	N/A	(HES Installed)
GIW-08	09/06/16	17.5	60.1	0.3	22.1	99.2	-5.0	N/A	(HES Installed)
GIW-08	09/06/16	17.4	59.6	0.4	22.6	98.8	-4.9	N/A	(HES Installed)
GIW-08	09/15/16	18.0	59.9	0.2	21.9	83.6	-7.1	N/A	(HES Installed)
GIW-08	09/21/16	23.1	60.0	0.3	16.6	88.9	-3.9	N/A	(HES Installed)
GIW-08	09/27/16	20.9	57.6	0.2	21.3	91.0	-6.9	N/A	(HES Installed)
GIW-08	10/04/16	23.3	59.2	0.0	17.5	75.7	-5.5	N/A	(HES Installed)
GIW-08	10/04/16	23.5	58.7	0.0	17.8	77.0	-5.1	N/A	(HES Installed)
GIW-08	10/13/16	23.2	52.2	0.0	24.6	64.0	-4.8	N/A	(HES Installed)
GIW-08	10/17/16	21.9	60.3	0.0	17.8	88.0	-4.0	N/A	(HES Installed)
GIW-08	10/25/16	25.7	57.6	0.2	16.5	63.6	-4.8	N/A	(HES Installed)
GIW-08	11/04/16	22.0	59.2	0.3	18.5	76.8	-5.0	N/A	(HES Installed)
GIW-08	11/08/16	23.6	52.4	0.1	23.9	62.8	-5.9	N/A	(HES Installed)
GIW-08	11/08/16	24.5	52.7	0.3	22.5	62.4	-5.8	N/A	(HES Installed)
GIW-08	11/15/16	32.9	51.8	0.0	15.3	69.0	-3.4	N/A	(HES Installed)
GIW-08	11/22/16	26.6	56.6	0.0	16.8	52.0	-4.6	N/A	(HES Installed)
GIW-08	11/29/16	28.2	55.7	0.0	16.1	68.1	-4.0	N/A	(HES Installed)
GIW-08	12/09/16	34.6	54.5	0.0	10.9	40.7	-4.7	N/A	(HES Installed)
GIW-08	12/09/16	35.9	51.7	0.0	12.4	42.5	-4.7	N/A	(HES Installed)
GIW-08	12/14/16	17.5	31.3	0.1	51.1	35.0	-4.1	N/A	(HES Installed)

GIW-8 Wellhead Temperatures

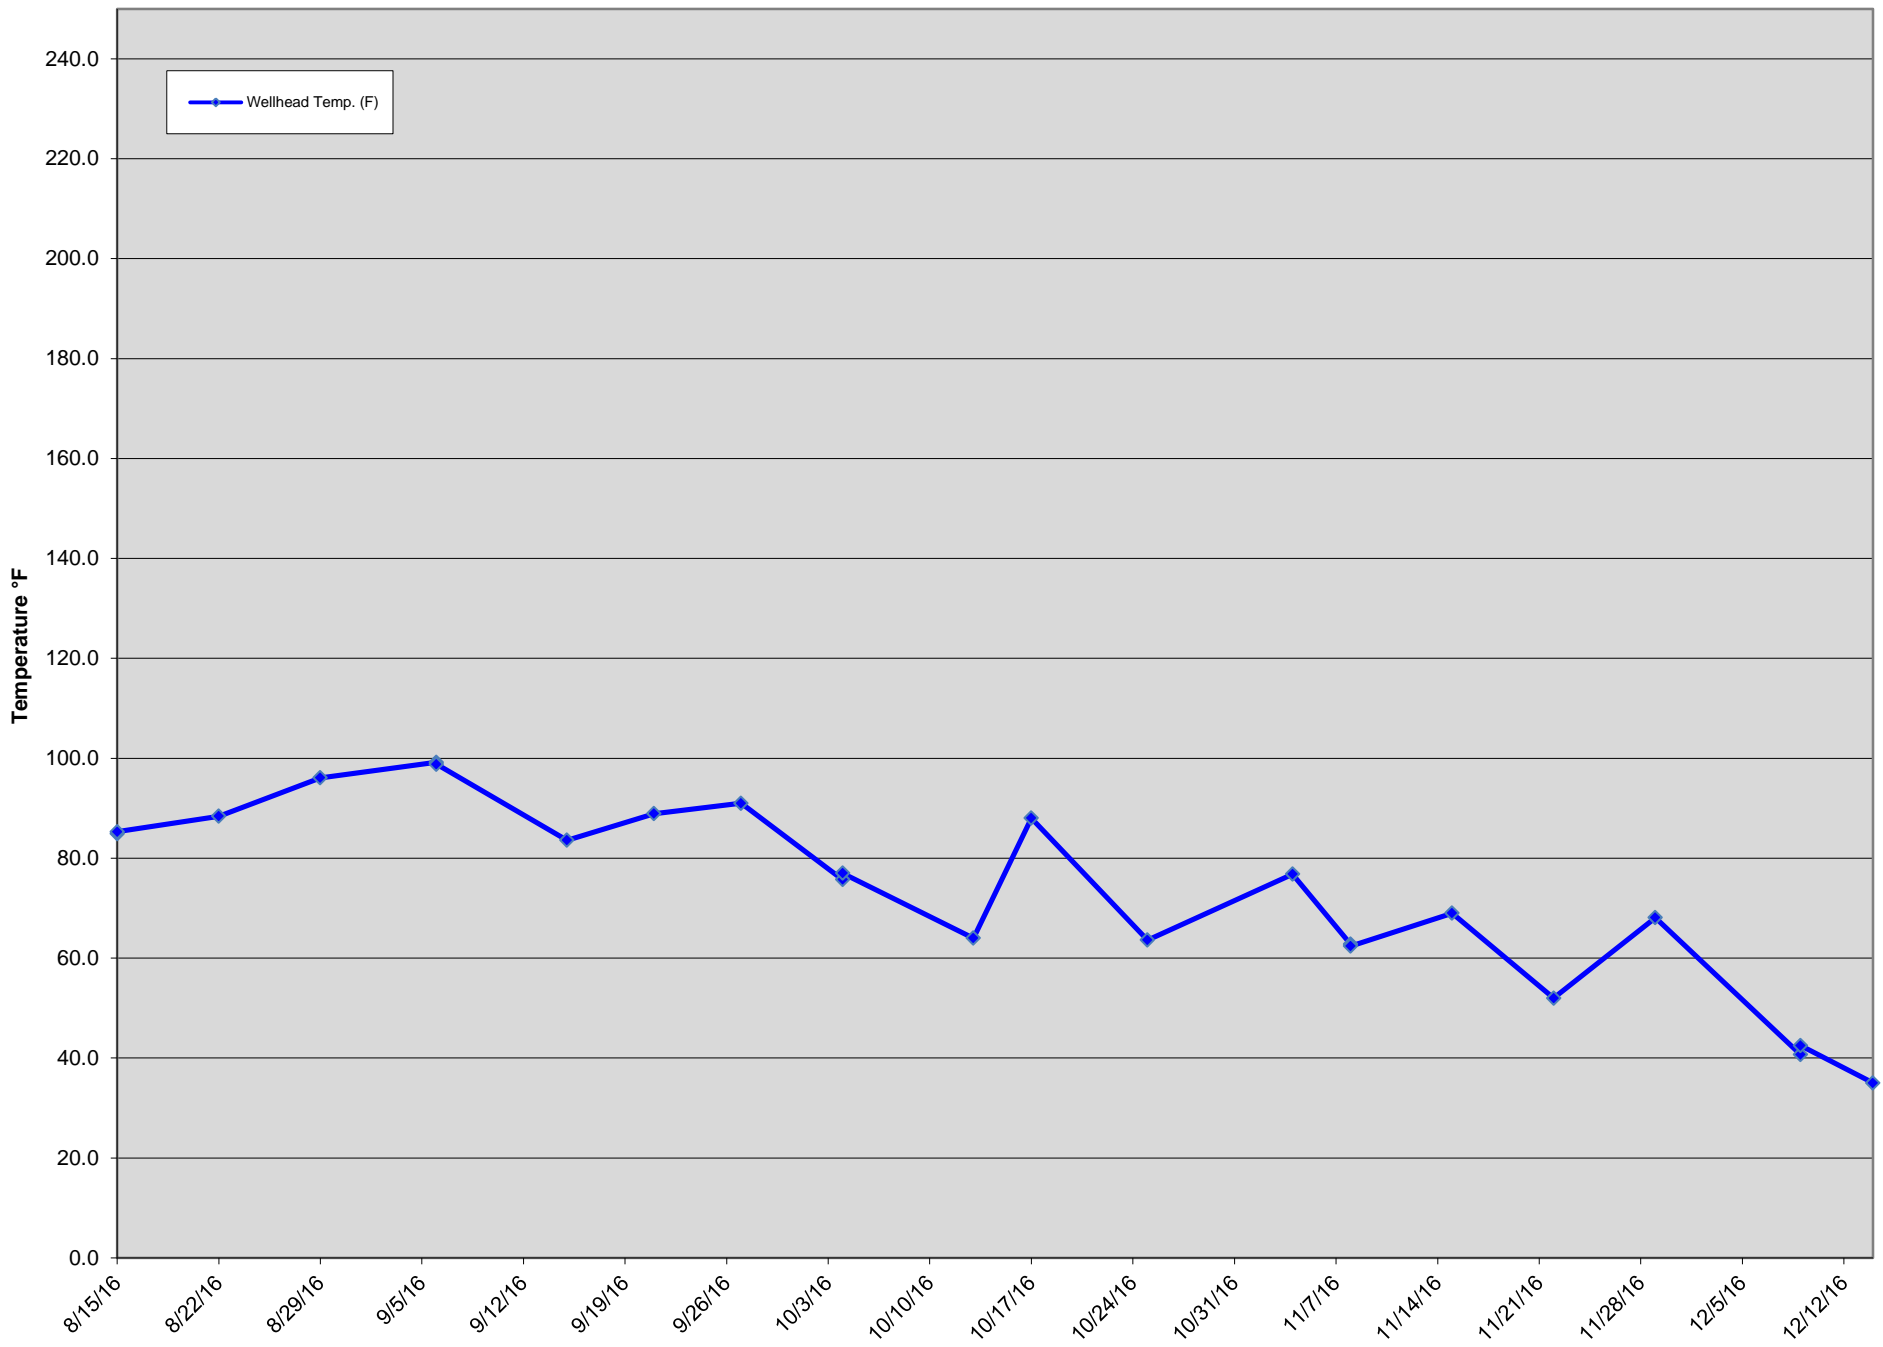


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-09	08/15/16	3.8	22.5	5.5	68.2	85.1	-5.7	N/A	(HES Installed)
GIW-09	08/15/16	3.9	22.8	5.3	68.0	84.7	-5.7	N/A	(HES Installed)
GIW-09	08/22/16	1.9	18.0	11.3	68.8	88.8	-4.7	N/A	(HES Installed)
GIW-09	08/22/16	2.0	15.9	11.5	70.6	89.0	-4.8	N/A	(HES Installed)
GIW-09	08/29/16	2.8	20.2	9.3	67.7	96.2	-4.6	N/A	(HES Installed)
GIW-09	08/29/16	2.6	18.5	9.4	69.5	96.4	-4.6	N/A	(HES Installed)
GIW-09	09/06/16	2.9	16.5	11.0	69.6	95.6	-4.2	N/A	(HES Installed)
GIW-09	09/06/16	2.6	15.3	11.1	71.0	96.2	-4.2	N/A	(HES Installed)
GIW-09	09/15/16	3.7	19.1	10.7	66.5	85.5	-5.1	N/A	(HES Installed)
GIW-09	09/15/16	3.4	17.0	10.9	68.7	85.7	-5.1	N/A	(HES Installed)
GIW-09	09/21/16	5.3	22.3	10.6	61.8	88.0	-3.1	N/A	(HES Installed)
GIW-09	09/21/16	5.4	20.9	10.7	63.0	88.4	-3.1	N/A	(HES Installed)
GIW-09	09/27/16	9.1	33.0	3.4	54.5	94.6	-4.5	N/A	(HES Installed)
GIW-09	10/04/16	5.4	20.2	10.4	64.0	90.1	-2.9	N/A	(HES Installed)
GIW-09	10/04/16	5.4	19.8	10.3	64.5	89.8	-2.8	N/A	(HES Installed)
GIW-09	10/04/16	5.6	21.5	7.8	65.1	99.0	-2.0	N/A	(HES Installed)
GIW-09	10/04/16	5.7	22.0	7.7	64.6	98.4	-2.0	N/A	(HES Installed)
GIW-09	10/13/16	4.9	30.2	12.2	52.7	66.2	-2.4	N/A	(HES Installed)
GIW-09	10/13/16	4.1	21.4	12.8	61.7	66.3	-2.4	N/A	(HES Installed)
GIW-09	10/17/16	15.9	37.6	8.0	38.5	88.6	-2.1	N/A	(HES Installed)
GIW-09	10/17/16	7.6	28.5	8.4	55.5	88.9	-2.2	N/A	(HES Installed)
GIW-09	10/25/16	5.3	23.5	11.3	59.9	66.1	-2.6	N/A	(HES Installed)
GIW-09	10/25/16	5.4	20.5	11.6	62.5	66.3	-2.5	N/A	(HES Installed)
GIW-09	11/04/16	4.2	22.0	13.7	60.1	79.8	-4.0	N/A	(HES Installed)
GIW-09	11/04/16	4.1	13.4	14.2	68.3	80.3	-1.1	N/A	(HES Installed)
GIW-09	11/09/16	0.8	7.6	18.0	73.6	69.8	-1.1	N/A	(HES Installed)
GIW-09	11/09/16	0.8	8.1	17.8	73.3	70.1	-1.1	N/A	(HES Installed)
GIW-09	11/15/16	7.8	22.9	10.9	58.4	71.6	-0.5	N/A	(HES Installed)
GIW-09	11/15/16	7.9	22.1	11.0	59.0	71.6	-0.5	N/A	(HES Installed)
GIW-09	11/22/16	1.6	13.9	17.5	67.0	52.1	-0.8	N/A	(HES Installed)
GIW-09	11/22/16	1.7	11.3	17.8	69.2	52.1	-0.9	N/A	(HES Installed)
GIW-09	11/29/16	5.8	27.4	9.4	57.4	68.4	-0.7	N/A	(HES Installed)
GIW-09	11/29/16	6.3	21.9	9.8	62.0	68.4	-0.7	N/A	(HES Installed)
GIW-09	12/09/16	5.4	17.9	11.5	65.2	42.1	-0.8	N/A	(HES Installed)
GIW-09	12/09/16	5.3	15.2	11.9	67.6	41.5	-0.8	N/A	(HES Installed)
GIW-09	12/14/16	5.7	21.8	8.2	64.3	36.5	-0.6	N/A	(HES Installed)
GIW-09	12/14/16	5.8	21.1	8.3	64.8	36.1	-0.6	N/A	(HES Installed)

GIW-9 Wellhead Temperatures

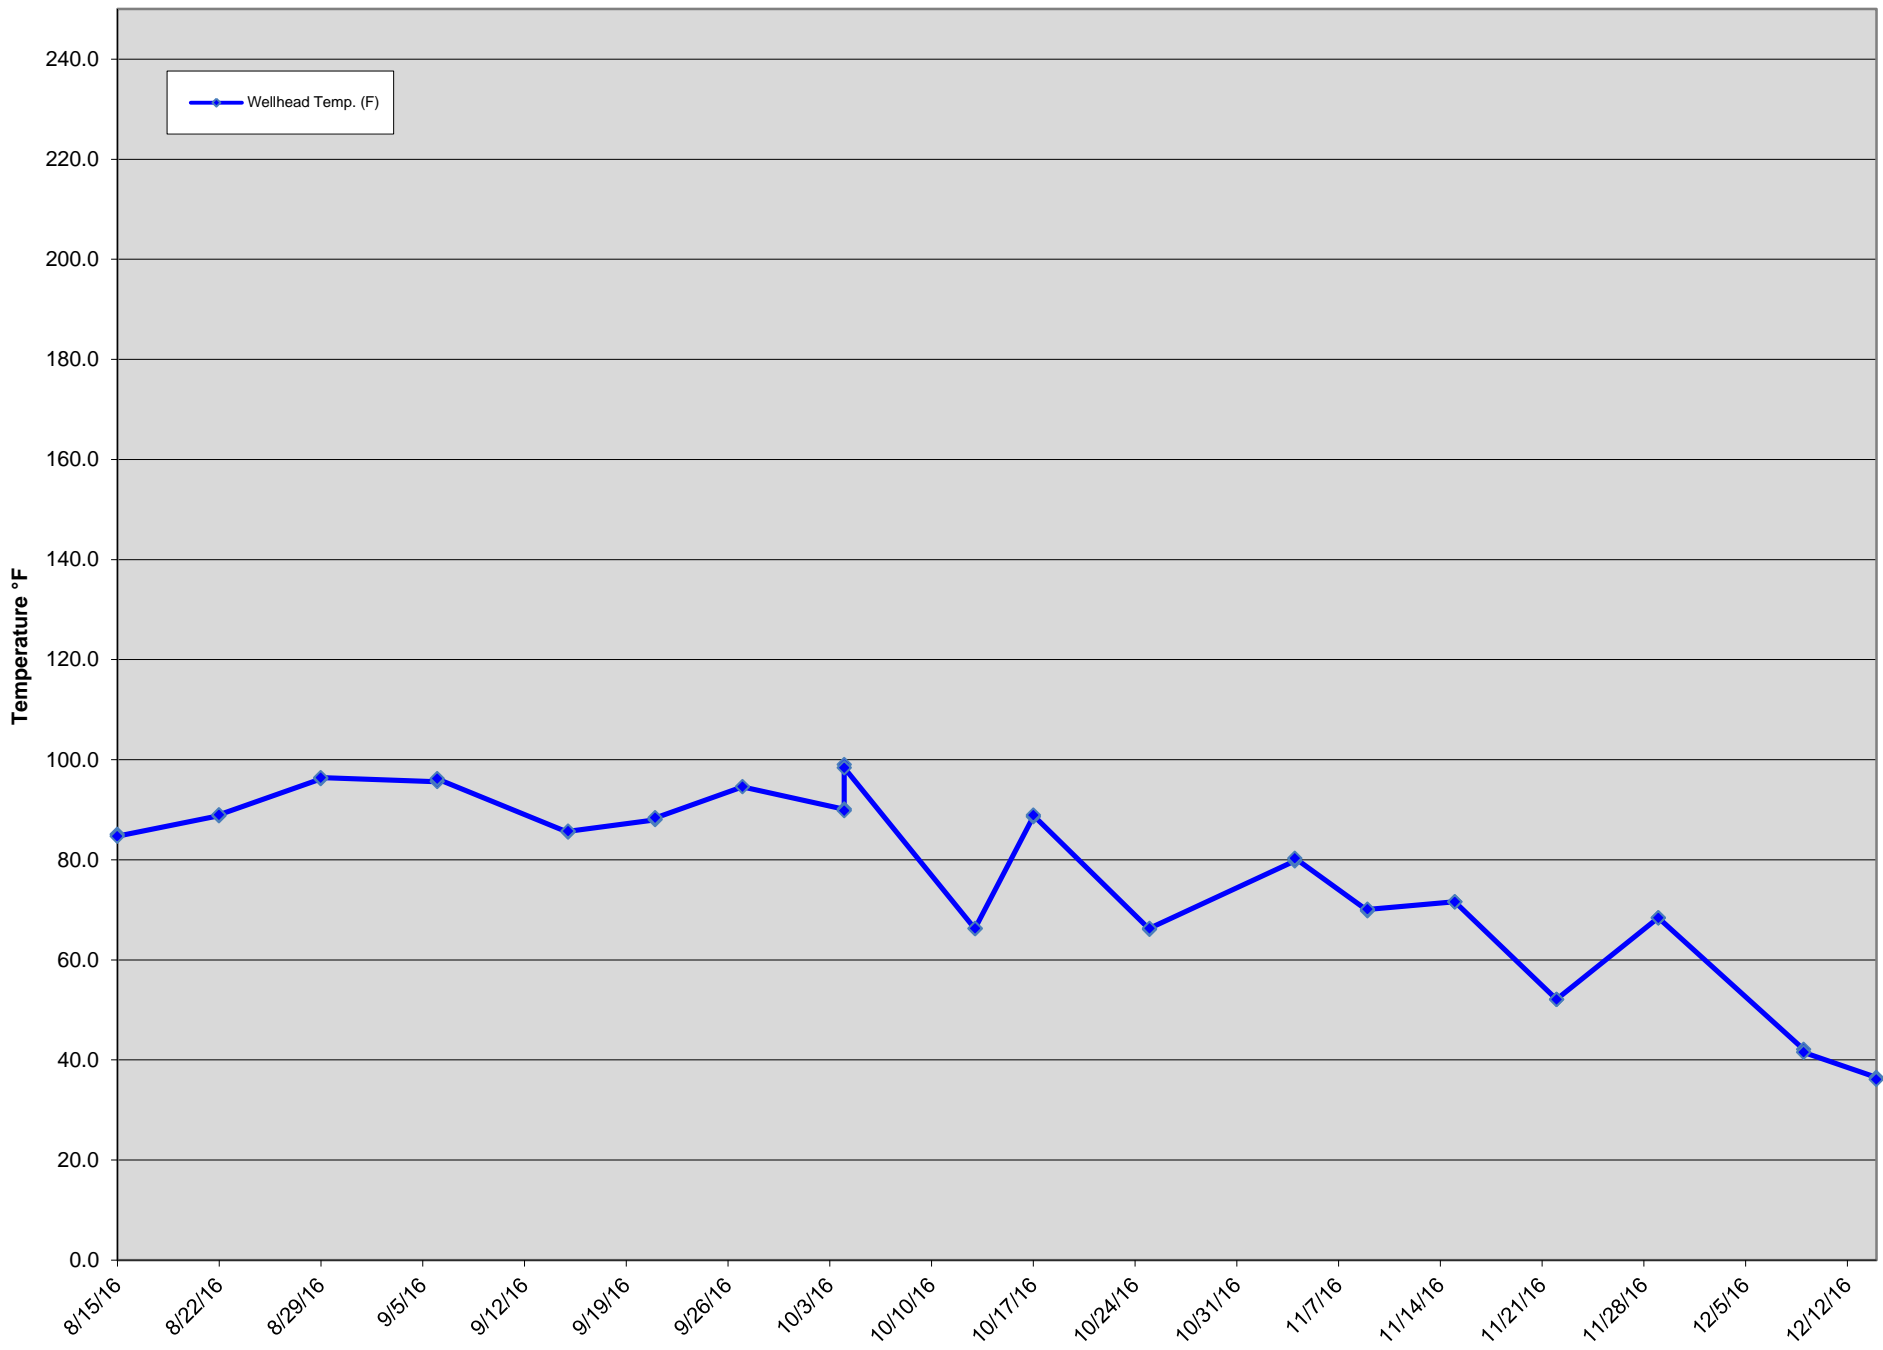


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-10	08/16/16	0.8	57.4	0.1	41.7	79.7	-1.7	N/A	(HES Installed)
GIW-10	08/22/16	1.0	56.5	0.1	42.4	88.6	-1.3	N/A	(HES Installed)
GIW-10	08/29/16	1.4	58.6	0.4	39.6	102.8	-1.2	N/A	(HES Installed)
GIW-10	09/06/16	1.3	57.5	0.3	40.9	99.4	-1.4	N/A	(HES Installed)
GIW-10	09/06/16	1.1	55.3	0.3	43.3	98.9	-1.4	N/A	(HES Installed)
GIW-10	09/15/16	3.3	55.5	0.2	41.0	89.7	-2.2	N/A	(HES Installed)
GIW-10	09/21/16	0.8	56.6	0.2	42.4	93.1	-0.6	N/A	(HES Installed)
GIW-10	09/27/16	6.4	50.6	0.1	42.9	88.9	-3.0	N/A	(HES Installed)
GIW-10	10/04/16	4.4	54.6	0.0	41.0	85.1	-1.7	N/A	(HES Installed)
GIW-10	10/04/16	4.9	51.9	0.0	43.2	86.1	-1.6	N/A	(HES Installed)
GIW-10	10/13/16	4.6	51.6	0.0	43.8	63.1	-2.0	N/A	(HES Installed)
GIW-10	10/17/16	6.0	34.7	0.0	59.3	86.8	-1.3	N/A	(HES Installed)
GIW-10	10/25/16	4.4	54.7	0.0	40.9	68.1	-2.1	N/A	(HES Installed)
GIW-10	11/04/16	5.0	50.9	0.2	43.9	79.8	-2.3	N/A	(HES Installed)
GIW-10	11/09/16	4.7	49.9	0.0	45.4	70.5	-2.0	N/A	(HES Installed)
GIW-10	11/09/16	4.4	51.0	0.0	44.6	71.1	-1.9	N/A	(HES Installed)
GIW-10	11/15/16	8.2	49.9	0.0	41.9	73.0	-1.3	N/A	(HES Installed)
GIW-10	11/22/16	4.9	53.5	0.0	41.6	51.6	-1.9	N/A	(HES Installed)
GIW-10	11/29/16	5.9	54.3	0.0	39.8	69.4	-1.7	N/A	(HES Installed)
GIW-10	12/08/16	10.2	49.9	0.0	39.9	38.1	-2.0	N/A	(HES Installed)
GIW-10	12/08/16	10.0	51.9	0.0	38.1	38.9	-1.9	N/A	(HES Installed)
GIW-10	12/14/16	7.1	45.8	0.2	46.9	31.8	-1.2	N/A	(HES Installed)

GIW-10 Wellhead Temperatures

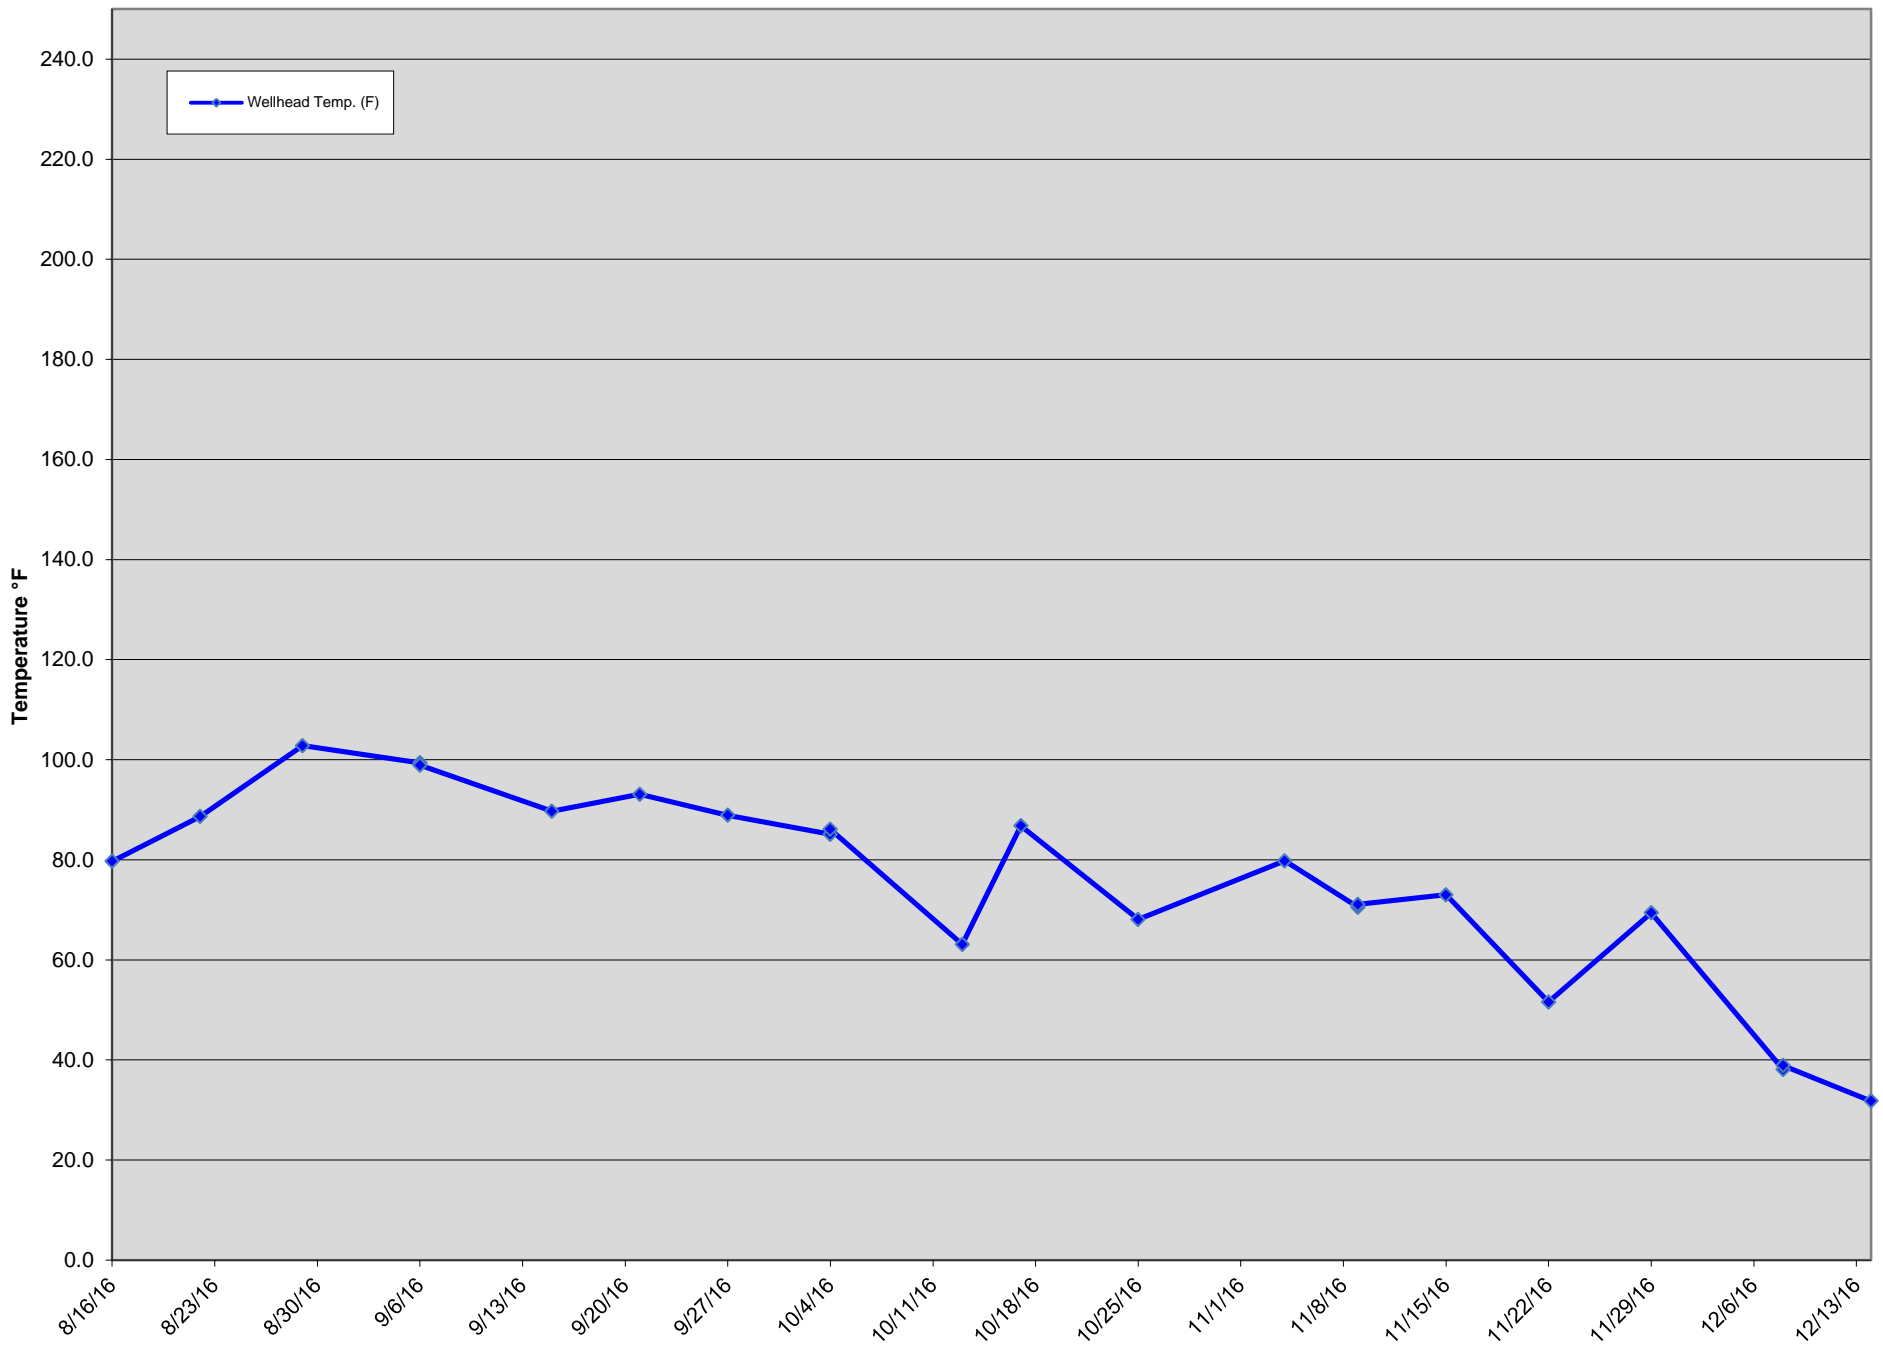


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-11	08/16/16	6.8	57.0	1.9	34.3	79.9	-1.8	N/A	(HES Installed)
GIW-11	08/22/16	7.3	55.7	1.2	35.8	86.8	-1.4	N/A	(HES Installed)
GIW-11	08/29/16	7.3	62.2	1.4	29.1	98.1	-1.3	N/A	(HES Installed)
GIW-11	09/06/16	9.5	61.6	1.6	27.3	97.3	-1.8	N/A	(HES Installed)
GIW-11	09/06/16	9.5	58.3	1.7	30.5	97.3	-1.7	N/A	(HES Installed)
GIW-11	09/15/16	9.0	57.7	1.6	31.7	88.6	-2.0	N/A	(HES Installed)
GIW-11	09/20/16	7.6	53.7	1.0	37.7	105.5	-1.5	N/A	(HES Installed)
GIW-11	09/21/16	6.7	55.3	0.9	37.1	89.8	-1.5	N/A	(HES Installed)
GIW-11	09/27/16	10.0	54.8	0.7	34.5	86.8	-1.6	N/A	(HES Installed)
GIW-11	10/04/16	8.1	59.9	0.6	31.4	81.9	-1.6	N/A	(HES Installed)
GIW-11	10/04/16	7.4	56.1	0.7	35.8	83.0	-1.6	N/A	(HES Installed)
GIW-11	10/13/16	7.8	56.1	0.3	35.8	63.3	-1.7	N/A	(HES Installed)
GIW-11	10/17/16	5.6	57.8	0.3	36.3	87.7	-1.4	N/A	(HES Installed)
GIW-11	10/25/16	10.5	52.3	0.6	36.6	64.2	-1.8	N/A	(HES Installed)
GIW-11	11/04/16	8.4	43.2	2.8	45.6	82.8	-6.0	N/A	(HES Installed)
GIW-11	11/04/16	9.0	44.4	2.4	44.2	83.4	-0.9	N/A	(HES Installed)
GIW-11	11/09/16	1.1	57.4	0.0	41.5	71.6	0.2	N/A	(HES Installed)
GIW-11	11/09/16	0.8	59.6	0.0	39.6	72.6	0.0	N/A	(HES Installed)
GIW-11	11/15/16	2.3	62.0	0.0	35.7	72.0	-0.3	N/A	(HES Installed)
GIW-11	11/22/16	3.8	60.4	0.0	35.8	51.4	-0.5	N/A	(HES Installed)
GIW-11	11/29/16	2.8	59.8	0.0	37.4	69.1	-0.5	N/A	(HES Installed)
GIW-11	12/09/16	2.3	60.8	0.0	36.9	35.2	-0.5	N/A	(HES Installed)
GIW-11	12/09/16	1.6	59.0	0.0	39.4	35.7	-0.5	N/A	(HES Installed)
GIW-11	12/14/16	3.0	61.6	0.2	35.2	30.0	-0.4	N/A	(HES Installed)

GIW-11 Wellhead Temperatures

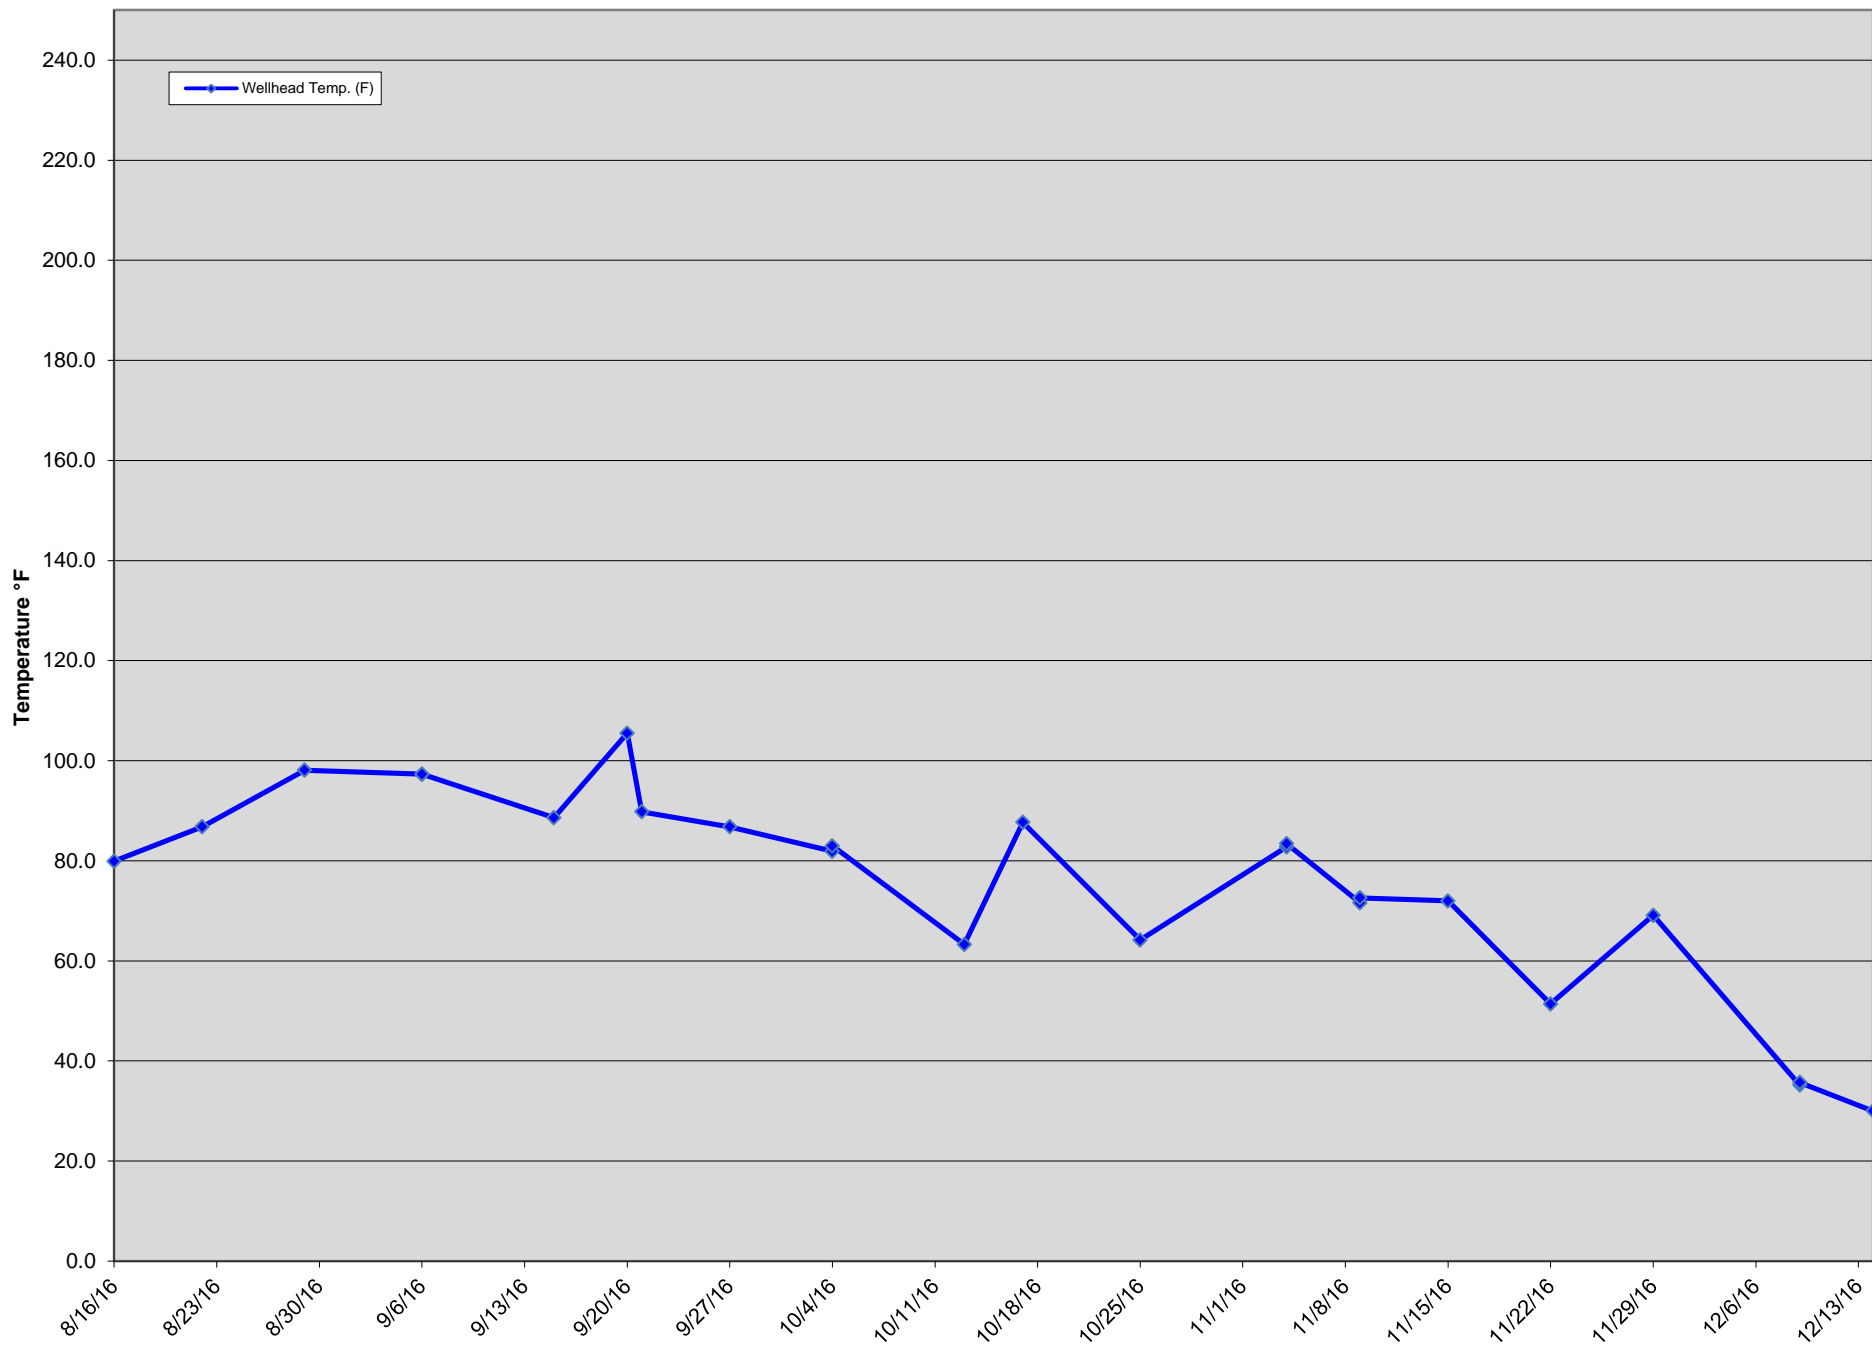

GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-12	08/16/16	5.6	34.0	9.3	51.1	79.0	-0.5	N/A	(HES Installed)
GIW-12	08/16/16	5.7	32.7	9.4	52.2	79.1	-0.5	N/A	(HES Installed)
GIW-12	08/22/16	13.6	39.8	5.0	41.6	83.5	-0.3	N/A	(HES Installed)
GIW-12	08/22/16	12.3	41.7	5.0	41.0	83.6	-0.3	N/A	(HES Installed)
GIW-12	08/29/16	13.1	45.8	5.7	35.4	97.3	-0.3	N/A	(HES Installed)
GIW-12	08/29/16	13.4	45.2	5.8	35.6	97.6	-0.3	N/A	(HES Installed)
GIW-12	09/06/16	8.7	32.4	9.1	49.8	97.7	-0.5	N/A	(HES Installed)
GIW-12	09/06/16	9.2	31.8	9.2	49.8	98.3	-0.5	N/A	(HES Installed)
GIW-12	09/15/16	5.8	30.1	10.6	53.5	87.0	-0.5	N/A	(HES Installed)
GIW-12	09/15/16	5.7	28.8	10.7	54.8	87.4	-0.6	N/A	(HES Installed)
GIW-12	09/20/16	5.2	25.2	11.2	58.4	95.5	-0.4	N/A	(HES Installed)
GIW-12	09/20/16	5.3	23.8	11.2	59.7	96.2	-0.4	N/A	(HES Installed)
GIW-12	09/21/16	7.4	34.6	7.3	50.7	89.1	-0.4	N/A	(HES Installed)
GIW-12	09/21/16	7.4	32.3	7.3	53.0	89.1	-0.4	N/A	(HES Installed)
GIW-12	09/27/16	13.5	41.1	5.2	40.2	87.0	-0.3	N/A	(HES Installed)
GIW-12	09/27/16	13.9	39.1	5.3	41.7	86.5	-0.4	N/A	(HES Installed)
GIW-12	10/04/16	13.7	39.1	6.2	41.0	80.3	-0.3	N/A	(HES Installed)
GIW-12	10/04/16	14.0	38.4	6.2	41.4	80.9	-0.4	N/A	(HES Installed)
GIW-12	10/04/16	14.3	40.7	4.6	40.4	86.1	-0.3	N/A	(HES Installed)
GIW-12	10/04/16	14.5	40.3	4.6	40.6	87.8	-0.3	N/A	(HES Installed)
GIW-12	10/13/16	13.5	48.2	6.7	31.6	62.1	-0.3	N/A	(HES Installed)
GIW-12	10/13/16	14.7	40.1	7.1	38.1	62.6	-0.4	N/A	(HES Installed)
GIW-12	10/17/16	10.7	47.2	4.7	37.4	87.3	-0.3	N/A	(HES Installed)
GIW-12	10/25/16	14.3	41.1	6.4	38.2	64.0	-0.4	N/A	(HES Installed)
GIW-12	10/25/16	14.5	38.8	6.5	40.2	63.8	-0.4	N/A	(HES Installed)
GIW-12	11/04/16	6.3	23.1	9.5	61.1	84.1	-10.5	N/A	(HES Installed)
GIW-12	11/04/16	6.5	22.9	9.7	60.9	83.0	-1.2	N/A	(HES Installed)
GIW-12	11/09/16	8.5	36.9	6.9	47.7	69.0	-0.5	N/A	(HES Installed)
GIW-12	11/09/16	8.9	34.4	7.1	49.6	69.8	-0.5	N/A	(HES Installed)
GIW-12	11/15/16	8.2	44.0	7.5	40.3	70.2	-0.5	N/A	(HES Installed)
GIW-12	11/15/16	9.5	34.8	7.9	47.8	70.7	-0.5	N/A	(HES Installed)
GIW-12	11/22/16	9.2	36.6	8.4	45.8	52.1	-0.5	N/A	(HES Installed)
GIW-12	11/22/16	9.3	35.3	8.5	46.9	52.1	-0.5	N/A	(HES Installed)
GIW-12	11/29/16	8.7	45.1	7.4	38.8	69.4	-0.6	N/A	(HES Installed)
GIW-12	11/29/16	9.5	35.8	8.0	46.7	69.8	-0.8	N/A	(HES Installed)
GIW-12	12/09/16	7.7	31.2	9.2	51.9	36.0	-0.6	N/A	(HES Installed)
GIW-12	12/09/16	8.3	30.9	9.1	51.7	37.1	-0.9	N/A	(HES Installed)
GIW-12	12/14/16	8.4	35.8	8.7	47.1	31.5	-1.0	N/A	(HES Installed)
GIW-12	12/14/16	8.4	35.0	8.8	47.8	30.1	-0.4	N/A	(HES Installed)

GIW-12 Wellhead Temperatures

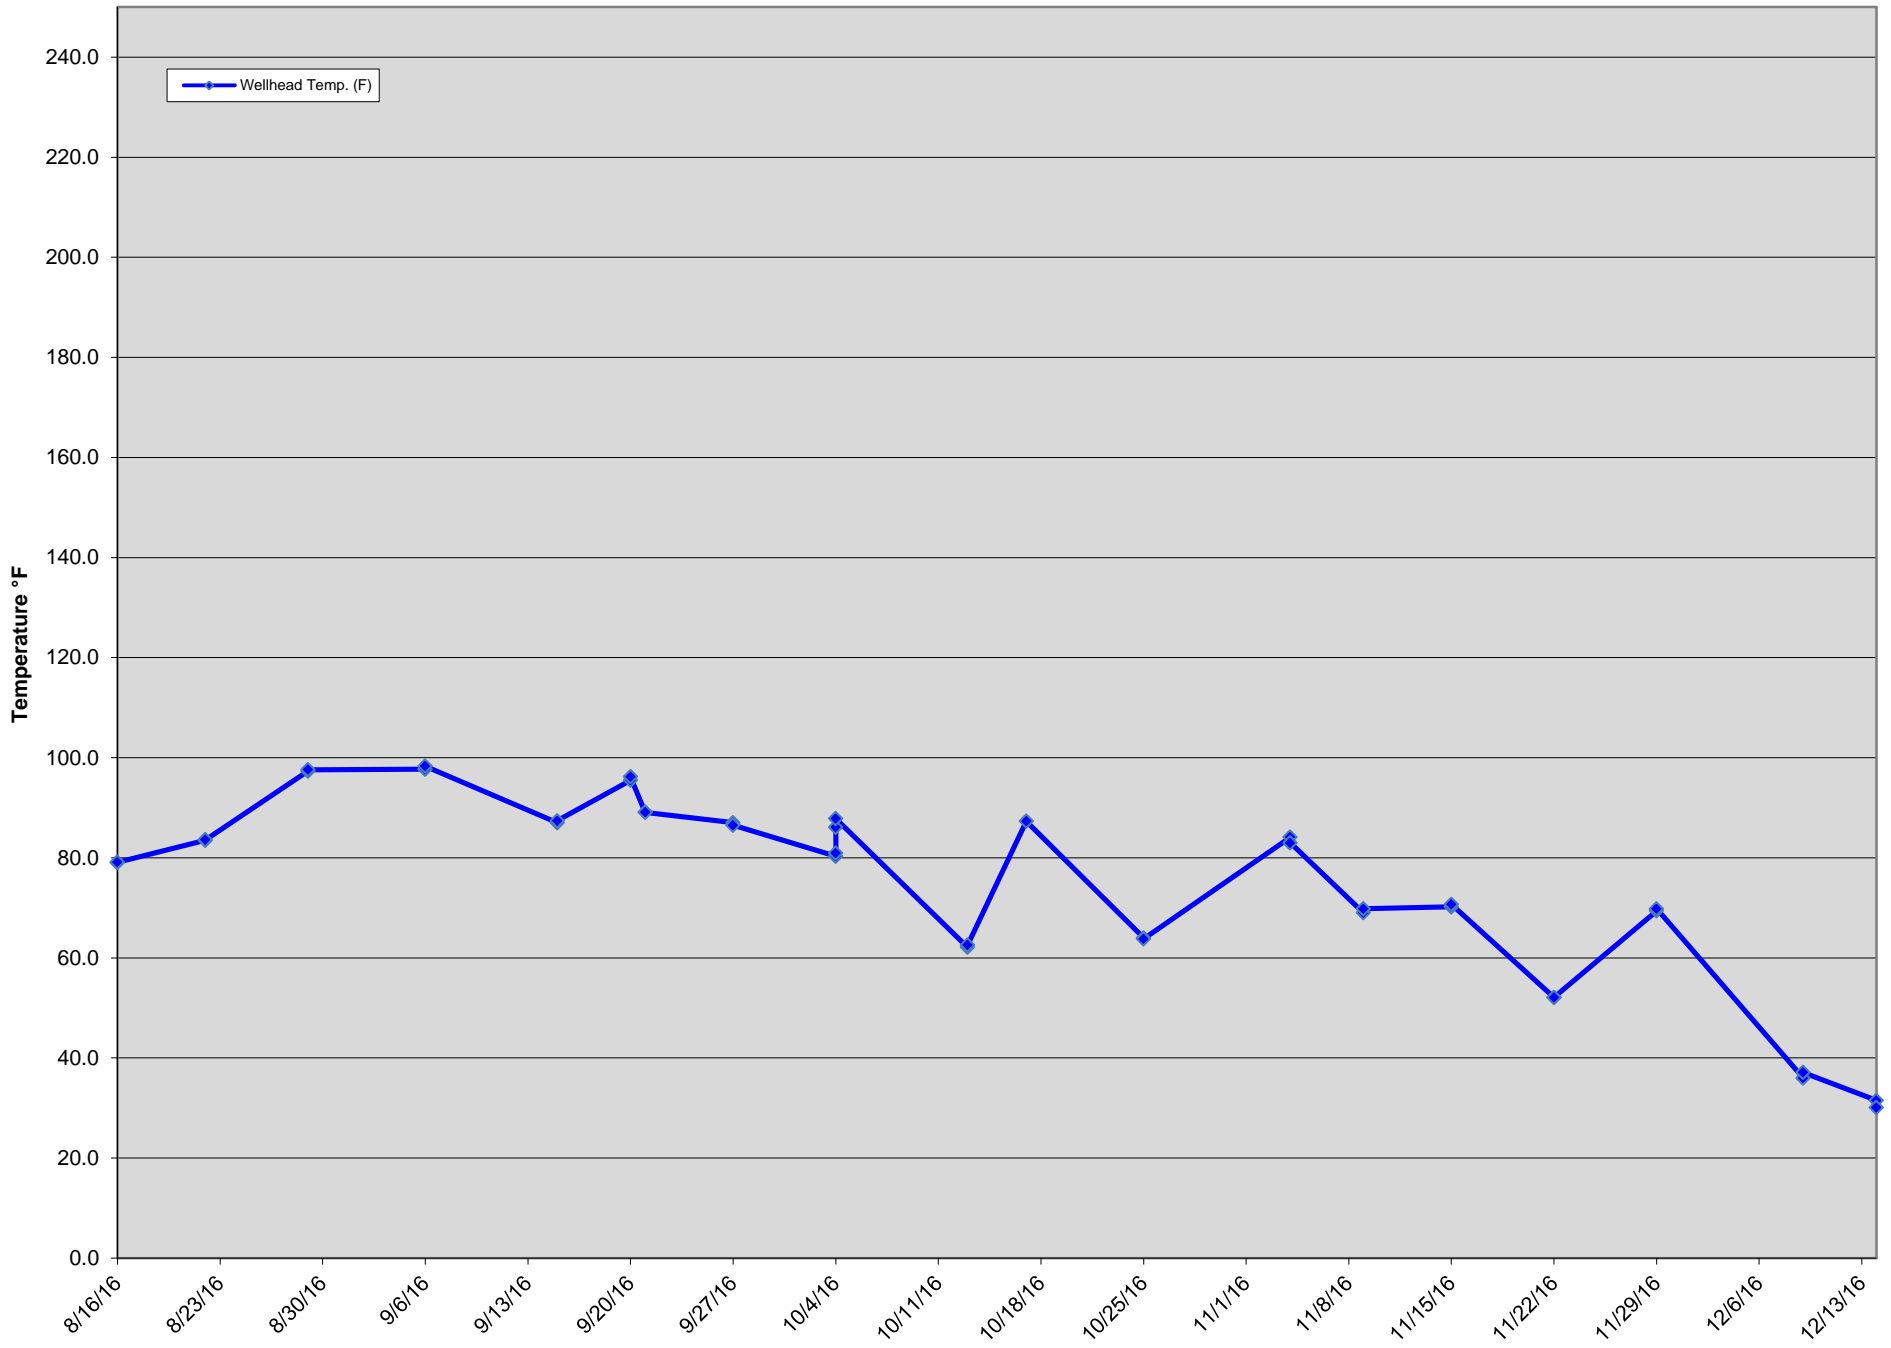

GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-13	08/16/16	10.9	64.5	0.2	24.4	78.6	-2.8	N/A	(HES Installed)
GIW-13	08/22/16	13.5	57.2	0.2	29.1	88.6	-2.5	N/A	(HES Installed)
GIW-13	08/29/16	14.7	59.3	0.5	25.5	99.6	-2.8	N/A	(HES Installed)
GIW-13	09/06/16	17.1	63.4	0.5	19.0	98.1	-2.9	N/A	(HES Installed)
GIW-13	09/06/16	15.8	60.4	0.6	23.2	99.5	-2.9	N/A	(HES Installed)
GIW-13	09/15/16	15.2	65.0	0.3	19.5	91.3	-2.9	N/A	(HES Installed)
GIW-13	09/20/16	12.2	60.2	0.3	27.3	98.7	-2.7	N/A	(HES Installed)
GIW-13	09/21/16	13.3	59.8	0.3	26.6	91.8	-2.6	N/A	(HES Installed)
GIW-13	09/27/16	16.1	56.2	0.2	27.5	84.0	-2.5	N/A	(HES Installed)
GIW-13	10/04/16	13.8	59.8	0.1	26.3	77.5	-2.4	N/A	(HES Installed)
GIW-13	10/04/16	13.4	56.4	0.2	30.0	79.2	-0.5	N/A	(HES Installed)
GIW-13	10/13/16	10.2	47.5	0.0	42.3	61.3	-0.9	N/A	(HES Installed)
GIW-13	10/17/16	10.8	58.7	0.0	30.5	87.6	-0.6	N/A	(HES Installed)
GIW-13	10/25/16	9.8	59.2	0.0	31.0	64.3	-0.6	N/A	(HES Installed)
GIW-13	11/04/16	9.8	44.9	4.3	41.0	78.7	-15.3	N/A	(HES Installed)
GIW-13	11/04/16	12.4	53.0	2.1	32.5	80.0	-5.6	N/A	(HES Installed)
GIW-13	11/09/16	12.1	58.6	0.0	29.3	71.3	-2.3	N/A	(HES Installed)
GIW-13	11/09/16	10.4	58.3	0.0	31.3	72.0	-2.1	N/A	(HES Installed)
GIW-13	11/15/16	11.8	61.8	0.0	26.4	73.0	-1.8	N/A	(HES Installed)
GIW-13	11/22/16	12.1	62.9	0.0	25.0	51.5	-1.8	N/A	(HES Installed)
GIW-13	11/29/16	11.6	53.7	0.0	34.7	70.9	-1.9	N/A	(HES Installed)
GIW-13	12/09/16	13.7	59.4	0.0	26.9	34.3	-2.2	N/A	(HES Installed)
GIW-13	12/09/16	11.9	60.5	0.0	27.6	35.9	-2.1	N/A	(HES Installed)
GIW-13	12/14/16	13.1	59.9	0.0	27.0	30.1	-2.0	N/A	(HES Installed)

GIW-13 Wellhead Temperatures

