



GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (°F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-01	02/14/17	5.0	60.9	0.1	34.0	178.0	-3.4	Y	
GIW-01	02/14/17	3.7	63.5	0.1	32.7	178.6	-3.4	Y	
GIW-01	02/21/17	22.5	39.1	2.7	35.7	75.0	-17.3	Y	
GIW-01	02/28/17	18.8	50.7	1.4	29.1	85.6	-17.9	Y	
GIW-01	03/07/17	14.1	56.4	2.4	27.1	62.6	-17.7	Y	
GIW-01	03/07/17	13.9	56.3	2.1	27.7	63.3	-17.5	Y	
GIW-01	03/16/17	18.2	48.0	1.6	32.2	65.6	-18.1	Y	
GIW-01	03/21/17	15.6	34.2	5.1	45.1	61.5	-19.1	Y	
GIW-01	03/21/17	15.0	35.7	5.0	44.3	61.8	-19.2	Y	
GIW-01	03/27/17	17.2	60.1	0.6	22.1	69.1	-18.9	Y	
GIW-01	04/05/17	19.4	61.3	0.0	19.3	73.0	-17.9	Y	
GIW-01	04/10/17	18.7	38.4	5.4	37.5	79.1	-19.0	Y	
GIW-01	04/10/17	18.1	38.9	5.7	37.3	79.8	-19.2	Y	
GIW-01	04/18/17	15.3	62.3	0.0	22.4	76.5	-17.9	Y	
GIW-01	04/24/17	14.0	62.9	0.0	23.1	96.5	-17.9	Y	
GIW-01	05/01/17	6.8	27.0	9.7	56.5	63.8	-18.6	Y	
GIW-01	05/01/17	6.5	27.8	9.9	55.8	61.5	-19.2	Y	
GIW-01	05/11/17	7.5	41.1	6.9	44.5	82.1	-19.0	Y	
GIW-01	05/11/17	9.7	34.6	7.3	48.4	82.3	-19.0	Y	
GIW-01	05/15/17	7.4	36.6	3.2	52.8	98.4	-17.6	Y	
GIW-01	05/23/17	9.3	43.6	1.9	45.2	88.3	-18.1	Y	
GIW-01	05/30/17	6.6	42.4	4.3	46.7	102.1	-18.7	Y	
GIW-01	06/05/17	14.5	52.3	2.1	31.1	109.9	-18.2	Y	
GIW-01	06/05/17	14.6	50.6	2.2	32.6	111.0	-17.5	Y	
GIW-01	06/12/17	20.2	46.8	1.0	32.0	104.8	-17.5	Y	

GIW-1 Wellhead Temperatures

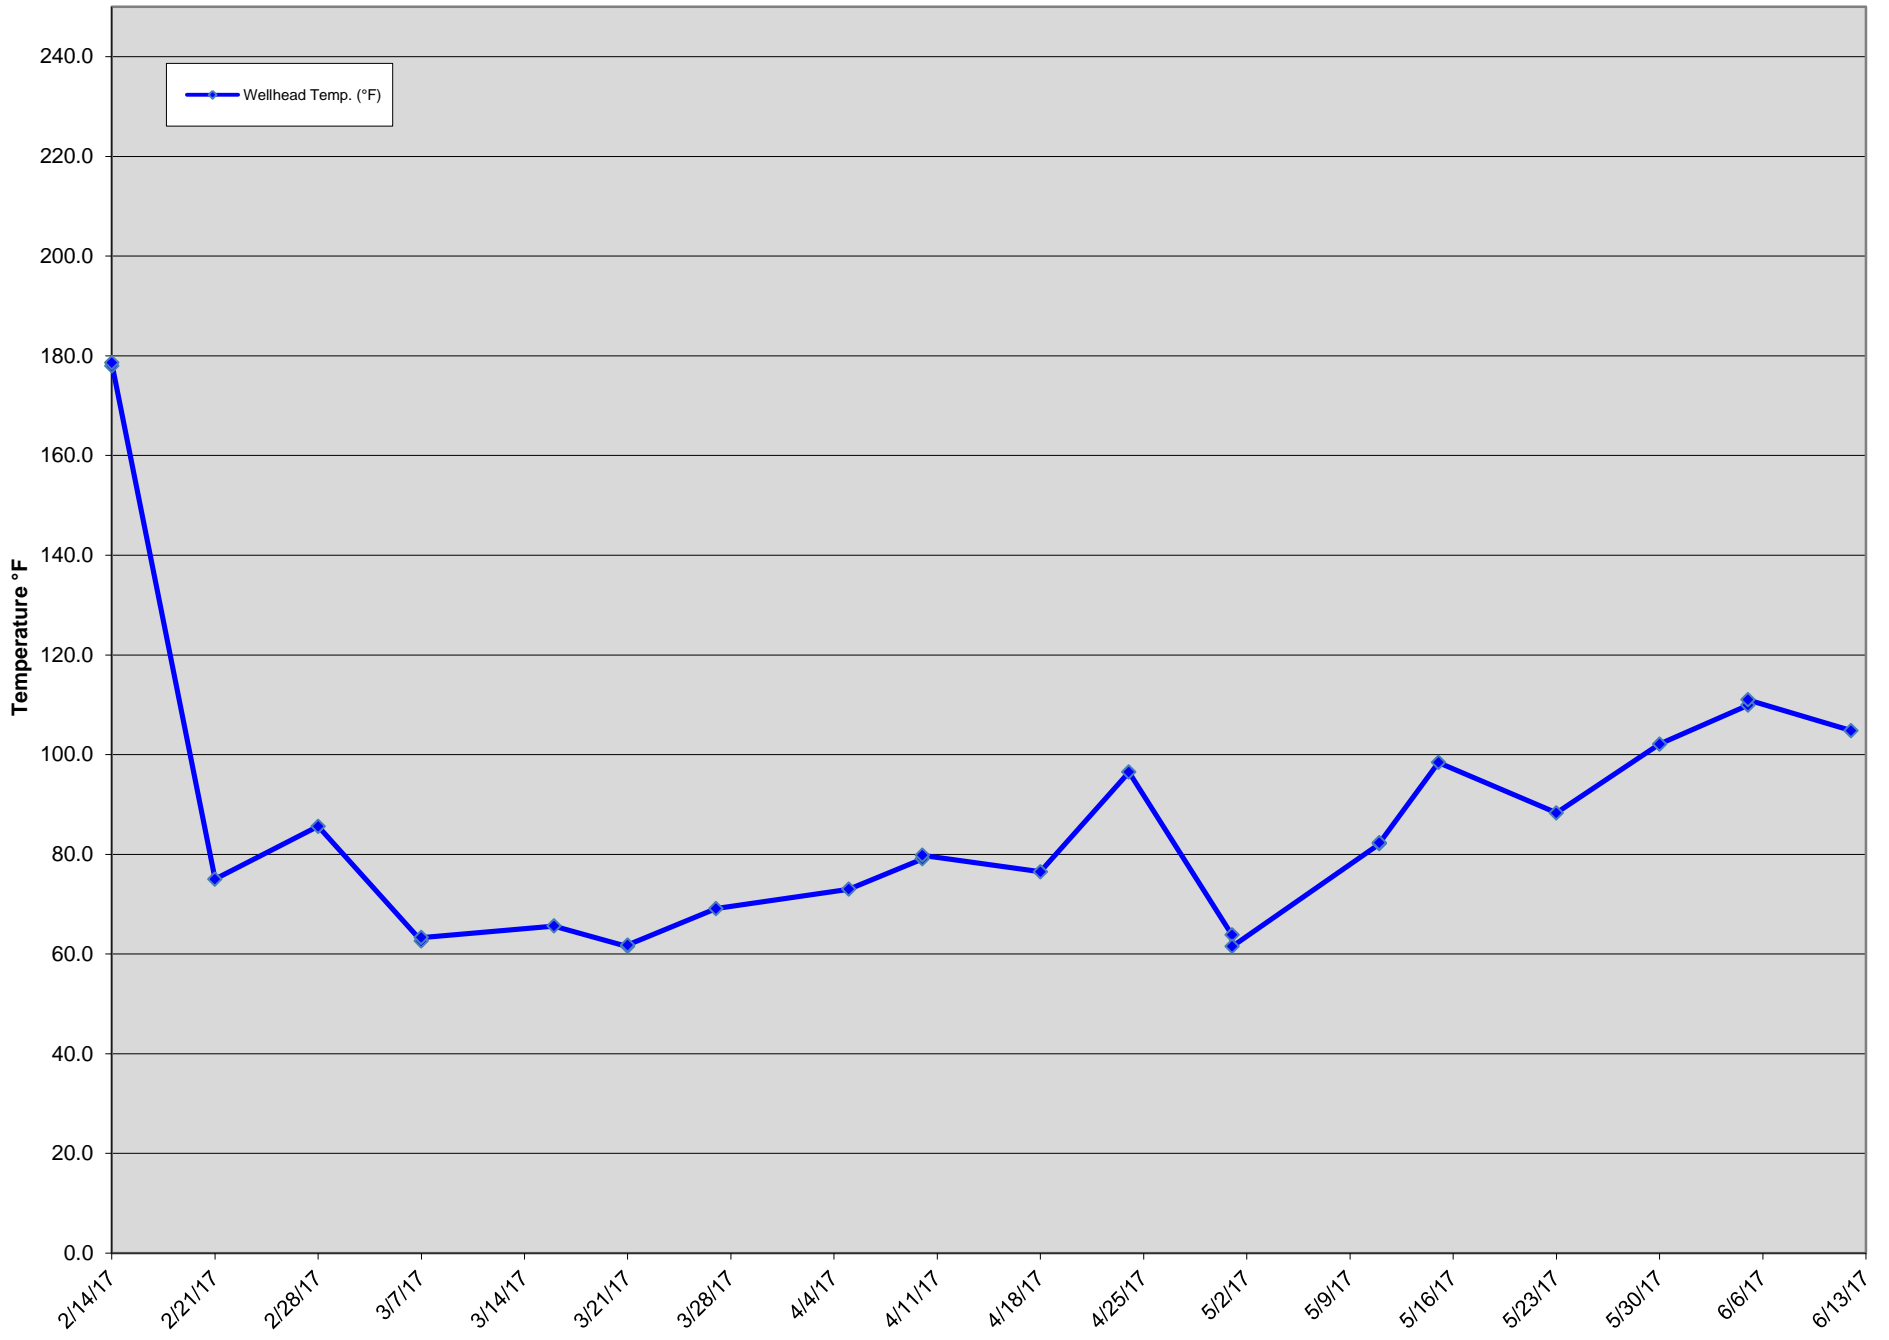


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-02	02/14/17	7.6	45.2	5.5	41.7	60.5	-0.1	N/A	(HES Installed)
GIW-02	02/14/17	8.2	41.6	5.8	44.4	59.9	-0.2	N/A	(HES Installed)
GIW-02	02/21/17	8.0	40.2	6.2	45.6	62.8	-0.2	N/A	(HES Installed)
GIW-02	02/21/17	6.9	41.7	6.2	45.2	62.9	-0.1	N/A	(HES Installed)
GIW-02	02/28/17	8.3	42.8	5.4	43.5	78.5	-0.1	N/A	(HES Installed)
GIW-02	02/28/17	8.2	42.4	5.3	44.1	78.9	-0.1	N/A	(HES Installed)
GIW-02	03/07/17	5.0	35.3	9.6	50.1	58.0	-0.3	N/A	(HES Installed)
GIW-02	03/07/17	5.3	32.3	9.6	52.8	58.5	-0.2	N/A	(HES Installed)
GIW-02	03/16/17	10.6	45.0	3.2	41.2	56.9	-0.2	N/A	(HES Installed)
GIW-02	03/21/17	4.2	28.7	10.5	56.6	51.3	-0.3	N/A	(HES Installed)
GIW-02	03/21/17	4.0	28.5	10.5	57.0	51.4	-0.3	N/A	(HES Installed)
GIW-02	03/27/17	4.5	35.6	6.7	53.2	58.0	-0.3	N/A	(HES Installed)
GIW-02	03/27/17	4.6	33.2	6.8	55.4	58.0	-0.3	N/A	(HES Installed)
GIW-02	04/05/17	9.9	45.8	4.2	40.1	62.8	-0.3	N/A	(HES Installed)
GIW-02	04/10/17	3.5	21.6	13.9	61.0	67.9	-0.4	N/A	(HES Installed)
GIW-02	04/10/17	3.6	18.3	14.1	64.0	67.8	-0.4	N/A	(HES Installed)
GIW-02	04/18/17	5.3	38.7	8.3	47.7	75.2	-0.1	N/A	(HES Installed)
GIW-02	04/18/17	5.2	37.2	8.4	49.2	75.2	-0.1	N/A	(HES Installed)
GIW-02	04/24/17	10.0	50.4	0.4	39.2	87.0	-0.2	N/A	(HES Installed)
GIW-02	05/01/17	6.9	32.2	10.3	50.6	59.8	-0.3	N/A	(HES Installed)
GIW-02	05/01/17	6.6	32.7	10.3	50.4	60.1	-0.2	N/A	(HES Installed)
GIW-02	05/11/17	8.1	31.3	9.5	51.1	71.6	-0.3	N/A	(HES Installed)
GIW-02	05/11/17	7.2	35.3	9.5	48.0	71.8	-0.3	N/A	(HES Installed)
GIW-02	05/15/17	8.7	35.8	7.9	47.6	96.0	-0.3	N/A	(HES Installed)
GIW-02	05/15/17	8.7	36.8	7.9	46.6	96.3	-0.3	N/A	(HES Installed)
GIW-02	05/23/17	7.2	37.3	8.1	47.4	74.8	-0.3	N/A	(HES Installed)
GIW-02	05/23/17	7.1	37.2	8.2	47.5	75.2	-0.3	N/A	(HES Installed)
GIW-02	05/30/17	7.1	36.9	8.2	47.8	89.6	-0.3	N/A	(HES Installed)
GIW-02	05/30/17	7.3	36.5	8.1	48.1	90.5	-0.3	N/A	(HES Installed)
GIW-02	06/05/17	7.0	38.2	7.2	47.6	101.8	-0.3	N/A	(HES Installed)
GIW-02	06/05/17	7.0	37.1	7.4	48.5	101.8	-0.3	N/A	(HES Installed)
GIW-02	06/12/17	6.4	37.0	8.6	48.0	101.8	-0.36	N/A	(HES Installed)
GIW-02	06/12/17	6.0	35.9	8.7	49.4	101.8	-0.34	N/A	(HES Installed)

GIW-2 Wellhead Temperatures

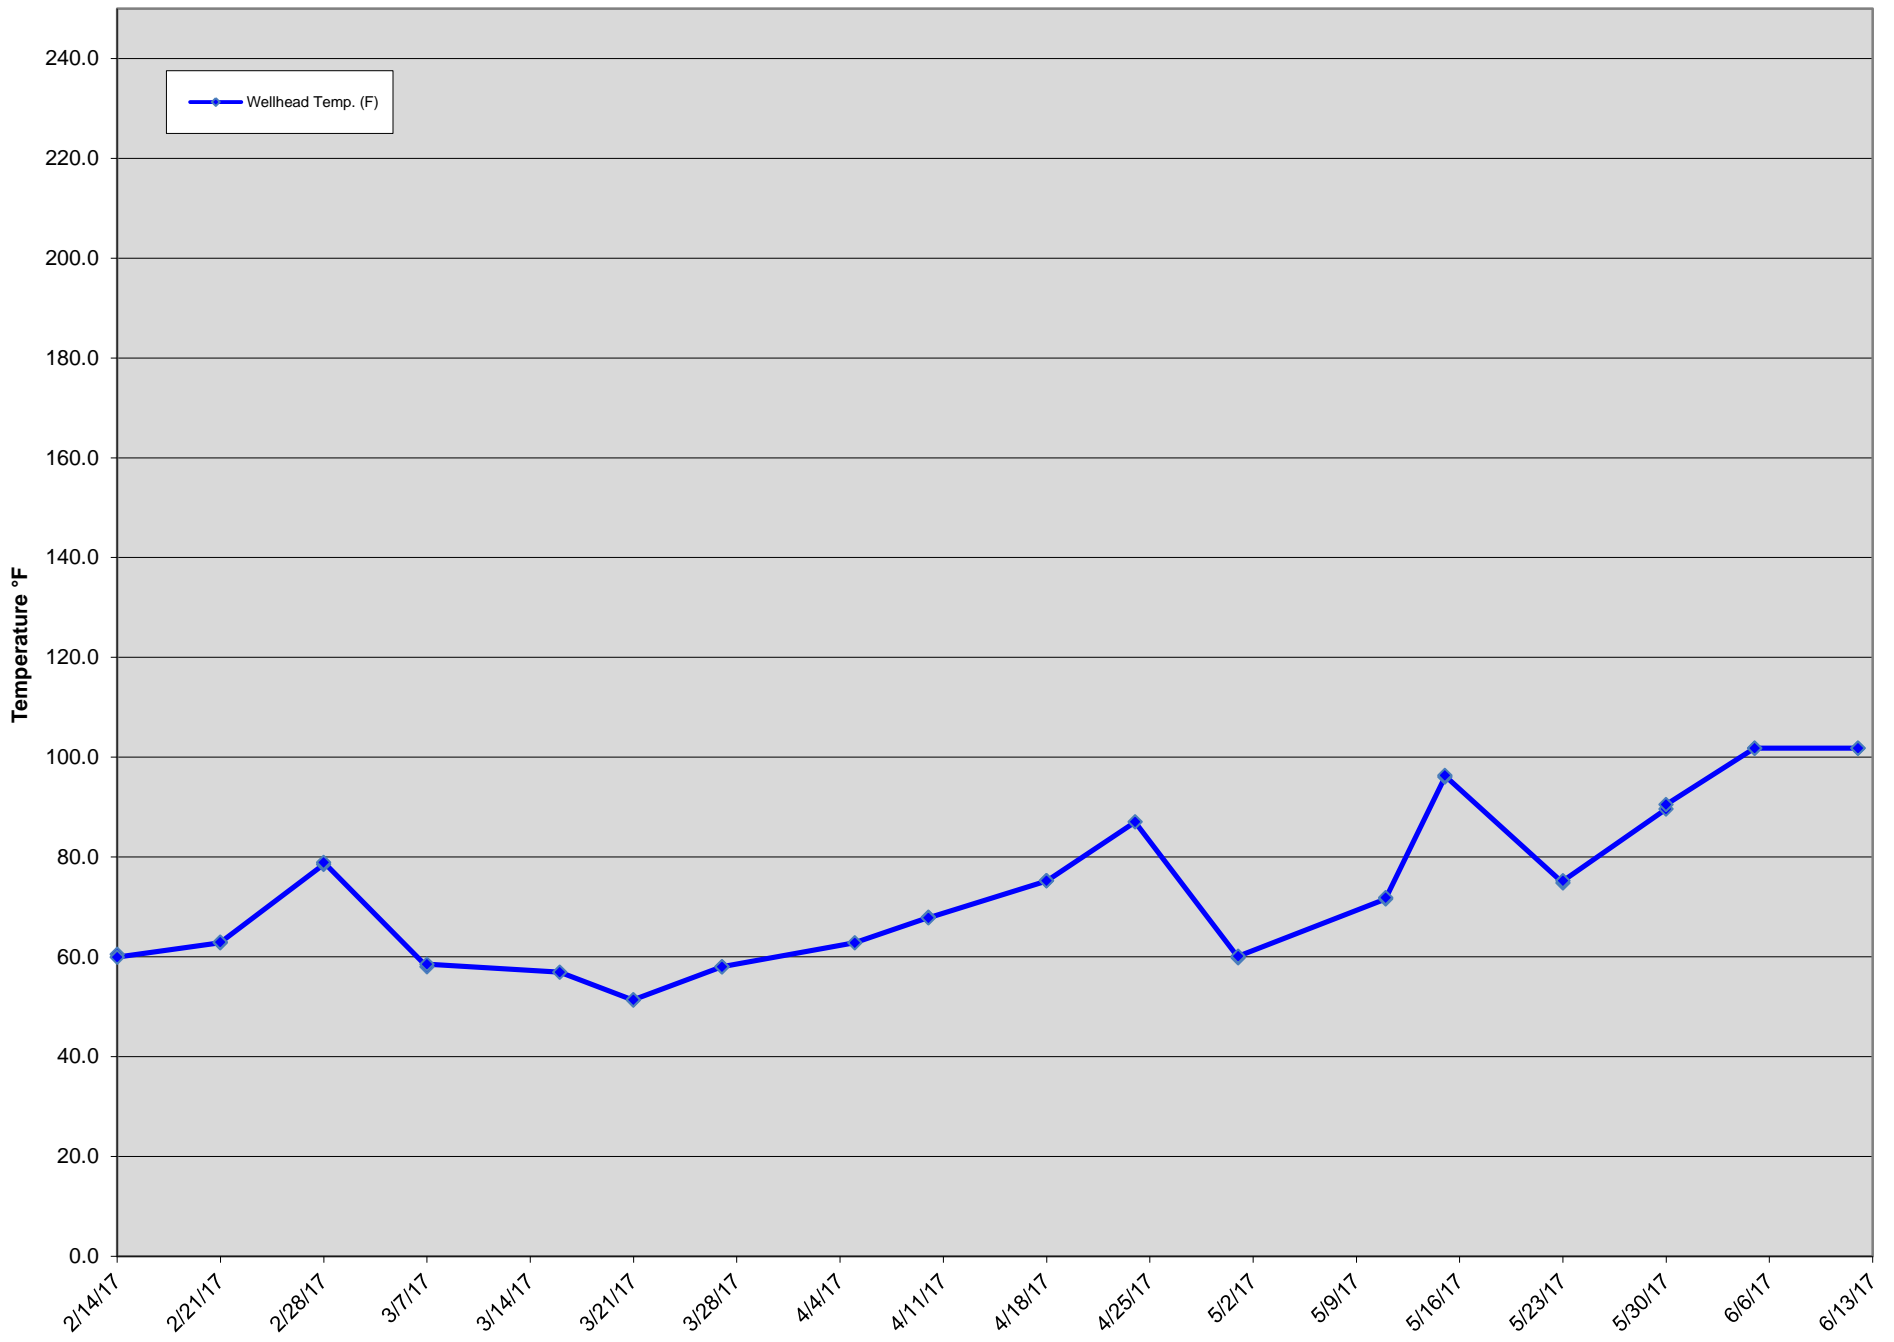


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-03	02/14/17	2.2	64.1	0.0	33.7	74.1	0.6	N/A	(HES Installed)
GIW-03	02/14/17	2.3	61.2	0.0	36.5	75.9	-0.2	N/A	(HES Installed)
GIW-03	02/21/17	2.7	53.7	1.9	41.7	65.5	-0.6	N/A	(HES Installed)
GIW-03	02/28/17	2.1	49.7	4.0	44.2	76.8	-3.4	N/A	(HES Installed)
GIW-03	03/07/17	1.4	56.5	0.4	41.7	54.8	-0.2	N/A	(HES Installed)
GIW-03	03/07/17	1.2	61.1	0.5	37.2	56.3	-0.1	N/A	(HES Installed)
GIW-03	03/16/17	1.8	46.1	4.6	47.5	55.7	-4.9	N/A	(HES Installed)
GIW-03	03/16/17	1.8	49.7	4.0	44.5	57.8	-1.1	N/A	(HES Installed)
GIW-03	03/21/17	1.1	43.9	6.1	48.9	49.4	-6.9	N/A	(HES Installed)
GIW-03	03/21/17	1.0	46.7	5.8	46.5	49.6	-6.9	N/A	(HES Installed)
GIW-03	03/27/17	2.0	41.9	6.3	49.8	58.5	-13.2	N/A	(HES Installed)
GIW-03	03/27/17	2.3	43.2	6.3	48.2	58.5	-13.1	N/A	(HES Installed)
GIW-03	04/05/17	2.0	46.3	4.9	46.8	60.0	-5.6	N/A	(HES Installed)
GIW-03	04/10/17	1.0	51.0	3.9	44.1	79.6	-3.7	N/A	(HES Installed)
GIW-03	04/10/17	0.7	49.6	3.8	45.9	78.8	-3.7	N/A	(HES Installed)
GIW-03	04/18/17	1.4	49.1	3.6	45.9	70.9	-3.4	N/A	(HES Installed)
GIW-03	04/24/17	1.6	52.2	2.4	43.8	90.7	-2.8	N/A	(HES Installed)
GIW-03	05/01/17	1.0	56.0	2.1	40.9	59.3	-1.6	N/A	(HES Installed)
GIW-03	05/01/17	0.8	52.6	2.5	44.1	57.0	-1.6	N/A	(HES Installed)
GIW-03	05/11/17	1.0	49.1	3.1	46.8	71.8	-3.0	N/A	(HES Installed)
GIW-03	05/15/17	1.2	50.4	2.5	45.9	92.4	-2.3	N/A	(HES Installed)
GIW-03	05/23/17	0.9	47.8	5.1	46.2	75.9	-3.1	N/A	(HES Installed)
GIW-03	05/23/17	0.8	48.9	5.2	45.1	76.2	-3.5	N/A	(HES Installed)
GIW-03	05/30/17	0.8	49.2	4.7	45.3	92.6	-4.4	N/A	(HES Installed)
GIW-03	06/05/17	1.1	48.4	4.4	46.1	112.4	-4.1	N/A	(HES Installed)
GIW-03	06/05/17	1.3	48.9	4.2	45.6	111.8	-4.3	N/A	(HES Installed)
GIW-03	06/12/17	0.8	53.7	2.1	43.4	97.4	-4.5	N/A	(HES Installed)

GIW-3 Wellhead Temperatures

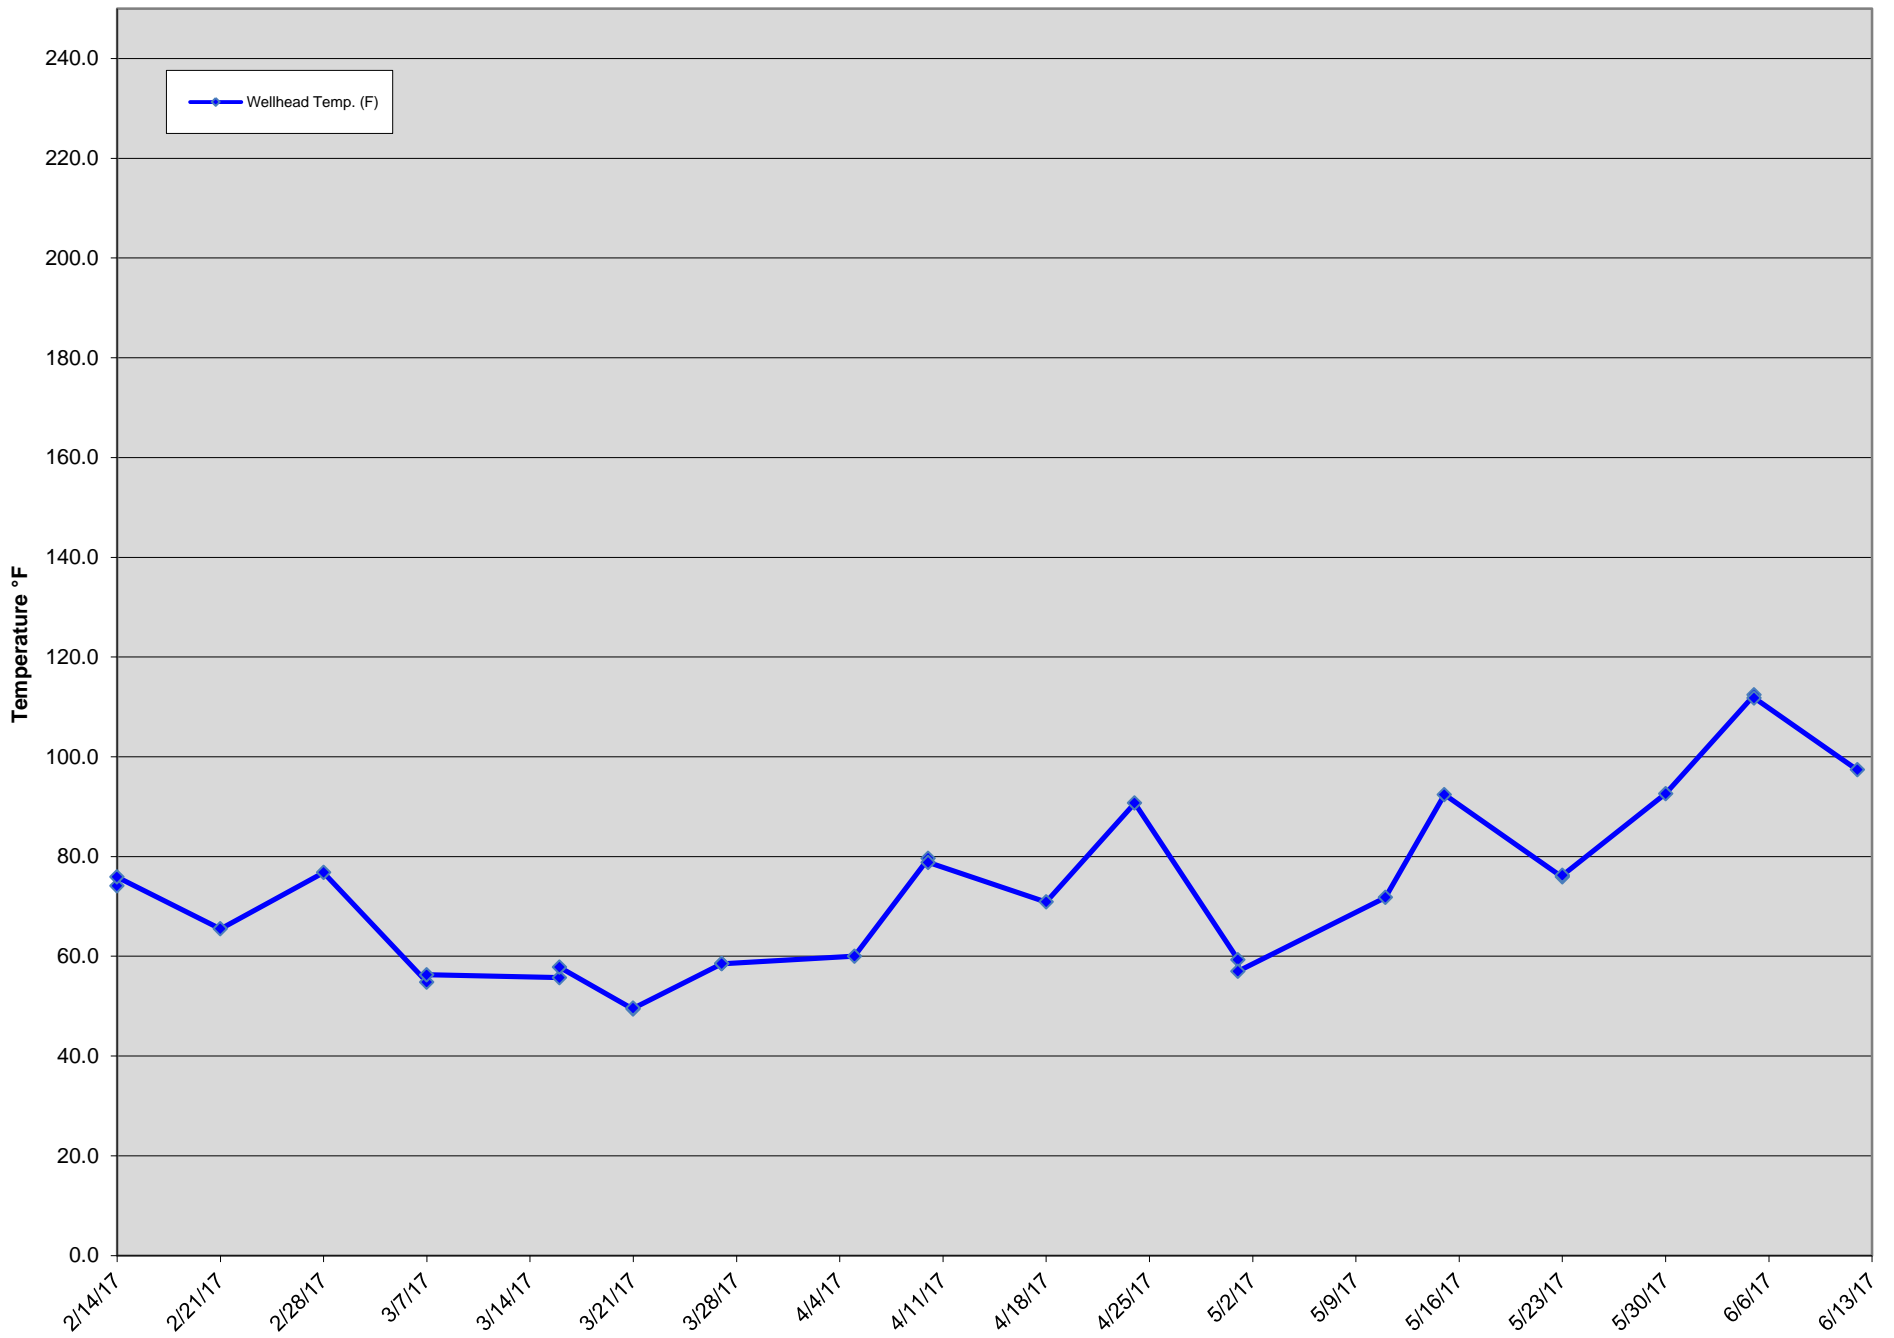


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-04	02/14/17	0.5	45.0	5.7	48.8	55.7	-7.2	N/A	(HES Installed)
GIW-04	02/14/17	0.6	41.8	5.9	51.7	59.3	-7.3	N/A	(HES Installed)
GIW-04	02/21/17	0.6	51.4	1.3	46.7	64.2	-4.3	N/A	(HES Installed)
GIW-04	02/28/17	0.1	9.7	18.7	71.5	75.0	-7.0	N/A	(HES Installed)
GIW-04	02/28/17	0.1	6.3	19.2	74.4	76.1	-7.0	N/A	(HES Installed)
GIW-04	03/07/17	0.1	15.2	17.7	67.0	57.8	-7.8	N/A	(HES Installed)
GIW-04	03/07/17	0.1	9.9	18.6	71.4	54.7	-7.9	N/A	(HES Installed)
GIW-04	03/16/17	0.1	10.9	17.6	71.4	58.7	-9.7	N/A	(HES Installed)
GIW-04	03/16/17	0.1	8.0	18.0	73.9	59.2	-9.7	N/A	(HES Installed)
GIW-04	03/21/17	0.2	15.9	17.2	66.7	53.1	-9.6	N/A	(HES Installed)
GIW-04	03/21/17	0.2	11.2	17.9	70.7	53.7	-9.8	N/A	(HES Installed)
GIW-04	03/27/17	0.4	25.6	13.2	60.8	59.0	-18.1	N/A	(HES Installed)
GIW-04	03/27/17	0.5	23.4	12.8	63.3	59.3	-18.1	N/A	(HES Installed)
GIW-04	04/05/17	0.5	38.2	7.7	53.6	63.9	-7.6	N/A	(HES Installed)
GIW-04	04/05/17	0.6	40.9	6.1	52.4	65.8	-7.6	N/A	(HES Installed)
GIW-04	04/10/17	0.3	26.3	12.5	60.9	77.1	-4.9	N/A	(HES Installed)
GIW-04	04/10/17	0.2	24.4	12.3	63.1	76.9	-5.0	N/A	(HES Installed)
GIW-04	04/18/17	0.3	24.9	12.4	62.4	76.9	-5.0	N/A	(HES Installed)
GIW-04	04/18/17	0.3	25.8	11.9	62.0	78.4	-5.0	N/A	(HES Installed)
GIW-04	04/24/17	0.6	29.7	10.3	59.4	82.6	-3.2	N/A	(HES Installed)
GIW-04	04/24/17	0.6	27.7	10.0	61.7	83.0	-3.0	N/A	(HES Installed)
GIW-04	05/02/17	0.5	25.5	10.8	63.2	73.9	-2.2	N/A	(HES Installed)
GIW-04	05/02/17	0.6	27.3	10.5	61.6	77.4	-2.1	N/A	(HES Installed)
GIW-04	05/11/17	0.9	45.5	4.6	49.0	71.0	-3.5	N/A	(HES Installed)
GIW-04	05/15/17	0.6	25.6	11.2	62.6	96.5	-2.7	N/A	(HES Installed)
GIW-04	05/16/17	0.5	24.3	11.1	64.1	89.8	-2.8	N/A	(HES Installed)
GIW-04	05/23/17	0.4	25.7	12.8	61.1	75.0	-3.7	N/A	(HES Installed)
GIW-04	05/23/17	0.4	24.1	12.7	62.8	76.0	-3.6	N/A	(HES Installed)
GIW-04	05/30/17	0.4	21.7	13.4	64.5	85.2	-4.3	N/A	(HES Installed)
GIW-04	05/30/17	0.4	20.3	13.4	65.9	86.8	-4.3	N/A	(HES Installed)
GIW-04	06/05/17	0.8	32.5	9.5	57.2	103.3	-4.4	N/A	(HES Installed)
GIW-04	06/05/17	0.9	32.5	9.3	57.3	103.0	-4.2	N/A	(HES Installed)
GIW-04	06/12/17	0.3	27.4	12.5	59.8	99.1	-4.7	N/A	(HES Installed)
GIW-04	06/12/17	0.3	28.2	12.3	59.2	99.9	-4.7	N/A	(HES Installed)

GIW-4 Wellhead Temperatures

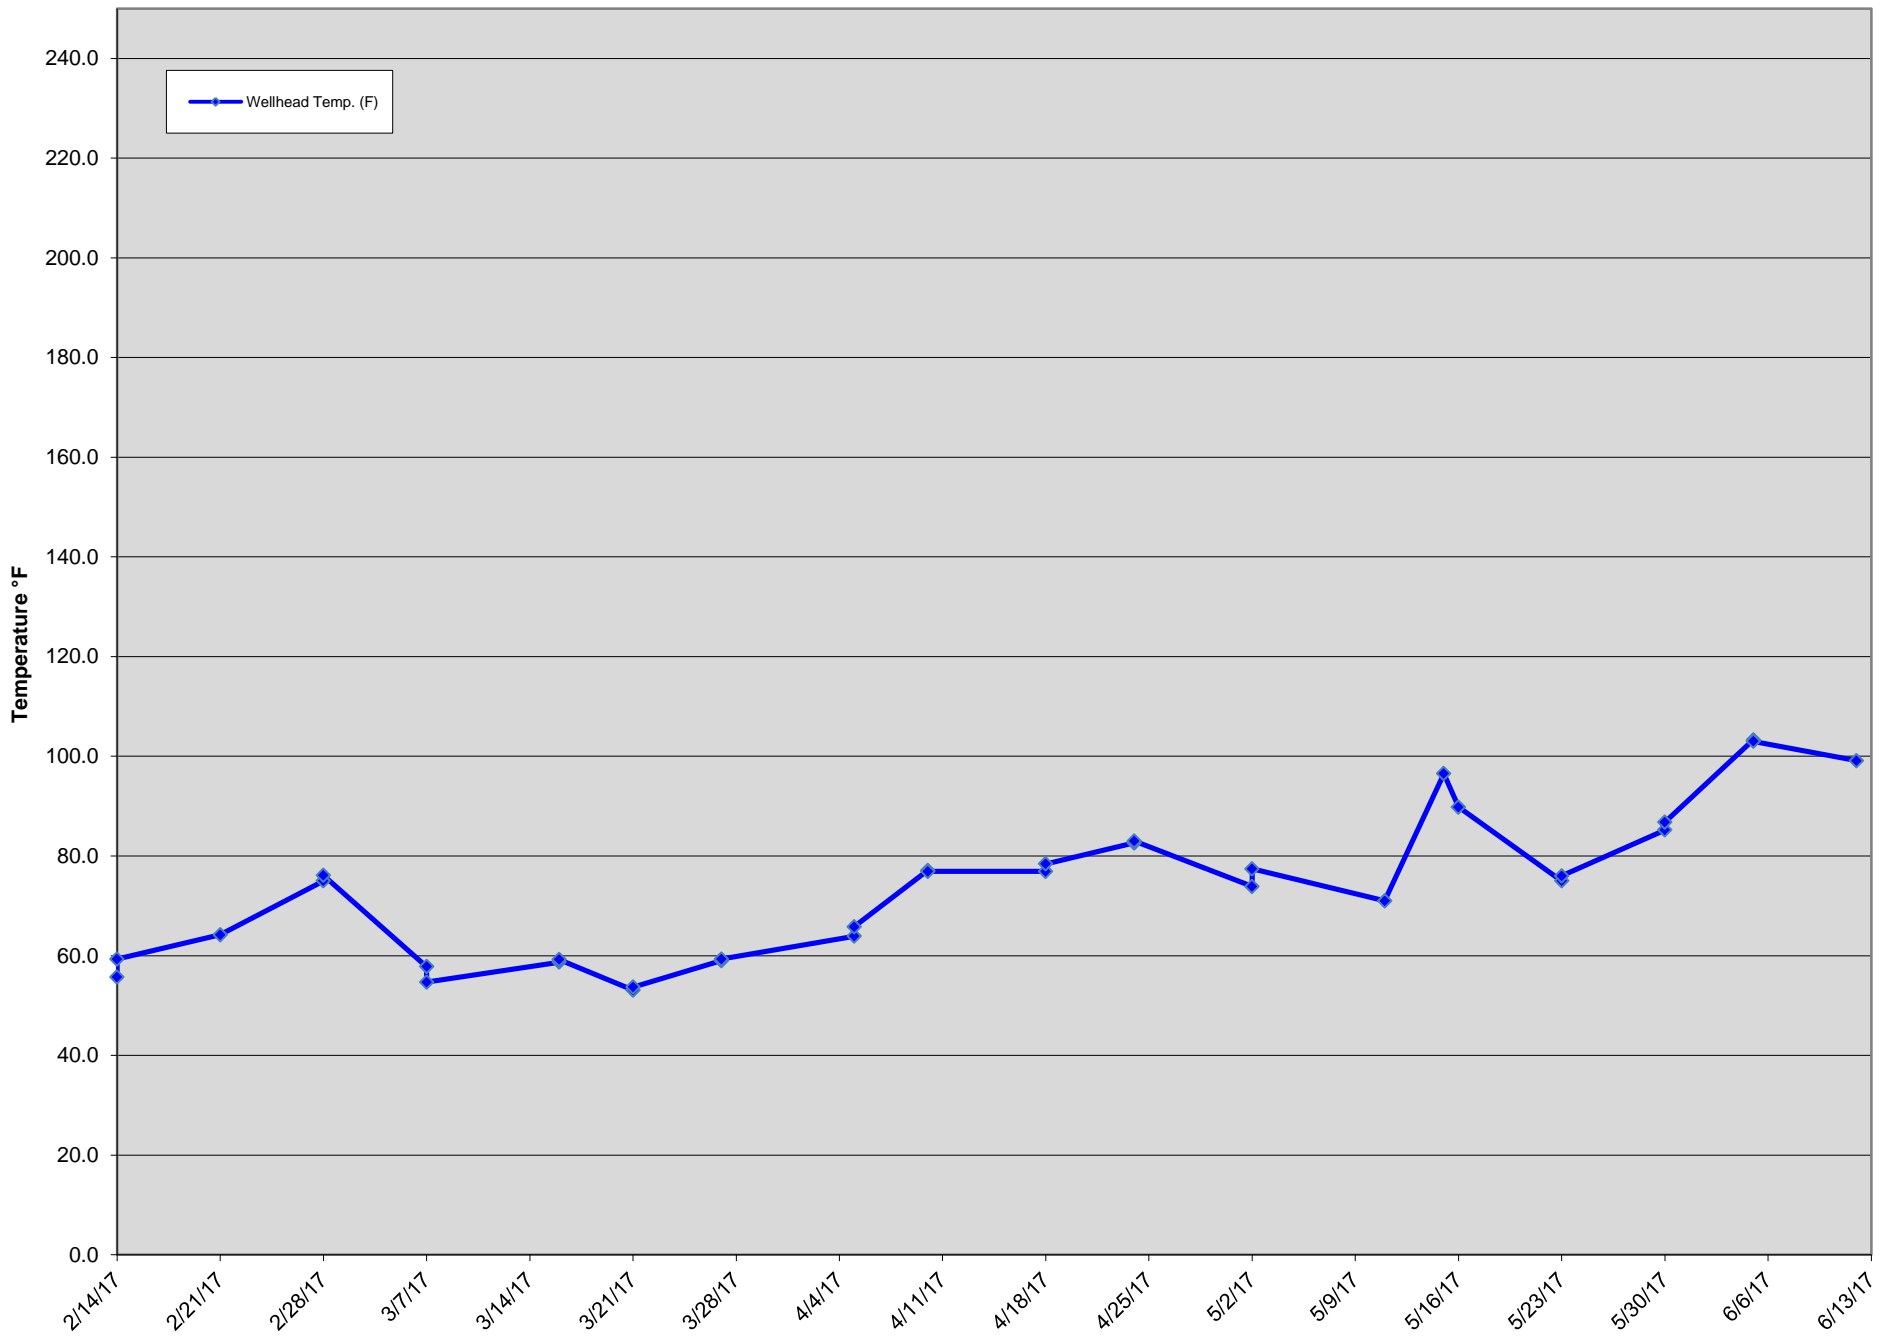


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-05	02/14/17	0.0	7.6	20.2	72.2	58.7	-0.3	N/A	(HES Installed)
GIW-05	02/14/17	0.0	1.8	21.4	76.8	60.5	-0.4	N/A	(HES Installed)
GIW-05	02/21/17	0.3	19.8	19.7	60.2	65.3	-0.7	N/A	(HES Installed)
GIW-05	02/21/17	0.0	6.2	21.0	72.8	65.1	-0.7	N/A	(HES Installed)
GIW-05	02/28/17	0.0	2.9	20.7	76.4	75.5	-0.1	N/A	(HES Installed)
GIW-05	02/28/17	0.0	0.8	21.1	78.1	75.0	-0.2	N/A	(HES Installed)
GIW-05	03/07/17	0.1	8.6	20.1	71.2	57.1	-0.3	N/A	(HES Installed)
GIW-05	03/07/17	0.0	3.1	21.1	75.8	57.8	-0.3	N/A	(HES Installed)
GIW-05	03/16/17	0.0	3.0	20.2	76.8	53.9	-13.7	N/A	(HES Installed)
GIW-05	03/16/17	0.0	1.6	20.5	77.9	54.1	-20.1	N/A	(HES Installed)
GIW-05	03/21/17	0.1	13.3	18.8	67.8	54.4	-8.5	N/A	(HES Installed)
GIW-05	03/21/17	0.0	10.5	19.3	70.2	54.7	-16.7	N/A	(HES Installed)
GIW-05	03/27/17	0.1	12.5	19.1	68.3	58.3	-8.8	N/A	(HES Installed)
GIW-05	03/27/17	0.0	7.7	20.0	72.3	58.5	-16.2	N/A	(HES Installed)
GIW-05	04/05/17	0.0	12.1	19.4	68.5	62.1	0.0	N/A	(HES Installed)
GIW-05	04/05/17	0.0	5.7	20.7	73.6	61.2	-0.1	N/A	(HES Installed)
GIW-05	04/10/17	0.0	8.4	20.4	71.2	76.8	-4.2	N/A	(HES Installed)
GIW-05	04/10/17	0.0	1.8	21.5	76.7	76.8	-4.3	N/A	(HES Installed)
GIW-05	04/18/17	0.0	5.1	21.0	73.9	76.9	-5.0	N/A	(HES Installed)
GIW-05	04/18/17	0.0	2.1	21.5	76.4	76.1	-5.6	N/A	(HES Installed)
GIW-05	04/24/17	0.0	5.7	20.0	74.3	84.9	-7.8	N/A	(HES Installed)
GIW-05	04/24/17	0.0	3.3	20.4	76.3	84.5	-11.8	N/A	(HES Installed)
GIW-05	05/02/17	0.0	7.8	19.6	72.6	62.6	-5.8	N/A	(HES Installed)
GIW-05	05/02/17	0.0	2.2	21.0	76.8	64.3	-4.3	N/A	(HES Installed)
GIW-05	05/11/17	0.0	5.7	20.8	73.5	70.9	-4.8	N/A	(HES Installed)
GIW-05	05/11/17	0.0	2.9	21.4	75.7	70.9	-5.4	N/A	(HES Installed)
GIW-05	05/15/17	0.1	2.6	20.5	76.8	89.6	-7.9	N/A	(HES Installed)
GIW-05	05/15/17	0.1	1.6	20.6	77.7	91.5	-10.2	N/A	(HES Installed)
GIW-05	05/23/17	0.0	4.1	20.8	75.1	73.0	-4.4	N/A	(HES Installed)
GIW-05	05/23/17	0.0	2.0	21.3	76.7	73.6	-3.7	N/A	(HES Installed)
GIW-05	05/30/17	0.0	3.0	20.5	76.5	83.1	-0.1	N/A	(HES Installed)
GIW-05	05/30/17	0.0	1.6	20.8	77.6	83.6	-0.1	N/A	(HES Installed)
GIW-05	06/05/17	0.2	5.5	20.2	74.1	101.3	-4.2	N/A	(HES Installed)
GIW-05	06/05/17	1.2	22.6	11.9	64.3	101.1	-4.3	N/A	(HES Installed)
GIW-05	06/12/17	0.2	13.9	17.9	68.0	95.3	-0.6	N/A	(HES Installed)
GIW-05	06/12/17	0.7	23.0	14.1	62.2	96.7	-0.2	N/A	(HES Installed)

GIW-5 Wellhead Temperatures

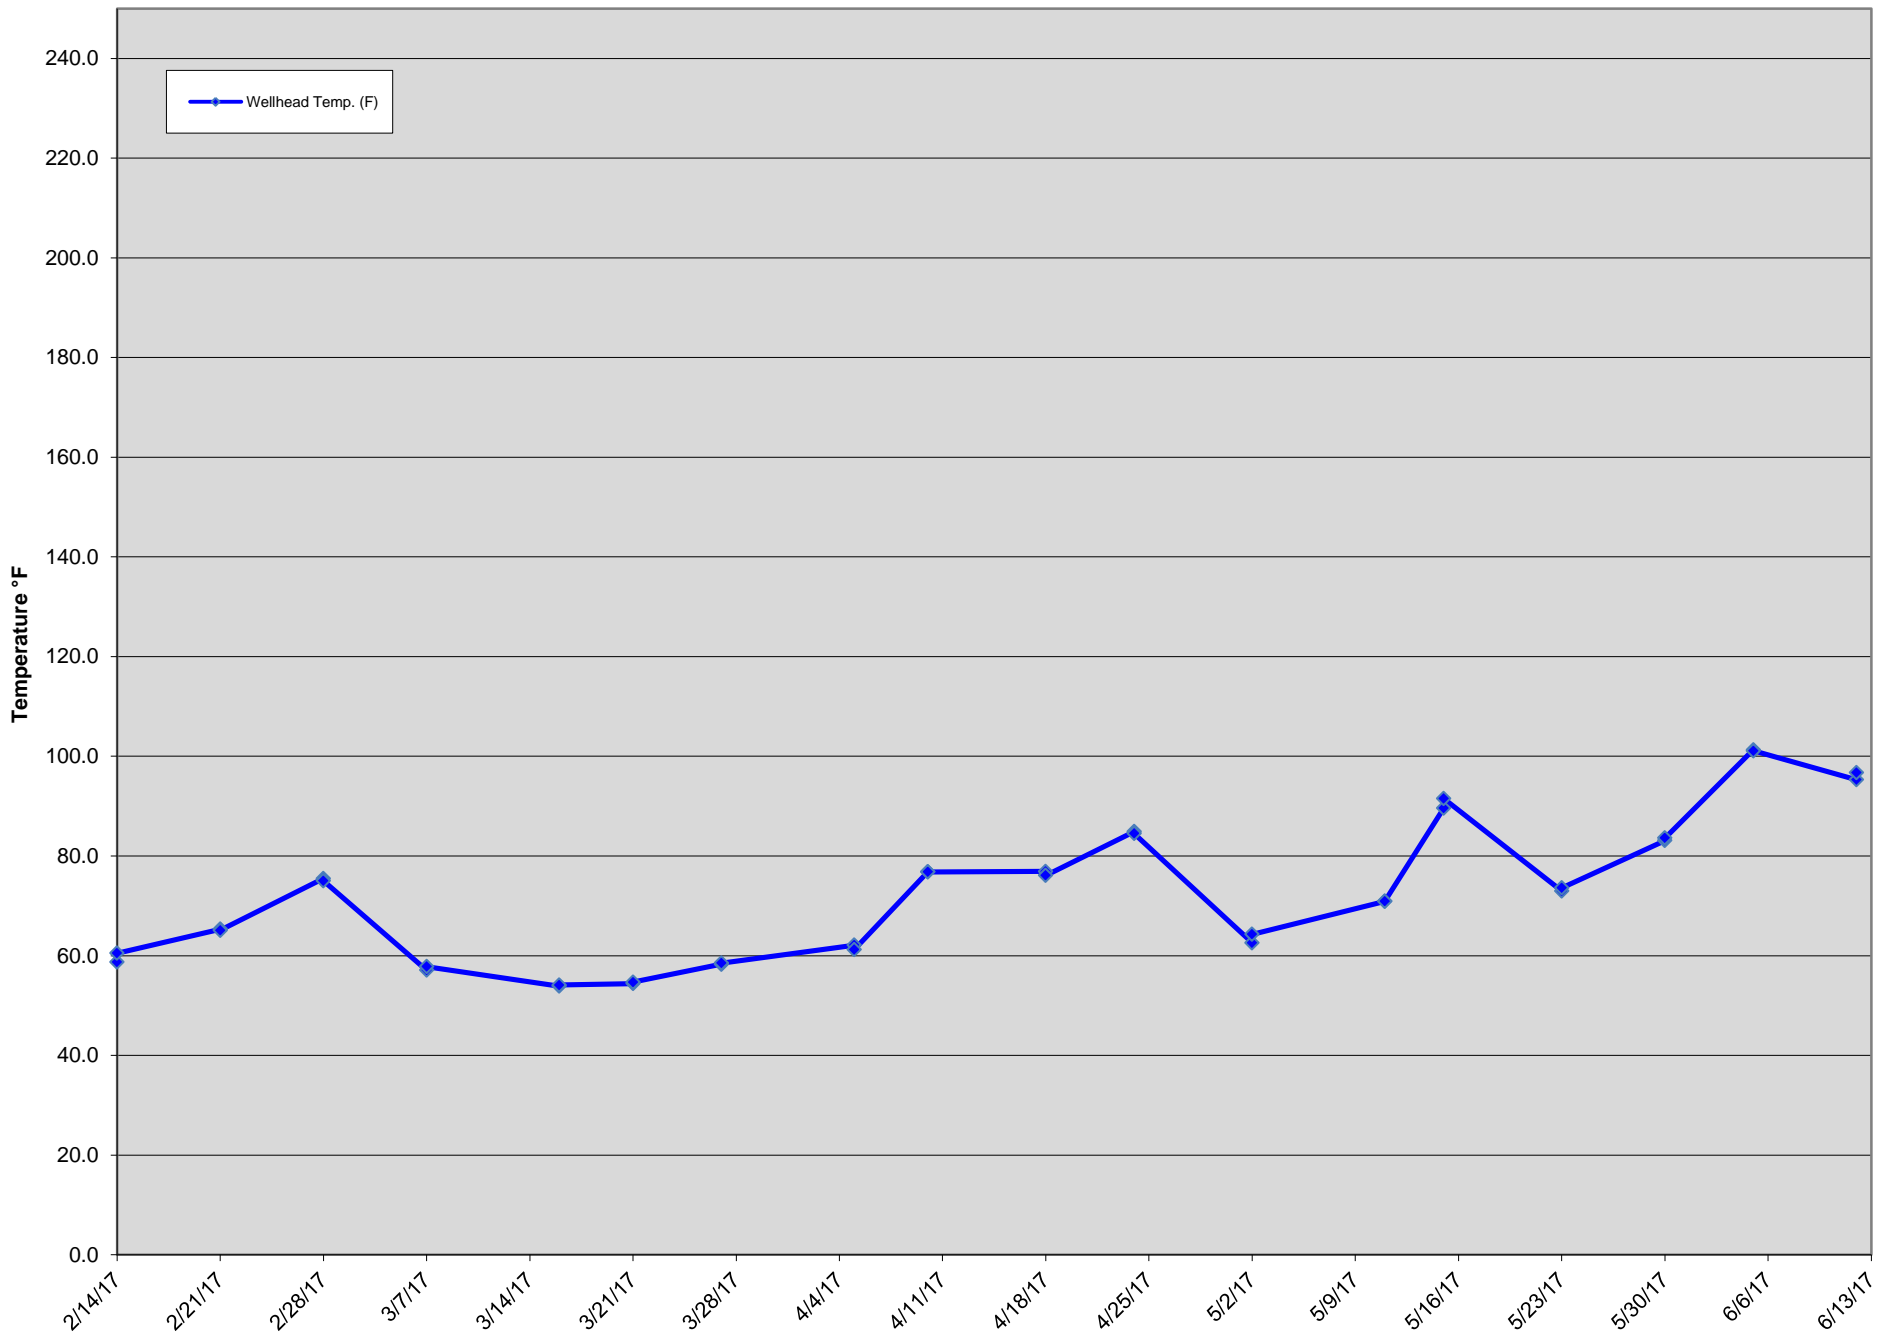


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-06	02/14/17	26.1	47.8	0.4	25.7	62.9	-7.9	N/A	(HES Installed)
GIW-06	02/14/17	25.5	46.5	0.3	27.7	64.4	-8.0	N/A	(HES Installed)
GIW-06	02/21/17	25.4	45.4	0.3	28.9	65.4	-7.1	N/A	(HES Installed)
GIW-06	02/28/17	28.2	49.1	0.2	22.5	75.6	-7.4	N/A	(HES Installed)
GIW-06	03/07/17	31.5	45.9	0.4	22.2	64.0	-6.9	N/A	(HES Installed)
GIW-06	03/07/17	30.9	46.1	0.3	22.7	64.1	-6.9	N/A	(HES Installed)
GIW-06	03/16/17	32.2	44.3	0.3	23.2	48.1	-9.4	N/A	(HES Installed)
GIW-06	03/21/17	14.3	47.3	0.4	38.0	57.5	-9.9	N/A	(HES Installed)
GIW-06	03/27/17	10.3	46.2	0.0	43.5	59.1	-19.1	N/A	(HES Installed)
GIW-06	04/05/17	8.3	46.4	0.2	45.1	60.0	-7.4	N/A	(HES Installed)
GIW-06	04/11/17	7.3	51.5	0.0	41.2	52.9	-4.0	N/A	(HES Installed)
GIW-06	04/11/17	7.2	51.1	0.0	41.7	52.6	-3.2	N/A	(HES Installed)
GIW-06	04/18/17	6.2	45.3	0.1	48.4	74.8	-5.3	N/A	(HES Installed)
GIW-06	04/24/17	6.0	47.3	0.1	46.6	84.0	-3.4	N/A	(HES Installed)
GIW-06	05/02/17	4.8	52.9	0.0	42.3	72.5	-2.3	N/A	(HES Installed)
GIW-06	05/02/17	5.5	51.2	0.0	43.3	70.7	-2.3	N/A	(HES Installed)
GIW-06	05/11/17	24.9	48.6	0.1	26.4	70.4	-3.4	N/A	(HES Installed)
GIW-06	05/15/17	24.7	46.3	0.0	29.0	91.9	-2.7	N/A	(HES Installed)
GIW-06	05/23/17	17.3	48.3	0.2	34.2	75.0	-3.5	N/A	(HES Installed)
GIW-06	05/30/17	22.1	48.5	0.1	29.3	90.3	-4.4	N/A	(HES Installed)
GIW-06	06/05/17	9.8	50.6	0.6	39.0	98.4	-4.5	N/A	(HES Installed)
GIW-06	06/05/17	11.2	48.7	0.6	39.5	95.8	-4.4	N/A	(HES Installed)
GIW-06	06/12/17	14.4	48.6	0.7	36.3	99.1	-4.8	N/A	(HES Installed)

GIW-6 Wellhead Temperatures

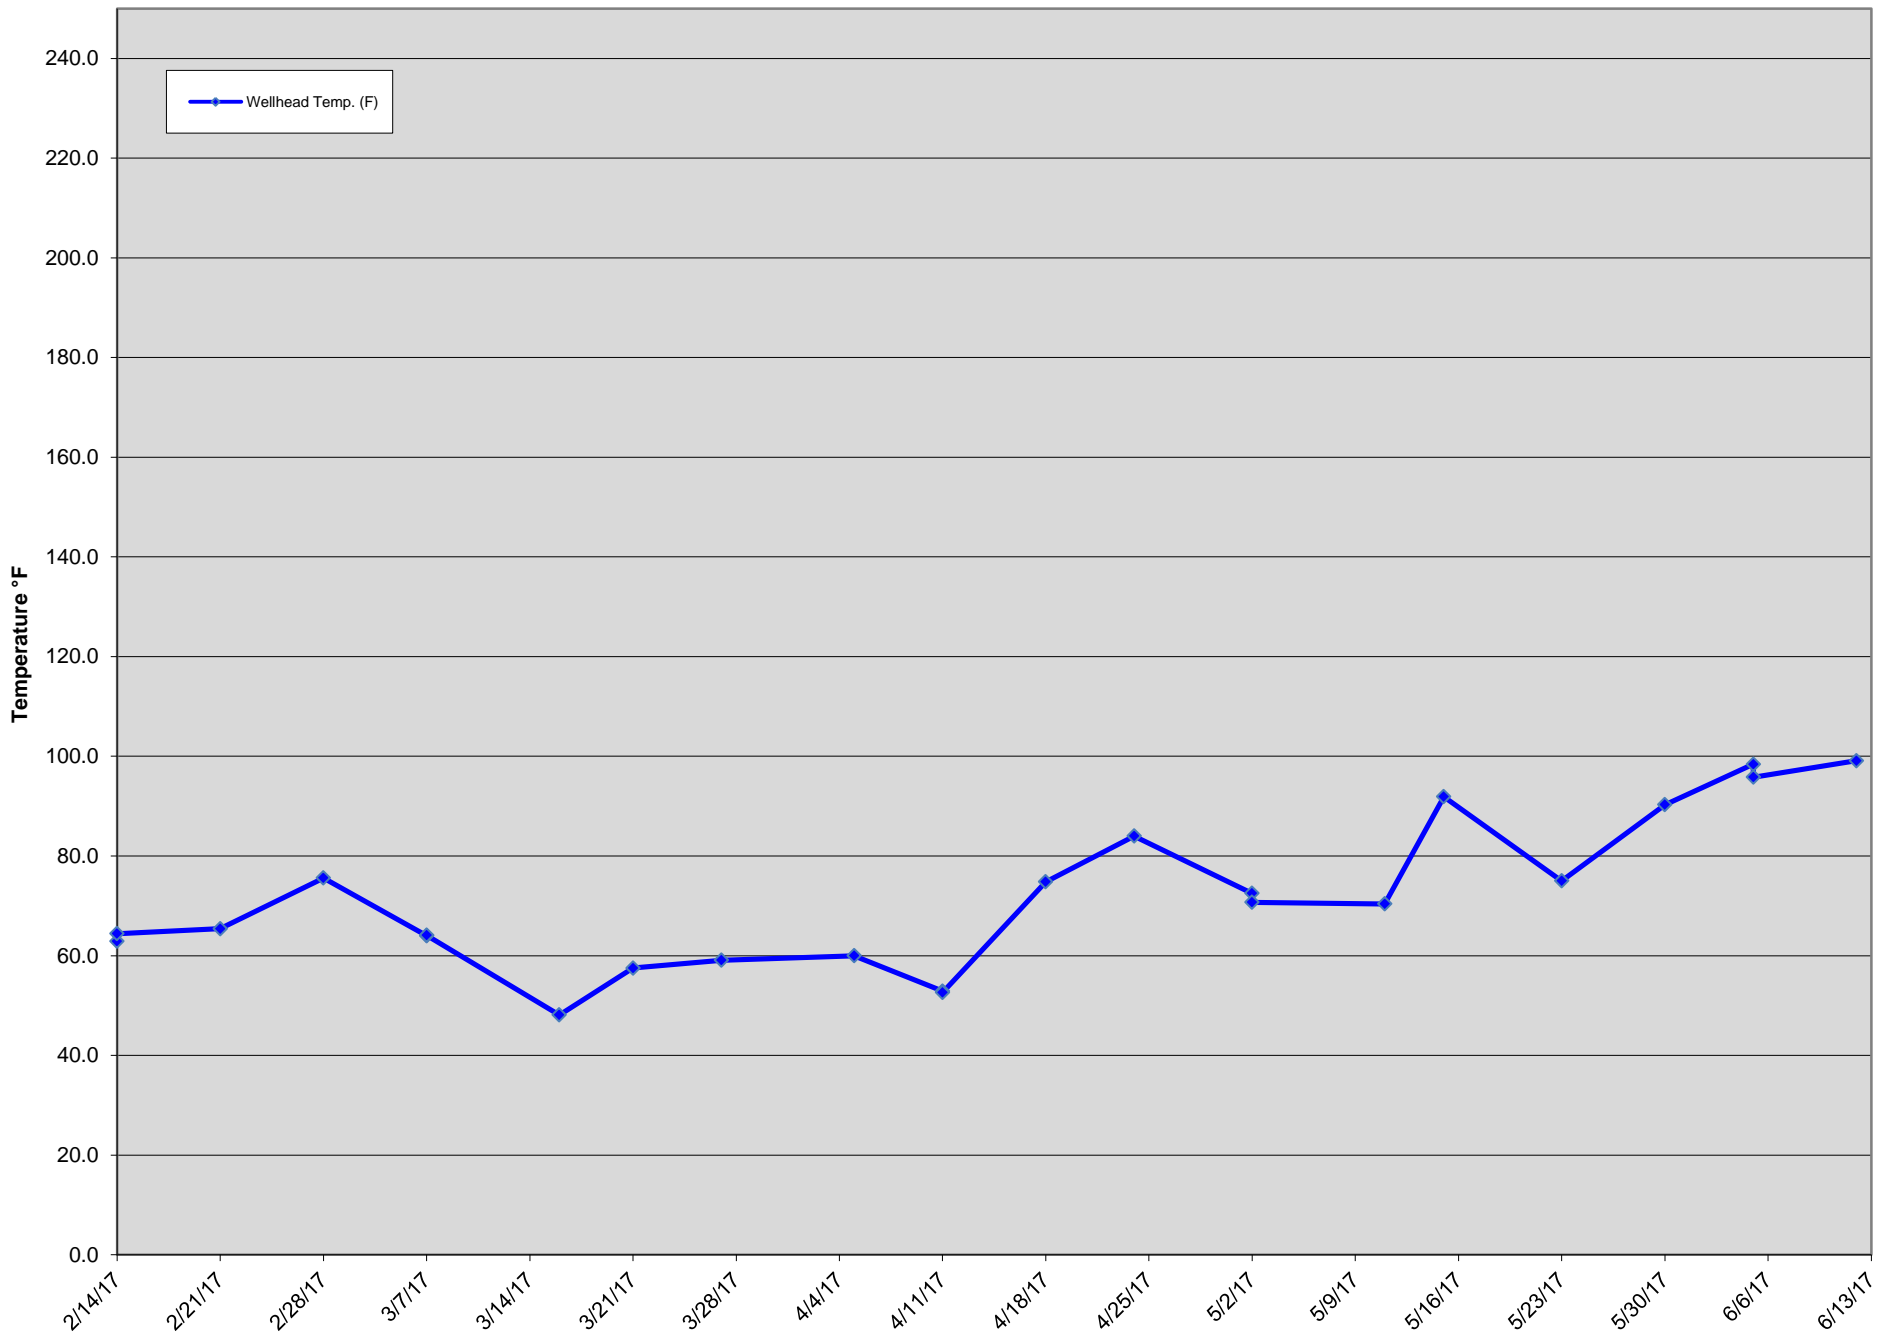


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-07	02/14/17	34.6	48.4	1.6	15.4	67.2	-1.7	N/A	(HES Installed)
GIW-07	02/14/17	33.7	48.9	1.8	15.6	66.4	-1.5	N/A	(HES Installed)
GIW-07	02/21/17	30.6	49.2	0.4	19.8	65.2	-1.3	N/A	(HES Installed)
GIW-07	02/28/17	35.3	50.9	0.5	13.3	75.1	-1.0	N/A	(HES Installed)
GIW-07	03/07/17	37.6	46.2	1.0	15.2	66.1	-1.9	N/A	(HES Installed)
GIW-07	03/07/17	37.7	47.9	1.0	13.4	67.1	-1.7	N/A	(HES Installed)
GIW-07	03/16/17	43.3	44.1	0.8	11.8	47.5	-2.2	N/A	(HES Installed)
GIW-07	03/21/17	28.3	50.6	2.7	18.4	56.8	-4.8	N/A	(HES Installed)
GIW-07	03/27/17	25.9	56.0	1.4	16.7	58.4	-8.0	N/A	(HES Installed)
GIW-07	04/05/17	22.3	55.9	2.0	19.8	59.7	-3.4	N/A	(HES Installed)
GIW-07	04/11/17	12.6	43.1	7.3	37.0	53.0	-2.6	N/A	(HES Installed)
GIW-07	04/11/17	14.4	45.5	6.3	33.8	52.7	-2.5	N/A	(HES Installed)
GIW-07	04/18/17	17.0	55.6	2.6	24.8	76.7	-3.0	N/A	(HES Installed)
GIW-07	04/24/17	21.5	54.2	1.2	23.1	85.2	-1.4	N/A	(HES Installed)
GIW-07	05/02/17	18.1	50.3	3.1	28.5	77.7	-1.8	N/A	(HES Installed)
GIW-07	05/02/17	16.9	51.8	2.9	28.4	78.0	-1.7	N/A	(HES Installed)
GIW-07	05/11/17	29.0	48.4	1.6	21.0	70.4	-2.3	N/A	(HES Installed)
GIW-07	05/15/17	34.0	47.9	0.9	17.2	100.9	-1.7	N/A	(HES Installed)
GIW-07	05/23/17	33.4	48.7	0.9	17.0	75.7	-2.1	N/A	(HES Installed)
GIW-07	05/30/17	34.9	49.1	0.8	15.2	88.2	-2.6	N/A	(HES Installed)
GIW-07	06/05/17	36.9	47.7	0.9	14.5	92.0	-2.3	N/A	(HES Installed)
GIW-07	06/05/17	37.4	46.7	1.0	14.9	91.6	-2.4	N/A	(HES Installed)
GIW-07	06/12/17	35.4	46.9	0.9	16.8	100.8	-2.8	N/A	(HES Installed)

GIW-7 Wellhead Temperatures

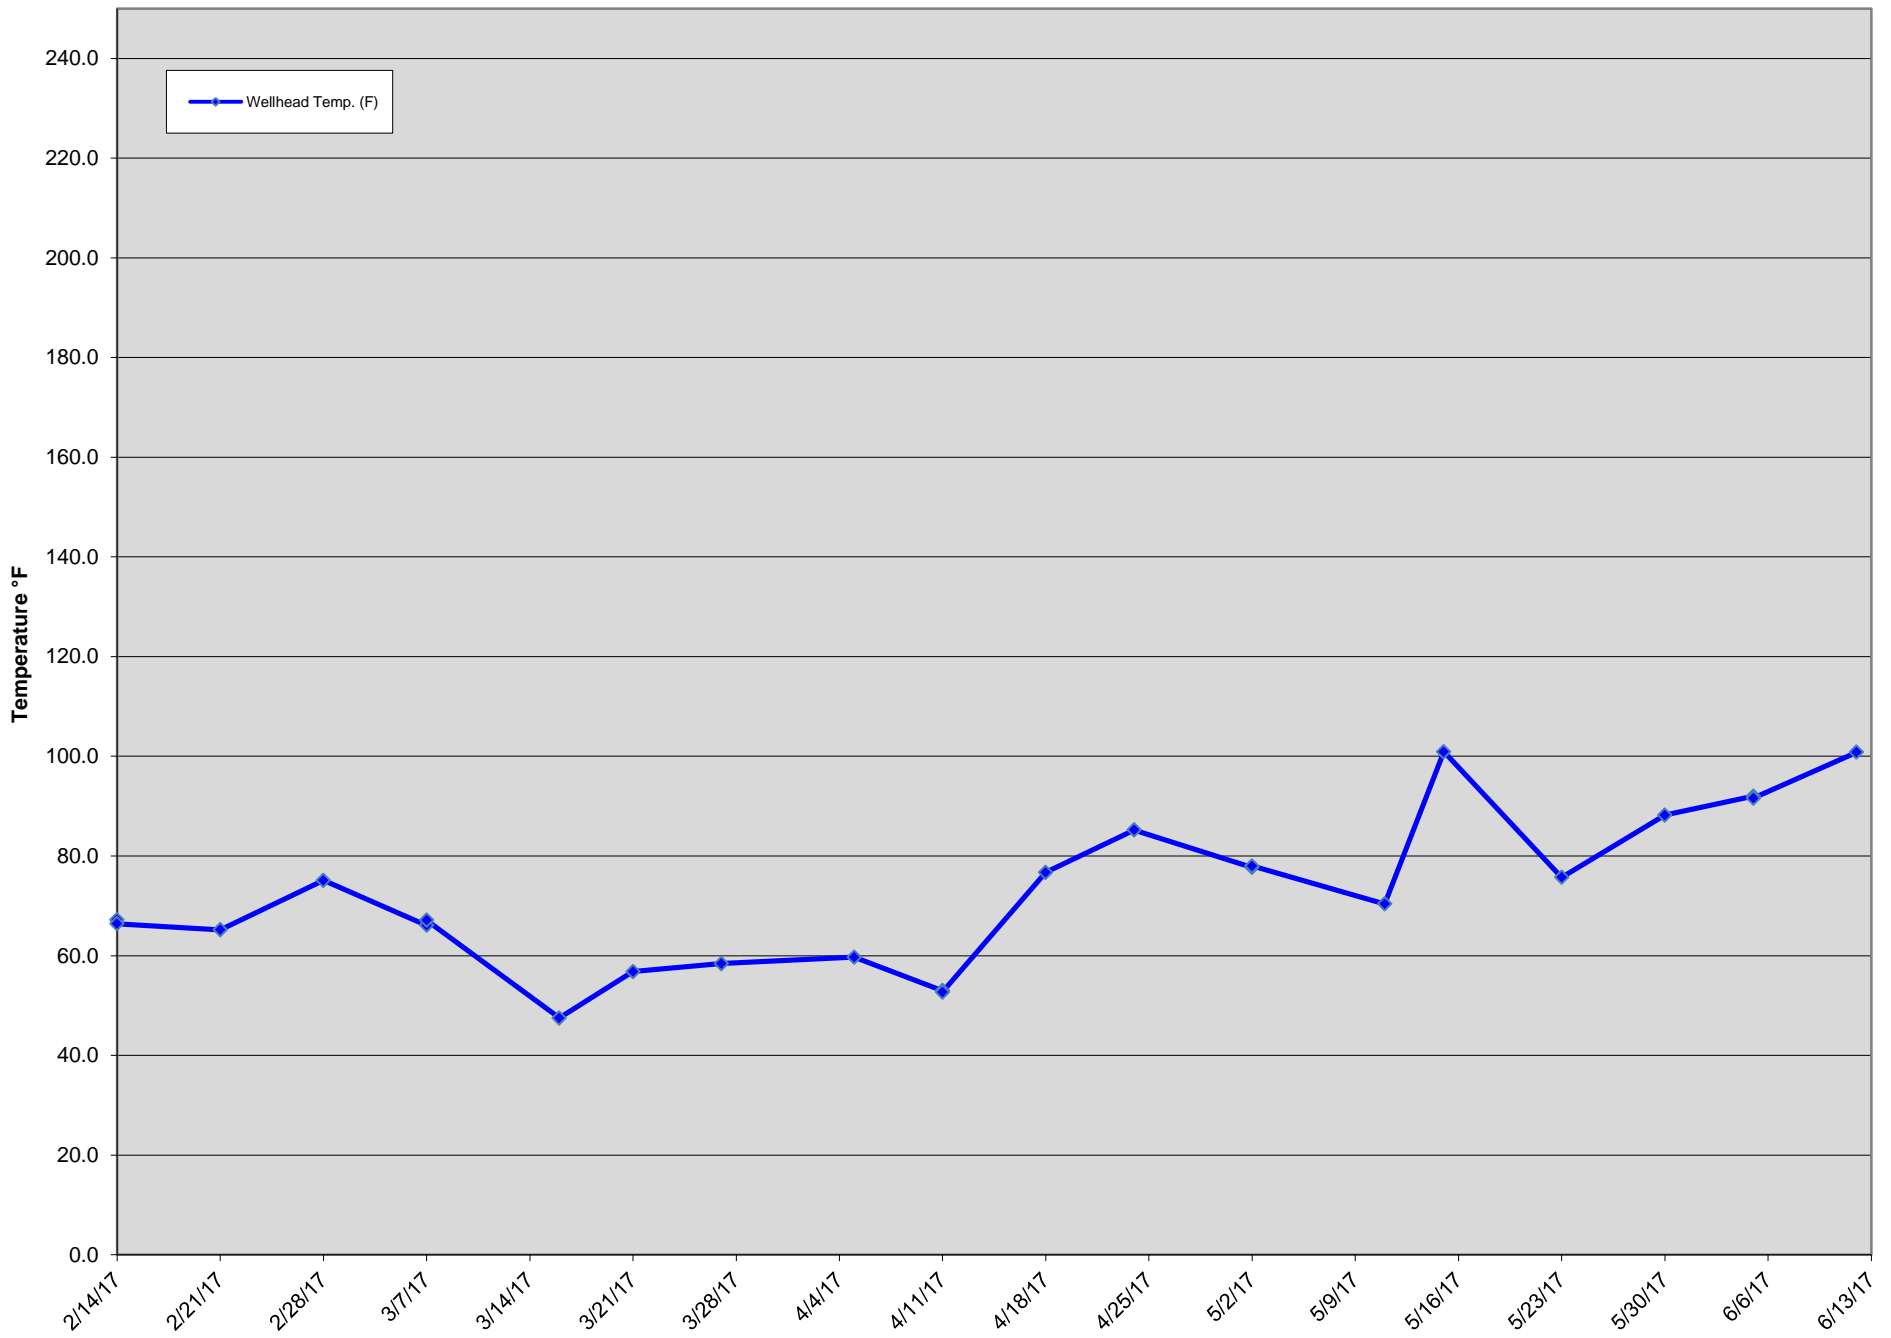


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-08	02/14/17	42.3	52.0	0.0	5.7	66.8	-3.0	N/A	(HES Installed)
GIW-08	02/14/17	43.8	50.5	0.1	5.6	66.5	-3.0	N/A	(HES Installed)
GIW-08	02/21/17	42.8	49.3	0.0	7.9	67.1	-2.9	N/A	(HES Installed)
GIW-08	02/28/17	42.2	51.9	0.0	5.9	76.8	-2.6	N/A	(HES Installed)
GIW-08	03/07/17	36.7	52.9	0.0	10.4	64.7	-3.1	N/A	(HES Installed)
GIW-08	03/07/17	37.1	53.1	0.0	9.8	64.9	-3.1	N/A	(HES Installed)
GIW-08	03/16/17	43.4	49.7	0.0	6.9	48.5	-4.0	N/A	(HES Installed)
GIW-08	03/23/17	24.2	57.4	0.0	18.4	41.7	-5.1	N/A	(HES Installed)
GIW-08	03/27/17	24.7	56.5	0.0	18.8	59.9	-7.8	N/A	(HES Installed)
GIW-08	04/05/17	22.8	59.1	0.0	18.1	60.3	-3.6	N/A	(HES Installed)
GIW-08	04/11/17	22.8	62.0	0.0	15.2	53.3	-2.1	N/A	(HES Installed)
GIW-08	04/11/17	22.4	62.1	0.0	15.5	53.3	-2.1	N/A	(HES Installed)
GIW-08	04/18/17	23.9	53.6	0.0	22.5	79.6	-2.6	N/A	(HES Installed)
GIW-08	04/24/17	24.5	57.3	0.0	18.2	89.4	-1.6	N/A	(HES Installed)
GIW-08	05/02/17	27.6	59.1	0.0	13.3	76.4	-1.5	N/A	(HES Installed)
GIW-08	05/02/17	28.2	61.8	0.0	10.0	77.1	-1.5	N/A	(HES Installed)
GIW-08	05/11/17	29.1	58.7	0.0	12.2	71.4	-1.9	N/A	(HES Installed)
GIW-08	05/15/17	31.0	57.5	0.0	11.5	101.5	-1.5	N/A	(HES Installed)
GIW-08	05/23/17	29.4	56.8	0.0	13.8	76.2	-1.8	N/A	(HES Installed)
GIW-08	05/30/17	30.0	57.2	0.0	12.8	94.6	-2.1	N/A	(HES Installed)
GIW-08	06/05/17	33.2	55.6	0.0	11.2	96.5	-2.2	N/A	(HES Installed)
GIW-08	06/05/17	33.3	54.9	0.0	11.8	94.2	-2.2	N/A	(HES Installed)
GIW-08	06/12/17	30.2	54.5	0.0	15.3	107.6	-2.3	N/A	(HES Installed)

GIW-8 Wellhead Temperatures

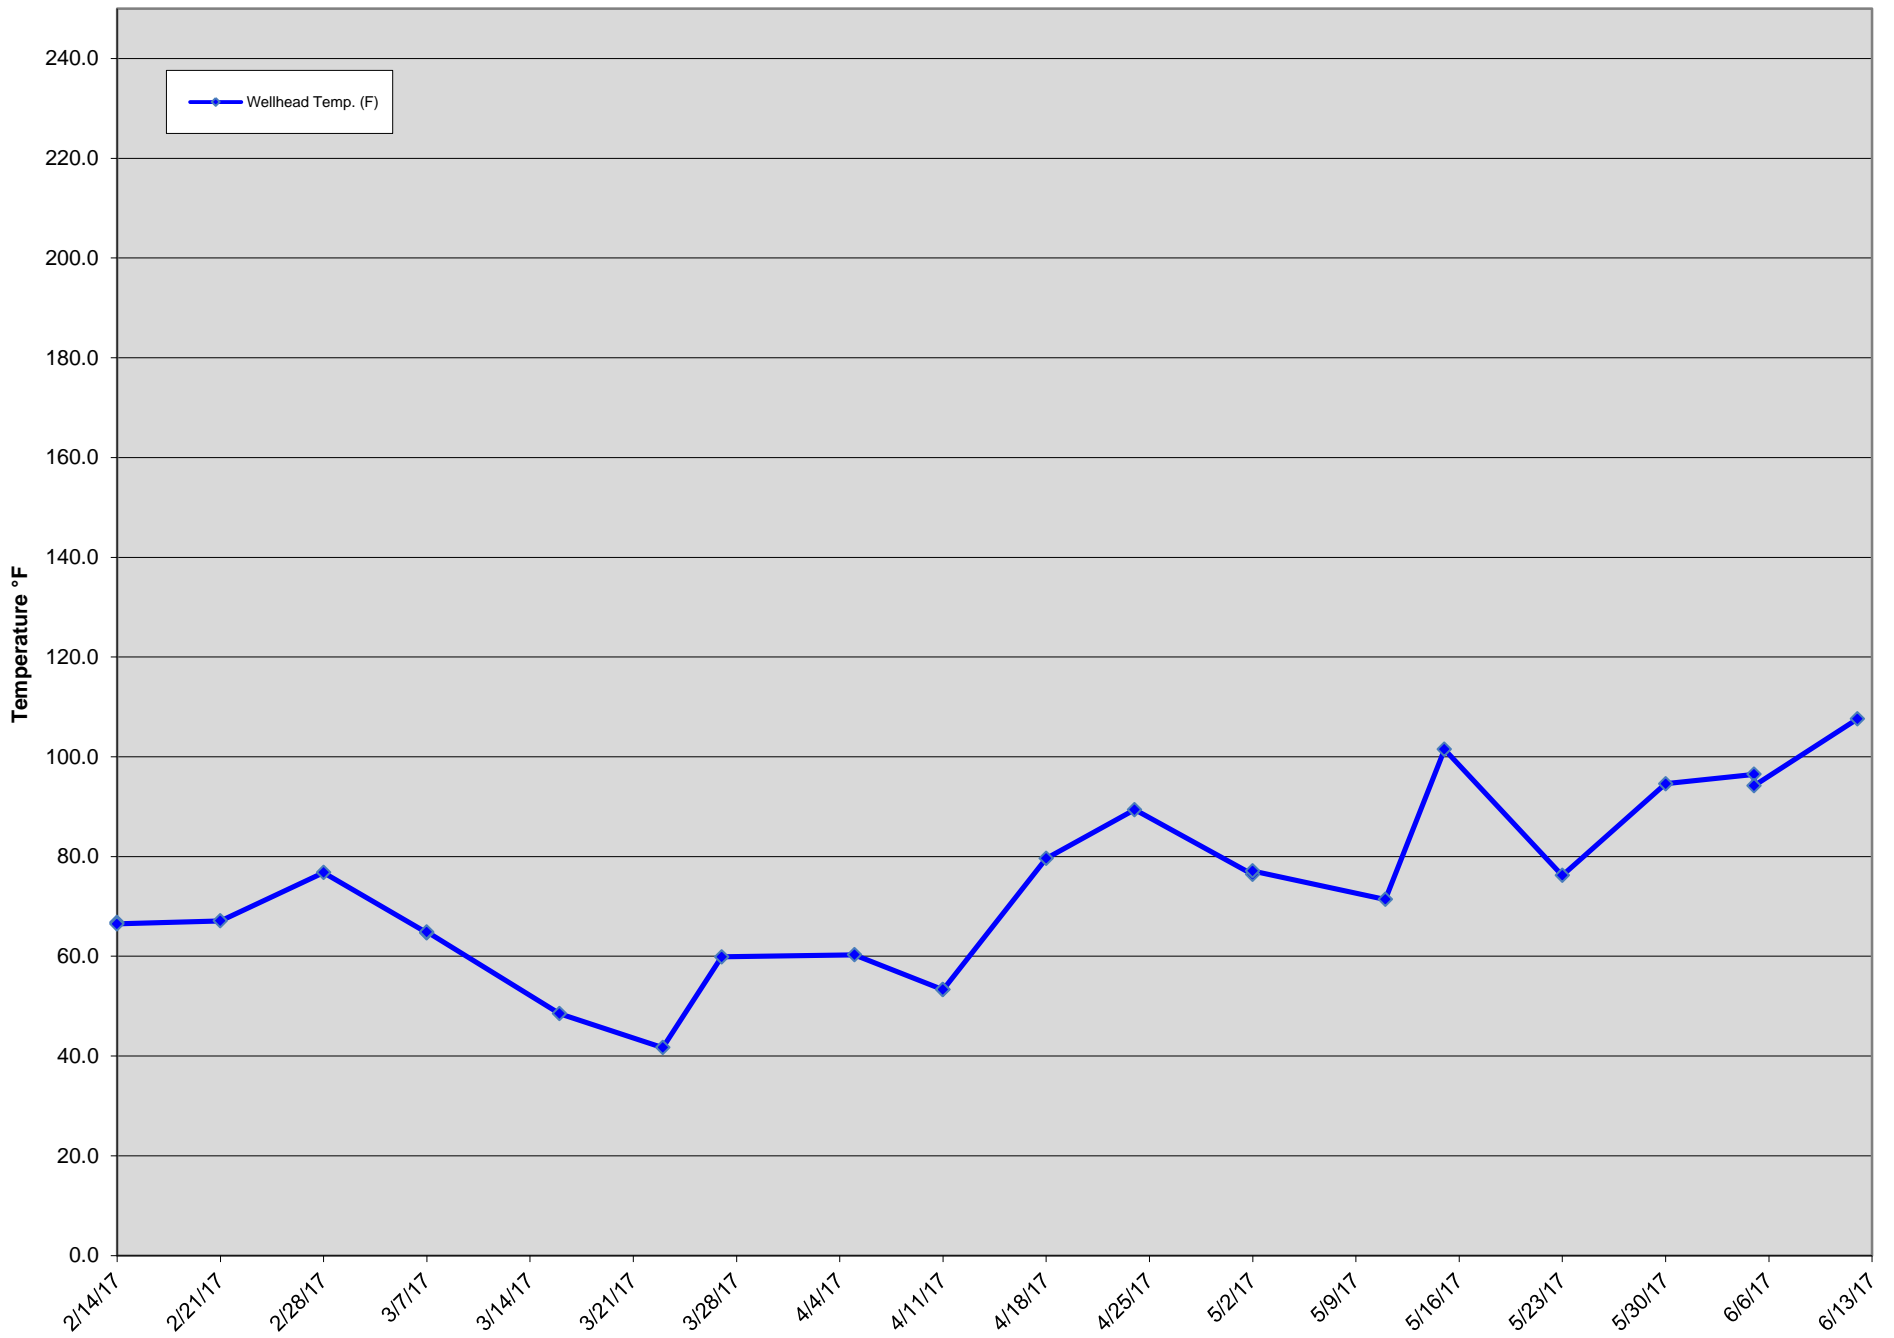


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Initial Static Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-09	02/14/17	30.6	42.9	1.4	25.1	67.2	-0.1	N/A	(HES Installed)
GIW-09	02/14/17	31.1	41.2	1.5	26.2	68.1	-0.1	N/A	(HES Installed)
GIW-09	02/21/17	19.7	40.0	3.4	36.9	65.8	-0.1	N/A	(HES Installed)
GIW-09	02/28/17	33.1	43.9	0.7	22.3	75.7	-0.1	N/A	(HES Installed)
GIW-09	03/07/17	5.8	31.4	5.8	57.0	65.0	-0.1	N/A	(HES Installed)
GIW-09	03/07/17	6.7	25.0	6.0	62.3	65.4	-0.1	N/A	(HES Installed)
GIW-09	03/16/17	26.7	38.9	2.3	32.1	48.3	-0.2	N/A	(HES Installed)
GIW-09	03/21/17	4.6	24.1	8.6	62.7	65.2	-0.5	N/A	(HES Installed)
GIW-09	03/21/17	4.9	21.6	8.8	64.7	65.8	-0.5	N/A	(HES Installed)
GIW-09	03/27/17	8.6	29.1	6.2	56.1	59.9	-0.7	N/A	(HES Installed)
GIW-09	03/27/17	9.3	25.6	6.4	58.7	59.7	-0.7	N/A	(HES Installed)
GIW-09	04/05/17	9.4	29.9	4.8	55.9	60.0	-0.3	N/A	(HES Installed)
GIW-09	04/11/17	2.4	23.6	11.7	62.3	53.4	-0.4	N/A	(HES Installed)
GIW-09	04/11/17	1.9	18.6	12.2	67.3	53.3	-0.4	N/A	(HES Installed)
GIW-09	04/18/17	4.9	23.6	6.3	65.2	75.7	-0.4	N/A	(HES Installed)
GIW-09	04/18/17	5.3	21.0	6.3	67.4	75.7	-0.4	N/A	(HES Installed)
GIW-09	04/24/17	7.3	33.8	1.5	57.4	87.3	-0.1	N/A	(HES Installed)
GIW-09	05/02/17	11.5	36.2	1.6	50.7	74.8	-0.2	N/A	(HES Installed)
GIW-09	05/02/17	12.4	30.6	1.8	55.2	74.5	-0.3	N/A	(HES Installed)
GIW-09	05/11/17	2.8	34.4	3.2	59.6	70.0	-0.3	N/A	(HES Installed)
GIW-09	05/15/17	2.6	25.2	3.7	68.5	95.1	-0.2	N/A	(HES Installed)
GIW-09	05/23/17	8.2	32.6	1.0	58.2	74.5	-0.2	N/A	(HES Installed)
GIW-09	05/30/17	3.9	29.4	1.7	65.0	92.1	-0.3	N/A	(HES Installed)
GIW-09	06/06/17	3.0	24.2	3.6	69.2	92.7	-0.3	N/A	(HES Installed)
GIW-09	06/06/17	2.6	25.0	3.5	68.9	92.9	-0.3	N/A	(HES Installed)
GIW-09	06/12/17	10.2	33.3	0.6	55.9	100.8	-0.4	N/A	(HES Installed)

GIW-9 Wellhead Temperatures

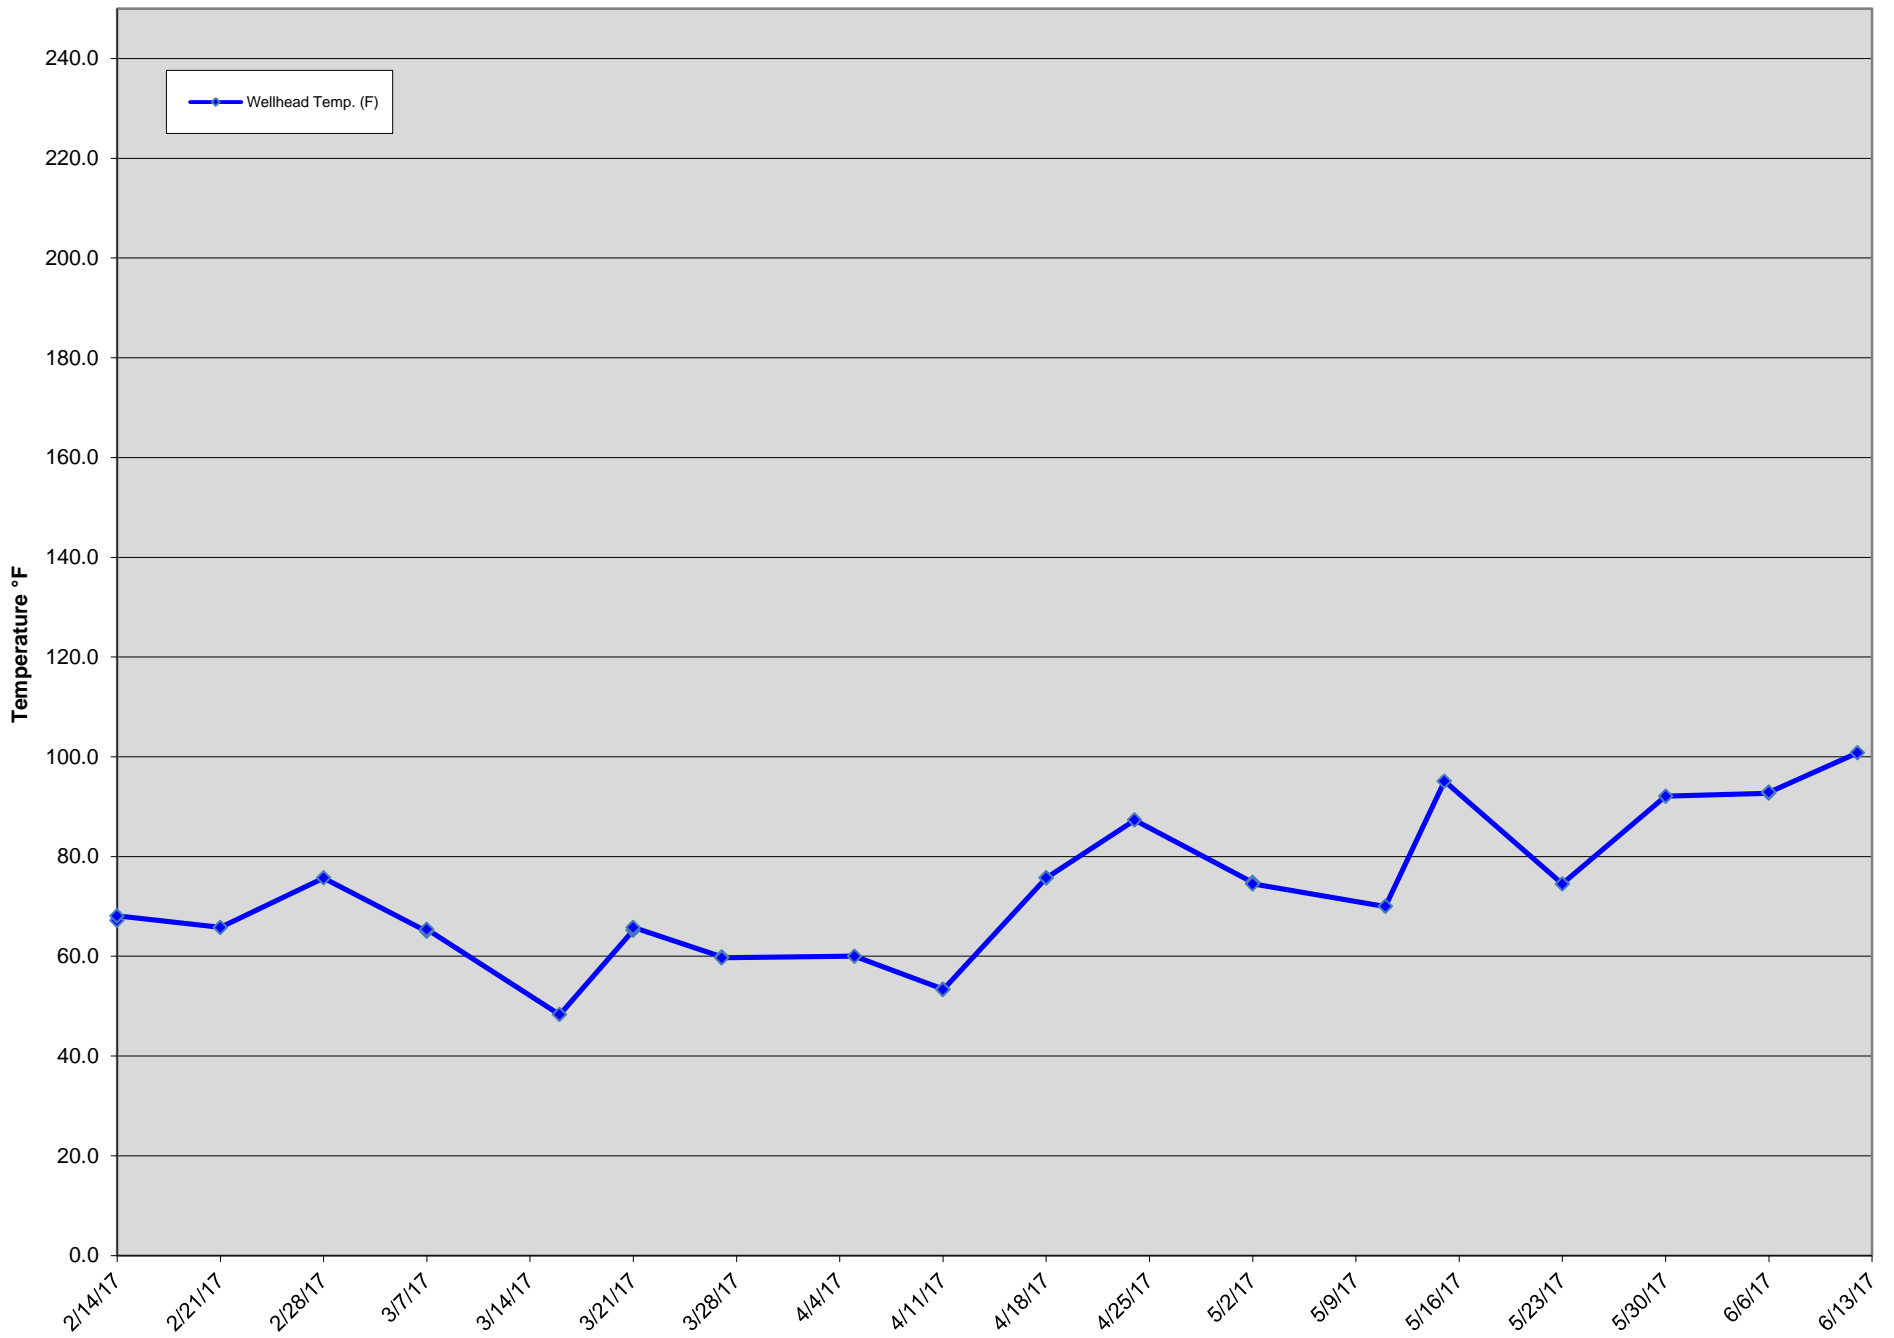


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-10	02/14/17	9.8	52.8	0.0	37.4	67.0	-1.1	N/A	(HES Installed)
GIW-10	02/21/17	8.8	53.7	0.0	37.5	67.5	-1.2	N/A	(HES Installed)
GIW-10	02/28/17	7.6	52.1	0.0	40.3	76.6	-0.7	N/A	(HES Installed)
GIW-10	03/07/17	7.2	54.5	0.0	38.3	59.8	-1.2	N/A	(HES Installed)
GIW-10	03/07/17	7.2	53.3	0.0	39.5	60.1	-1.2	N/A	(HES Installed)
GIW-10	03/16/17	6.7	55.6	0.0	37.7	54.9	-1.1	N/A	(HES Installed)
GIW-10	03/21/17	3.6	53.7	0.0	42.7	54.4	-2.0	N/A	(HES Installed)
GIW-10	03/27/17	3.7	56.3	0.0	40.0	59.2	-3.1	N/A	(HES Installed)
GIW-10	04/05/17	4.1	56.0	0.0	39.9	61.9	-1.4	N/A	(HES Installed)
GIW-10	04/10/17	2.0	52.7	0.0	45.3	79.6	-0.8	N/A	(HES Installed)
GIW-10	04/10/17	1.9	53.4	0.0	44.7	84.9	-0.9	N/A	(HES Installed)
GIW-10	04/18/17	1.3	55.4	0.0	43.3	76.8	-0.8	N/A	(HES Installed)
GIW-10	04/24/17	3.0	57.2	0.0	39.8	89.8	-0.1	N/A	(HES Installed)
GIW-10	05/02/17	5.3	48.9	0.0	45.8	60.0	-0.1	N/A	(HES Installed)
GIW-10	05/02/17	4.6	52.3	0.0	43.1	60.7	-0.1	N/A	(HES Installed)
GIW-10	05/11/17	2.3	52.6	0.0	45.1	71.1	-0.5	N/A	(HES Installed)
GIW-10	05/15/17	2.8	52.4	0.0	44.8	88.4	-0.3	N/A	(HES Installed)
GIW-10	05/23/17	3.6	52.4	0.0	44.0	76.6	-0.5	N/A	(HES Installed)
GIW-10	05/30/17	4.1	53.4	0.0	42.5	90.1	-0.7	N/A	(HES Installed)
GIW-10	06/05/17	5.3	50.8	0.0	43.9	108.0	-0.6	N/A	(HES Installed)
GIW-10	06/05/17	6.0	53.3	0.0	40.7	109.0	-0.6	N/A	(HES Installed)
GIW-10	06/12/17	3.8	50.4	0.0	45.8	96.5	-0.9	N/A	(HES Installed)

GIW-10 Wellhead Temperatures

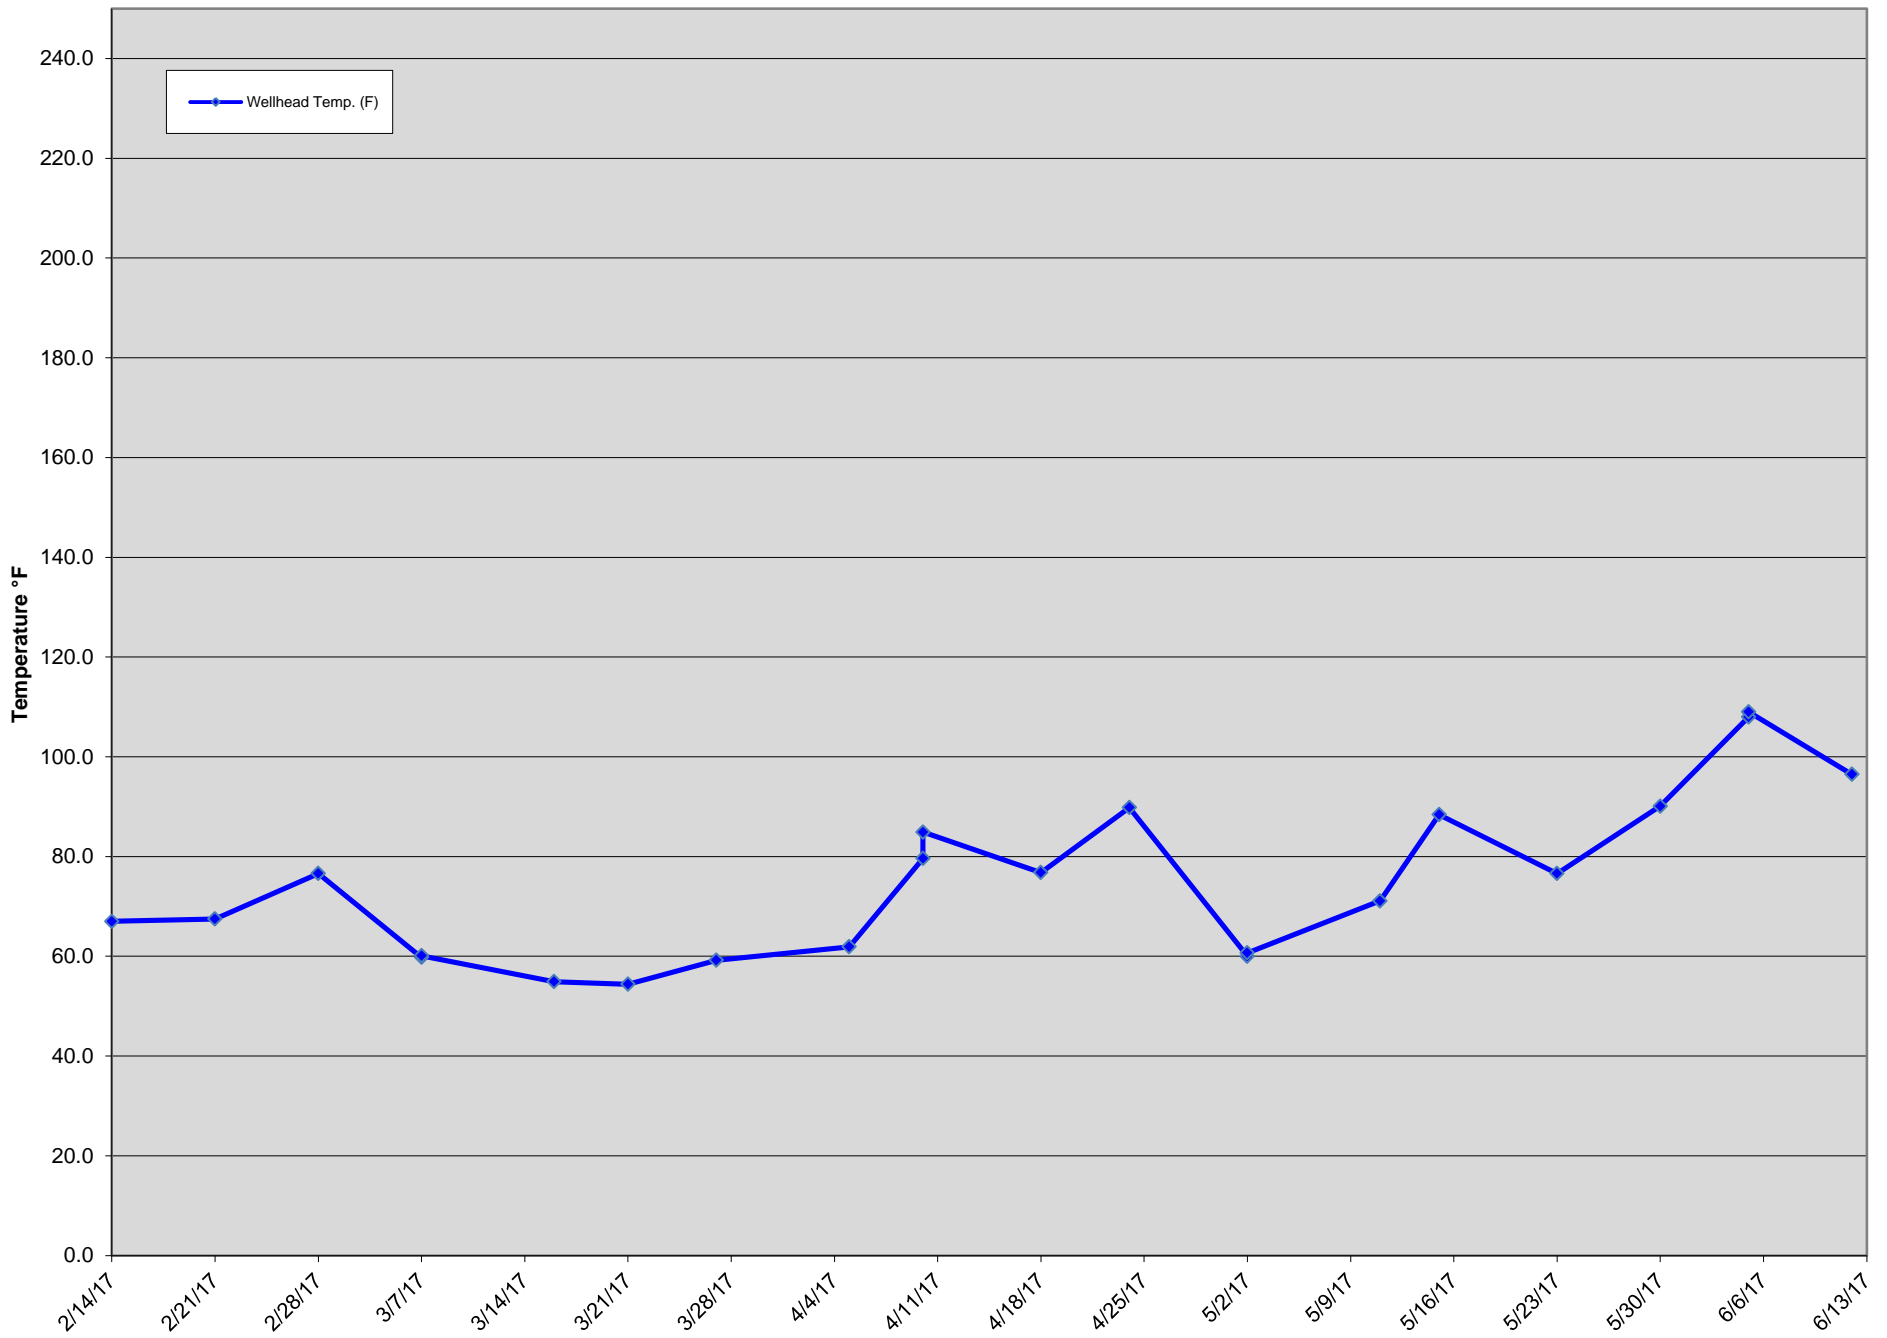


GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-11	02/14/17	6.3	58.1	0.0	35.6	65.6	-1.3	N/A	(HES Installed)
GIW-11	02/14/17	5.7	58.5	0.0	35.8	65.2	-1.4	N/A	(HES Installed)
GIW-11	02/21/17	6.5	55.8	0.0	37.7	68.8	-1.6	N/A	(HES Installed)
GIW-11	02/28/17	5.5	57.0	0.0	37.5	77.7	-1.4	N/A	(HES Installed)
GIW-11	03/07/17	6.9	53.4	0.2	39.5	61.8	-1.8	N/A	(HES Installed)
GIW-11	03/07/17	6.6	56.8	0.2	36.4	60.0	-0.4	N/A	(HES Installed)
GIW-11	03/16/17	1.8	59.3	0.0	38.9	55.4	0.1	N/A	(HES Installed)
GIW-11	03/16/17	1.6	61.9	0.0	36.5	55.7	-0.1	N/A	(HES Installed)
GIW-11	03/21/17	2.6	60.1	0.0	37.3	57.7	-0.6	N/A	(HES Installed)
GIW-11	03/27/17	3.3	59.3	0.0	37.4	58.7	-0.5	N/A	(HES Installed)
GIW-11	04/05/17	4.1	59.6	0.0	36.3	62.3	-0.4	N/A	(HES Installed)
GIW-11	04/11/17	3.3	61.4	0.1	35.2	52.8	-0.6	N/A	(HES Installed)
GIW-11	04/11/17	3.2	60.7	0.0	36.1	52.9	-0.6	N/A	(HES Installed)
GIW-11	04/18/17	2.7	60.9	0.0	36.4	76.9	-0.3	N/A	(HES Installed)
GIW-11	04/24/17	3.0	60.8	0.0	36.2	83.8	-0.1	N/A	(HES Installed)
GIW-11	05/02/17	2.3	58.1	0.0	39.6	71.1	-0.4	N/A	(HES Installed)
GIW-11	05/02/17	2.1	59.8	0.0	38.1	71.4	-0.4	N/A	(HES Installed)
GIW-11	05/11/17	3.1	57.7	0.0	39.2	71.6	-0.5	N/A	(HES Installed)
GIW-11	05/15/17	2.5	56.5	0.0	41.0	92.9	-0.3	N/A	(HES Installed)
GIW-11	05/23/17	2.3	57.8	0.0	39.9	74.1	-0.3	N/A	(HES Installed)
GIW-11	05/30/17	2.1	60.5	0.0	37.4	92.2	-0.3	N/A	(HES Installed)
GIW-11	06/05/17	1.9	59.4	0.0	38.7	98.4	-0.2	N/A	(HES Installed)
GIW-11	06/05/17	2.1	59.7	0.0	38.2	98.2	-0.2	N/A	(HES Installed)
GIW-11	06/12/17	4.8	58.5	0.0	36.7	100.1	-0.3	N/A	(HES Installed)

GIW-11 Wellhead Temperatures

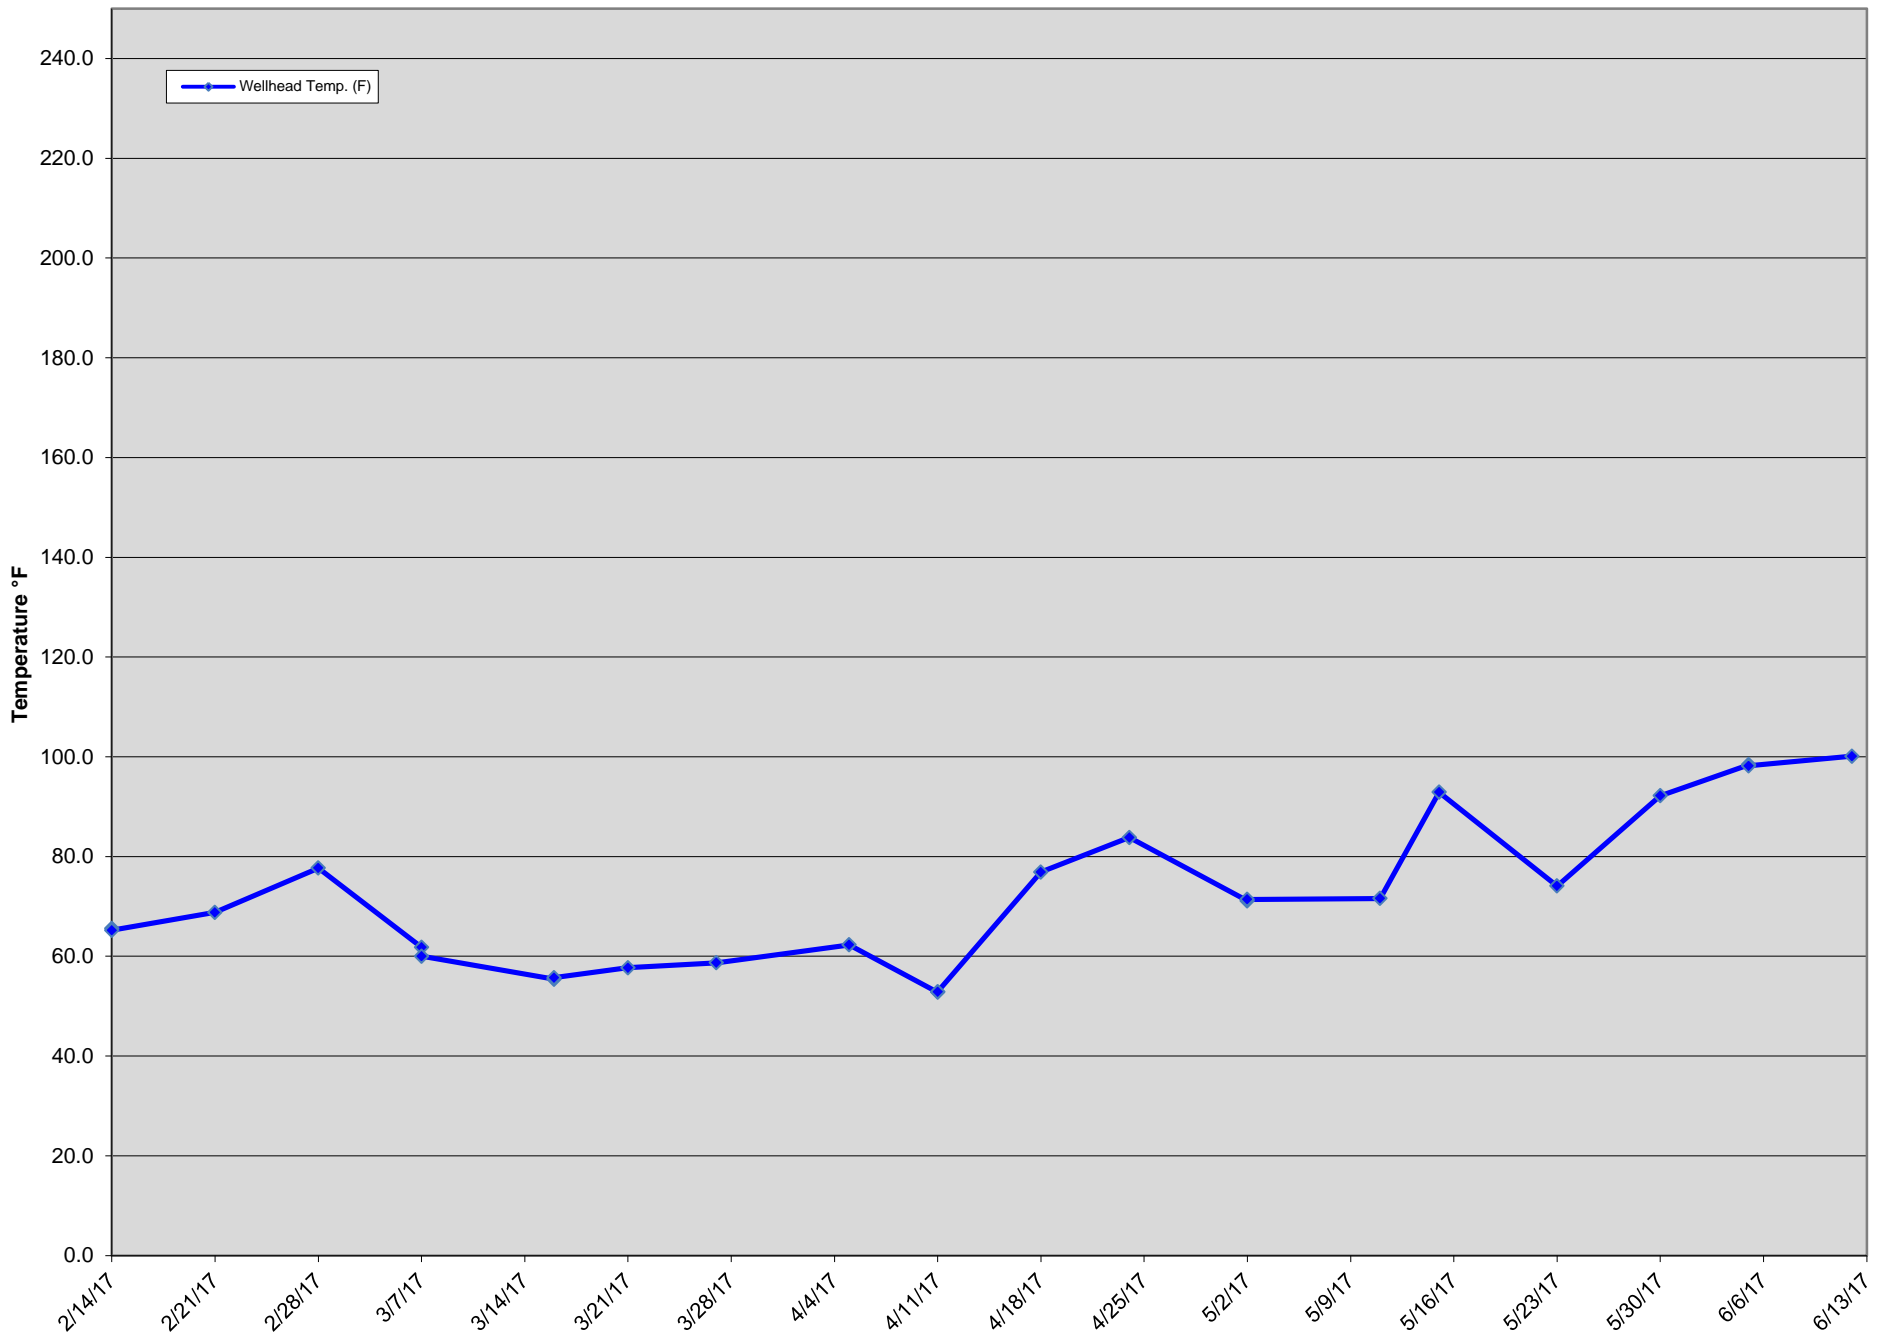

GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-12	02/14/17	11.2	38.5	5.2	45.1	60.7	-0.4	N/A	(HES Installed)
GIW-12	02/14/17	11.7	39.5	5.2	43.6	61.4	-0.2	N/A	(HES Installed)
GIW-12	02/21/17	10.3	47.2	5.1	37.4	67.0	-0.2	N/A	(HES Installed)
GIW-12	02/21/17	11.0	43.2	5.3	40.5	67.0	-0.2	N/A	(HES Installed)
GIW-12	02/28/17	11.5	44.1	4.1	40.3	77.5	-0.2	N/A	(HES Installed)
GIW-12	03/07/17	9.8	37.4	7.5	45.3	58.8	-0.3	N/A	(HES Installed)
GIW-12	03/07/17	10.3	34.4	7.8	47.5	58.8	-0.6	N/A	(HES Installed)
GIW-12	03/16/17	10.1	46.7	3.3	39.9	51.6	-0.2	N/A	(HES Installed)
GIW-12	03/21/17	9.6	35.7	8.1	46.6	52.3	-0.3	N/A	(HES Installed)
GIW-12	03/21/17	9.7	34.4	8.3	47.6	53.1	-0.3	N/A	(HES Installed)
GIW-12	03/27/17	11.2	38.3	7.1	43.4	58.2	-0.3	N/A	(HES Installed)
GIW-12	03/27/17	11.4	36.8	7.2	44.6	58.2	-0.2	N/A	(HES Installed)
GIW-12	04/05/17	10.8	40.6	6.3	42.3	64.4	-0.2	N/A	(HES Installed)
GIW-12	04/05/17	11.8	38.6	6.6	43.0	64.6	-0.2	N/A	(HES Installed)
GIW-12	04/10/17	10.3	40.9	6.2	42.6	78.4	-0.2	N/A	(HES Installed)
GIW-12	04/10/17	10.7	38.4	5.9	45.0	81.2	-0.2	N/A	(HES Installed)
GIW-12	04/18/17	11.8	43.7	5.3	39.2	75.7	-0.2	N/A	(HES Installed)
GIW-12	04/18/17	12.3	41.6	5.4	40.7	75.7	-0.2	N/A	(HES Installed)
GIW-12	04/24/17	12.4	50.0	2.2	35.4	81.2	-0.2	N/A	(HES Installed)
GIW-12	05/02/17	11.2	44.3	5.2	39.3	71.2	-0.2	N/A	(HES Installed)
GIW-12	05/02/17	11.7	38.8	5.5	44.0	73.0	-0.2	N/A	(HES Installed)
GIW-12	05/11/17	12.1	44.2	5.0	38.7	70.9	-0.3	N/A	(HES Installed)
GIW-12	05/11/17	12.2	43.1	5.0	39.7	70.7	-0.3	N/A	(HES Installed)
GIW-12	05/15/17	12.9	44.8	4.5	37.8	91.7	-0.2	N/A	(HES Installed)
GIW-12	05/23/17	12.1	45.7	4.6	37.6	73.6	-0.2	N/A	(HES Installed)
GIW-12	05/30/17	13.1	43.3	4.9	38.7	89.8	-0.2	N/A	(HES Installed)
GIW-12	06/05/17	11.7	45.3	4.2	38.8	97.0	-0.2	N/A	(HES Installed)
GIW-12	06/05/17	12.1	44.0	4.3	39.6	99.4	-0.2	N/A	(HES Installed)
GIW-12	06/12/17	11.9	43.3	4.9	39.9	98.6	-0.2	N/A	(HES Installed)

GIW-12 Wellhead Temperatures

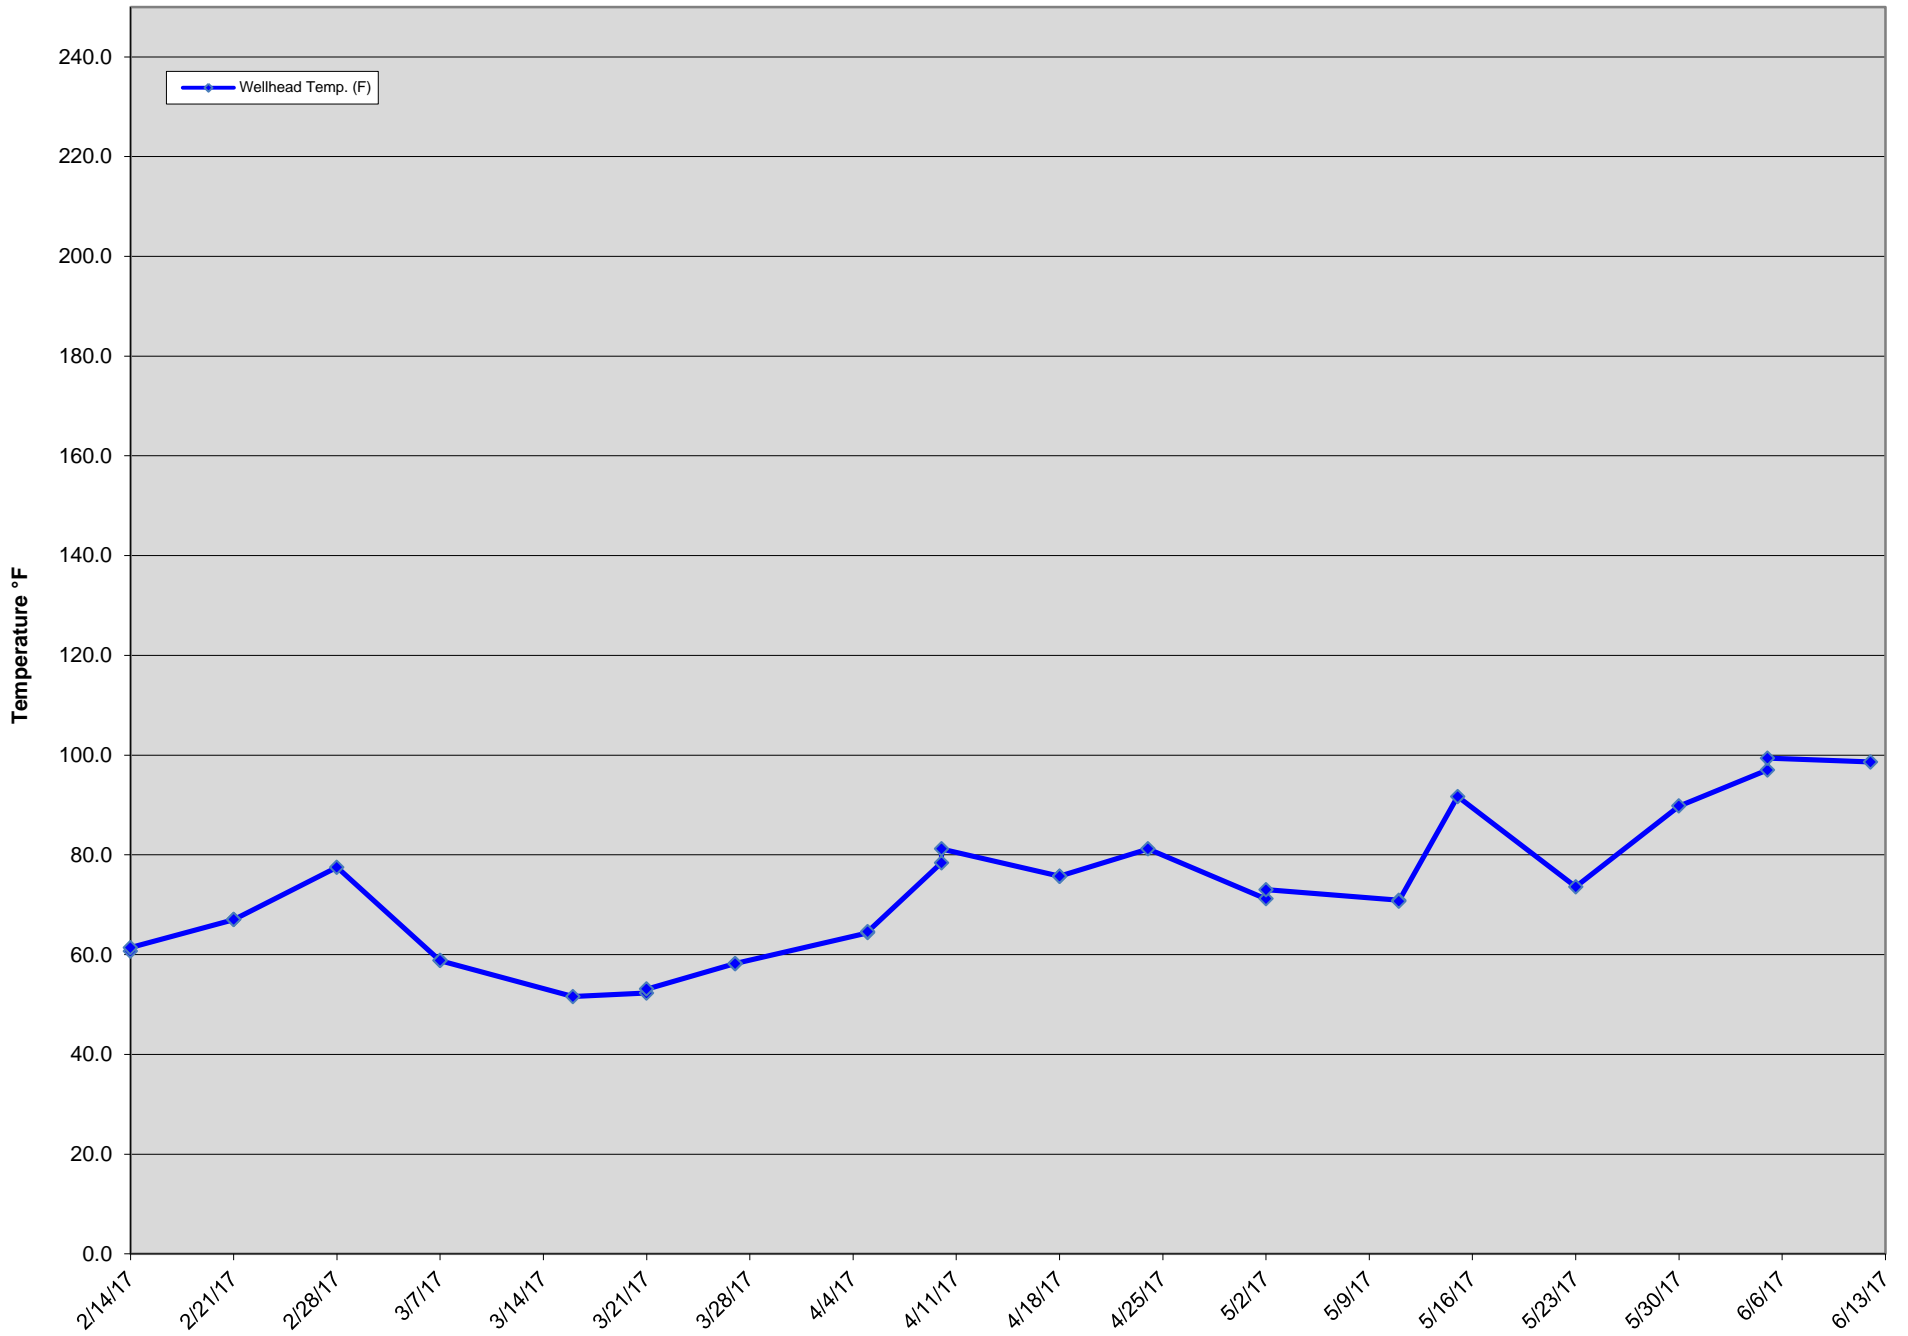

GIW ID#	Reading Date	CH4 (% Vol.)	CO2 (% Vol.)	Oxygen (% Vol.)	Balance (% Vol.)	Wellhead Temp. (F)	Pressure (In W.C.)	Pump Operational (Y/N)	Comments
GIW-13	02/14/17	13.0	61.8	0.0	25.2	60.9	-1.5	N/A	(HES Installed)
GIW-13	02/14/17	11.6	62.1	0.0	26.3	62.1	-1.5	N/A	(HES Installed)
GIW-13	02/21/17	14.0	56.5	0.0	29.5	66.3	-1.5	N/A	(HES Installed)
GIW-13	02/28/17	14.2	57.7	0.0	28.1	78.2	-1.3	N/A	(HES Installed)
GIW-13	03/07/17	14.2	63.5	0.0	22.3	58.2	-1.6	N/A	(HES Installed)
GIW-13	03/07/17	14.1	63.4	0.0	22.5	59.4	-1.7	N/A	(HES Installed)
GIW-13	03/16/17	14.1	60.7	0.0	25.2	52.1	-1.4	N/A	(HES Installed)
GIW-13	03/21/17	11.9	61.5	0.0	26.6	51.8	-0.9	N/A	(HES Installed)
GIW-13	03/27/17	11.8	63.0	0.0	25.2	58.1	-0.8	N/A	(HES Installed)
GIW-13	04/05/17	12.8	59.5	0.0	27.7	65.9	-0.6	N/A	(HES Installed)
GIW-13	04/10/17	12.4	60.5	0.0	27.1	75.9	-0.8	N/A	(HES Installed)
GIW-13	04/10/17	12.2	64.9	0.0	22.9	76.0	-0.6	N/A	(HES Installed)
GIW-13	04/18/17	11.3	59.4	0.0	29.3	77.7	-0.6	N/A	(HES Installed)
GIW-13	04/24/17	12.2	59.1	0.0	28.7	86.1	-0.4	N/A	(HES Installed)
GIW-13	05/02/17	11.3	60.0	0.0	28.7	71.6	-0.7	N/A	(HES Installed)
GIW-13	05/02/17	10.0	60.2	0.0	29.8	72.8	-0.7	N/A	(HES Installed)
GIW-13	05/11/17	10.2	62.6	0.0	27.2	71.4	-0.7	N/A	(HES Installed)
GIW-13	05/15/17	10.0	59.3	0.0	30.7	90.7	-0.5	N/A	(HES Installed)
GIW-13	05/23/17	9.6	62.2	0.0	28.2	74.3	-0.6	N/A	(HES Installed)
GIW-13	05/30/17	10.8	59.1	0.0	30.1	88.5	-0.8	N/A	(HES Installed)
GIW-13	06/05/17	9.8	61.0	0.0	29.2	100.1	-0.7	N/A	(HES Installed)
GIW-13	06/05/17	10.4	61.2	0.0	28.4	98.4	-0.7	N/A	(HES Installed)
GIW-13	06/12/17	9.5	62.6	0.0	27.9	99.1	-0.8	N/A	(HES Installed)

GIW-13 Wellhead Temperatures

